


# Guaranteeing Impactful Projects

REPORT OF CONSTITUENCY & EXECUTIVE PROJECTS TRACKING EXERCISE - PHASE V

SUPPORTED BY:

MacArthur Foundation

www.icpc.gov.ng

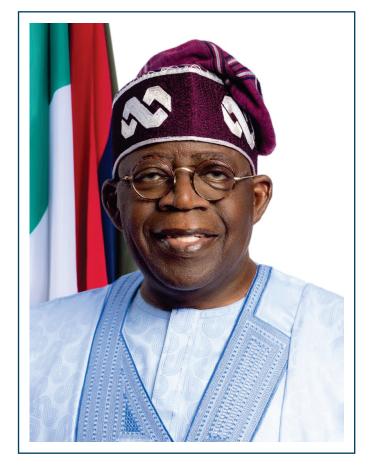

# HIS EXCELLENCY BOLA AHMED TINUBU GCFR

PRESIDENT, COMMANDER-IN-CHIEF OF THE ARMED FORCES FEDERAL REPUBLIC OF NIGERIA

#### Copyright © ICPC 2023

All rights reserved. No part of this publication may be reproduced or transmitted in any form or by any means, electronic or mechanical, including photocopying, recording or otherwise or stored in any retrieval system of any nature, without the written permission of the copyright holder.

#### NATIONAL LIBRARY OF NIGERIA CATALOGUING-IN-PUBLICATION DATA

Independent Corrupt Practices and Other Related Offences Commission (ICPC) Guaranteeing impactful projects: report of constituency executive projects tracking exercise phase v 1. Independent corrupt practices and other related offences commission, Tracking Budget – Reporting to 2. ICPC, Capital I. I Title II. Title ICPC HV6768.097 2023 353.669 ISBN: **978-978-782- 398-9** (pbk) AACR2

### Acknowledgment

The Constituency and Executive Projects Tracking Exercise is supported by MacArthur Foundation.



### Table of Content

| Table of Content                                | 03 |
|---|----|
| Tables, Figures and Boxes                       | 04 |
| Preface   | 05 |
| Introduction                                    | 06 |
| Tracking Strategy: Inputs, Outputs and Outcomes | 07 |
| Challenges                                      | 08 |
| Summary of Tracked Projects                     | 09 |
| Highlights of Findings                          | 17 |
| Enforcement Activities                          | 24 |
| New Strategies                                  | 25 |
| Recommendations                                 | 25 |
| Policy Advisory                                 | 25 |
| List of Contractors That Returned to Sites      | 27 |

### Tables, Figures and Boxes

### Tables

Table 1.1: Phase 5 Tracking Activities Table 1.2: Appropriations for Tracked Projects Table 1.3: Sectorial Distribution of Projects Tracked Table 2.1: Distribution of Projects Tracked by States Table 3.1: Distribution of Projects Tracked by Geo-Political Zones Table 4.1: Senatorial Districts with Highest Projects Allocations in the 2023 Budget Table 4.2: Senatorial Districts with Lowest Projects Allocations in the 2023 Budget Table 4.3: Federal Constituencies with Highest Projects Allocations in the 2023 Budget Table 4.4: Federal Constituencies with Lowest Projects Allocations in the 2023 Budget Table 4.5: List of Contractors Compelled to Return to Site Table 4.6: List of Cash Recoveries from Phase 5 Tracking Exercise

### Figures

- Figure 1.1: Status of Projects Tracked
- Figure 2.1: Distribution of Projects Tracked by States
- Figure 2.2: Distribution of Projects Tracked in Selected States
- Figure 3.1: Distribution of Projects Tracked by Geo-Political Zones
- Figure 3.2: Graphical Distribution of Projects Tracked by Geo-Political Zones
- Figure 3.3: Percentage of Projects Tracked by Geo-Political Zones
- Figure 4.1: Comparative Analysis of Projects Allocations in Selected Senatorial Districts
- Figure 4.2: Comparative Analysis of Projects Allocations in Selected Federal Constituencies
- Figure 4.3: Comparative Analysis of Projects Allocations in Selected Federal Constituencies

### Boxes

Box 1.1: Objectives of the Constituency and Executive Projects Tracking Initiative

- Box 1.2: Tracked Projects Budget and Recoveries
- Box 1.3: Sectors with Higher Number of Projects Tracked
- Box 2.1: States with Highest Number of Projects Tracked
- Box 3.1: Highlights of Policy Advisory

### Preface

In 2019, ICPC initiated the tracking of Zonal Intervention Projects (ZIPs) based upon the dissatisfaction of Nigerians with delivery of ZIPs in respect of which a minimum of N100 Billion had been budgeted annually since the year 2000. ZIPs were conceived as a way of bringing development to the grassroots, but over the years, the initiative has been mired in abuse, corruption, irregularities, poor or non-execution of projects. Tracking of ZIPs by the Constituency Projects Tracking Group was subsequently expanded to include tracking of executive projects because executive projects dominate the annual federal budget. Tracking exercises were conducted between 2019-2022 in Phases I-IV culminating in reports for each phase. The report in this publication is for Phase V which commenced on 7th November 2022 and covered projects executed under the 2019, 2020 and 2021 budget years which were not tracked in previous exercises due to capacity and other constraints.

As with previous phases, the Constituency and Executive Projects Tracking Group (comprising representatives of the Commission, Budget Office of the Federation, Bureau of Public Procurement, Office of the Auditor-General of the Federation. Nigerian Institute of Quantity Surveyors, CSOs, and the media) in accordance with agreed criteria, preselected 1,377 projects from the 2019, 2020 and 2021 ZIPs budgets and presented same to its Steering Committee for final selection, out of which 712 projects spread across 21 states in the six-geopolitical zone, including projects that citizens had complained of non-execution or poor execution, were selected for tracking.

This report documents the tracking exercise, highlights of findings, recommendations, and policy advisory. The tracking teams found that domiciliation of projects outside the core mandates of MDAs undermines project delivery and is prone to corruption. Other abuses are indiscriminate grant of approval for selective tendering, abuse of grant of certificate of no objection without proper evaluation of requests by MDAs, conflict of interests by project sponsors/facilitators and civil servants, corruption-prone empowerment projects, regulatory capture in agencies with captive funds such as TETFUND, UBEC, NHIS, NHF, NSITF, etc militate against the project delivery and value for money. The findings, recommendations and policy advisory are in furtherance of government's anti-corruption objectives. The initiative demonstrates the effectiveness of collaborative synergy between government agencies and partners in the fight against corruption. The report also corroborates findings in previous tracking exercises that shows that connivance between project sponsors/facilitators and civil servants undermines delivery of projects in critical areas like health, education, rural infrastructure.

While the Commission's intervention has led to the completion of projects and recovery of diverted funds, a wholistic reform of the process is advised at Executive and Legislative levels. Further delay will be economically catastrophic.

#### **Professor Bolaji Owasanoye, SAN, OFR** Chairman, ICPC September, 2023

### Introduction

This report represents the results/ outcome of the Phase 5 of the Commission's tracking initiative. Phase 5 tracking exercise which commenced on 7th November 2022 covered projects executed under the 2019, 2020 and 2021 only and was conducted across 20 states.

The project tracking which started in 2019 is an initiative of the current Chairman of the Commission. It aims to bring sanity, integrity and accountability into the execution of public funded projects. The initiative takes strength from the Commission's prevention and enforcement mandate as provided in S.6 of the Corrupt Practices and Other Related Offences Act, 2000. The Constituency and Executive Projects Tracking Group (CEPTG) is now a Division in the Operations Department.

The Commission brought together diverse stakeholders; state and nonstate actors alike to steer the initiative and created the Constituency and Executive Projects Tracking Group (CEPTG). In this regard, the Commission has been working with the Budget Office of the Federation (BOF), Bureau for Public Procurement (BPP), Office of the Auditor-General of the Federation (OAuGF), Office of the Accountant-General of the Federation (OAGF), Nigerian Institute of Quantity Surveyor (NIQS), CSOs and the media (local and national). The objectives of the initiative among others are to ensure diligent and satisfactory execution of public funded projects, ensure that the public gets value for every naira expended by the Treasury, curb abuses, strengthen project delivery processes, galvanize public awareness and participation in the project delivery chains as well as s a n c t i o n b o t h c r i m i n a l a n d administrative transgressions.

This is the fifth in the series of continuous tracking and investigations of public funded projects being conducted by the Commission following on the tracks of the successes achieved in the previous tracking exercises.

While Phase 4 tracking exercise focused on Executive Projects, Phase 5 focused on Zonal Intervention Projects (ZIP), popularly known as Constituency Projects. ZIP started in the year 2000 resulting from complaints from federal legislators to the then president, Olusegun Obasanjo regarding absence of infrastructural developments in their constituencies basing their argument on the distance between the Federal Government and local communities.

They submitted that being closer to the grassroot, they were better placed to know and assess the infrastructural needs of their constituencies.

Consequently, arrangement was made that N100 Billion would be provided in every budget year for projects to be nominated by legislators for execution in their respective constituencies. This is outside the main capital budget of the Federal Government.

Sadly, as against the original noble intent, and due to absence of check mechanisms, project facilitators and civil servants turned the initiative into a cash cow, as almost every stage of the implementation is mired in corruption and abuse, such that most projects were shoddily executed or not executed at all. In many cases, projects were executed by companies belonging to civil servants or project facilitators or companies in which they had substantial interests.

Despite the challenges, the initiative has gained the confidence of some sponsors who report anomalies to the Commission for investigation.

### Tracking Strategy: Inputs, Outputs and Outcomes

The Commission obtains the federal budgets for the years in focus, analyse the budgets, and in conjunction with the CEPTI Steering Committee, selects projects to be tracked and investigated based on already established parameters. The Commission's officers in teams with assigned Quantity Surveyors (QS) nominated by the NIQS, CSOs and the media are deployed to the location of each of the selected projects for tracking.

For clarity, the established parameters are national spread, monetary value of the project, intended and potential benefits of the project to the local communities. In addition, priority is also given to those sectors that have the most beneficial impact on the most vulnerable members of our societies such as education, agriculture, potable water, healthcare, power, rural infrastructures and now "empowerment".



For Phase 5, a total of 1,377 projects were preselected from the 2019, 2020 and 2021 Zonal Intervention Projects (ZIP) budgets and presented to the Steering Committee for final selection, out of which 712 including projects petitioned against were finally selected by the Steering Committee for tracking.

The Commission handles the investigations, the QS handles the professional valuation of the projects in terms of quality and quantities and gives opinion and advice as appropriate. The CSOs monitor the transparency and credibility of our processes and give feedback on projects tracked while the media give the entire processes the needed publicity and visibility which help to galvanize and ensure public participation towards achieving the objectives of the initiative.

The outcome of the tracking exercise includes further investigations on issues discovered on sites, as well as recoveries and confiscations of cash and assets, compelling contractors back to sites to complete uncompleted projects or to remedy shoddily executed projects.

It also includes recovery of hoarded or diverted assets for distribution to the intended beneficiaries, provision of policy advisories, guidance to Ministries, Departments and Agencies (MDAs) on project implementation, policy directives to agencies, administrative sanctions and or prosecutions as the case maybe.

### Challenges

**Funding:** The Commission can only track selected projects within the limit of its annual budget and with development assistance where available.

**Insecurity:** Certain areas of the country were inaccessible as a result of multidimensional security challenges. In those areas, the safety and security of our operatives and partners dictated that tracking projects in those areas should be stood down. Though at much reduced intensity, Boko Haram is still active in some parts of Borno. Some parts of Katsina are still bandits infested. Likewise in almost all the states in the South-East where IPOB is active.

### Summary of Tracked Projects

#### Table 1.1: Phase 5 Tracking Activities

| Detail   | Value               |
|--|---------------------|
| Projects Selected for Tracking                           | 712                 |
| Contractors/companies involved                           | 417                 |
| Focal Sectors of Tracked Projects                        | 12                  |
| Project Tracked (so far)                                 | 703                 |
| Projects Yet To Be Tracked (owing to insecurity)         | 16                  |
| Projects Executed to Completion                          | 654                 |
| Projects Ongoing   | 19                  |
| Projects Abandoned                                       | 04                  |
| Projects Not Executed                                    | 19                  |
| Projects Sites Not Found                                 | 07                  |
| Projects in which Contractors Returned to Site           | 88*                 |
| Appropriations for all Tracked Projects                  | N30,983,067,490.56  |
| Contract Value of all Projects Tracked                   | N29,944,214,730.40  |
| Funds Released to MDAs for the Projects Tracked          | N29,330,961,477.23  |
| Amount Paid to Contractors (so far)                      | N25,174,288,811.86  |
| Value of Projects on which Contractors Returned to Sites | N3,540,829,993.00   |
| Cash Recoveries Made (so far)                            | N529,699,351.60     |
| Recoveries Made in Assets (so far)                       | N1,551,937,543.41   |
| Recoveries Made (so far) - Cash and Assets               | N2,081,636,895.01   |
| Cumulative Savings to Government                         | N5,622,466,888.01** |

#### Notes

\* This reflects figures drawn from projects selected for tracking only. From intelligence received, many more contractors have gone back to sites on projects not listed for tracking in this phase and those figures are not computed here. \*\* Cumulative savings for Government is the sum total of our recoveries and the estimated value of those projects on which contractors were compelled back to sites as a result of the Commission's tracking activities. These amounts were computed as savings for Government as these are monies that would have been lost/misappropriated save for the Commission's intervention. The valuation Reports being awaited from the assigned QS will provide a definite value when received.

#### Box 1.2: Tracked Projects Budget and Recoveries

#### **BUDGET HIGHLIGHTS OF TRACKED PROJECTS**



**₩30.98bn** Appropriation for all the tracked projects in Phase 5.



#### **₩29.33bn** Funds Released to MDAs for the Tracked Projects







## ₦25.17bn

Amount Paid to Contractors (so far)

#### PHASE 5 RECOVERIES

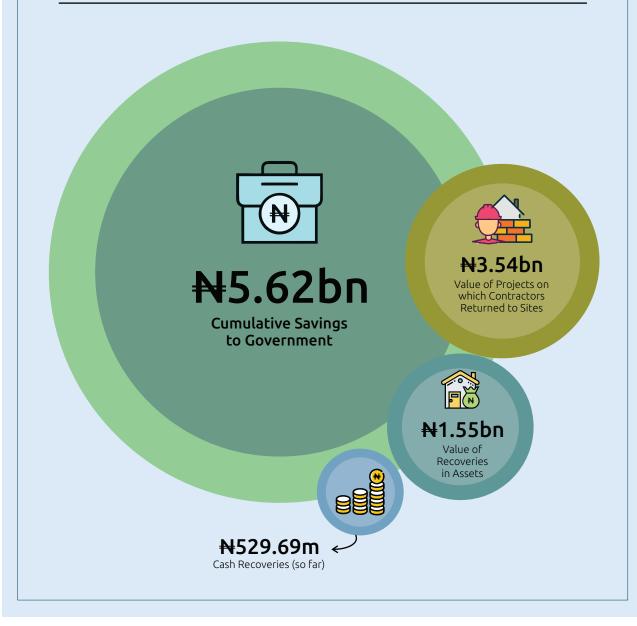

#### Figure 1.1: Status of Projects Tracked

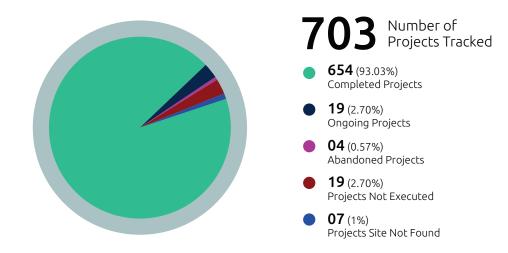

#### Table 1.2: Appropriations for Tracked Projects

| Year                  | Amount             | Percentage |        |
|-----------------------|--------------------|------------|--------|
| 2021                  | N13,758,091,849.56 |            | 44.41% |
| 2020                  | N16,473,975,641.00 |            | 53.17% |
| Petition (2014-2019)* | N751,000,000.00    | 2.42%      |        |
| Total                 | N30,983,067,490.56 |            |        |

\* Projects reported via petitions by members of the public and tracked during Phase 5.

#### Table 1.3: Sectorial Distribution of Projects Tracked

| Sector                          | No. of Projects | Percentage |
|---------------------------------|-----------------|------------|
| Education                       | 123             | 17.50%     |
| Empowerment & Capacity Building | 331             | 47.08%     |
| Water Supply                    | 69              | 9.82%      |
| Agriculture                     | 51              | 7.25%      |
| Power                           | 51              | 7.25%      |
| Healthcare                      | 24              | 3.41%      |
| Road Infrastructures            | 25              | 3.56%      |
| ICT                             | 08              | 1.14%      |
| Environment & Natural Resource  | 04              | 0.57%      |
| Art & Culture                   | 07              | 1%         |
| Law Enforcement & Security      | 04              | 0.57%      |
| Trade & Investment              | 06              | 0.85%      |
| Total                           | 703             |            |




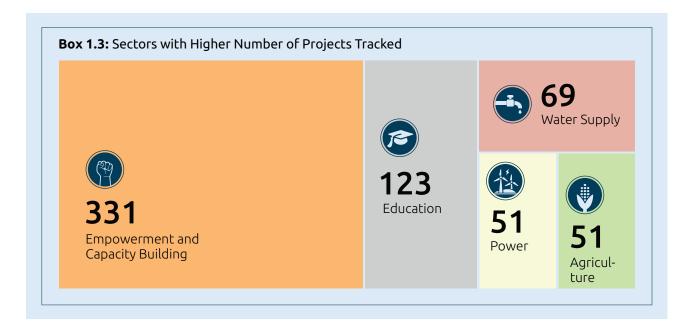


 Table 2.1: Distribution of Projects Tracked by States

| State       | No. of Projects | Percentage |
|-------------|-----------------|------------|
| Abia        | 99              | 14.08%     |
| Anambra     | 73              | 10.38%     |
| Enugu       | 33              | 4.69%      |
| Cross River | 44              | 6.26%      |
| Delta       | 53              | 7.54%      |
| Rivers      | 15              | 2.13%      |
| Оуо         | 32              | 4.55%      |
| Osun        | 28              | 3.98%      |
| Ondo        | 28              | 3.98%      |
| Ogun        | 27              | 3.84%      |
| Bauchi      | 32              | 4.55%      |
| Borno       | 30              | 4.27%      |
| Gombe       | 30              | 4.27%      |
| Katsina     | 32              | 4.55%      |
| Jigawa      | 24              | 3.41%      |
| Kaduna      | 22              | 3.13%      |
| Sokoto      | 11              | 1.56%      |
| Niger       | 21              | 2.99%      |
| Kwara       | 24              | 3.41%      |
| Коді        | 45              | 6.40%      |
| Total       | 703             |            |

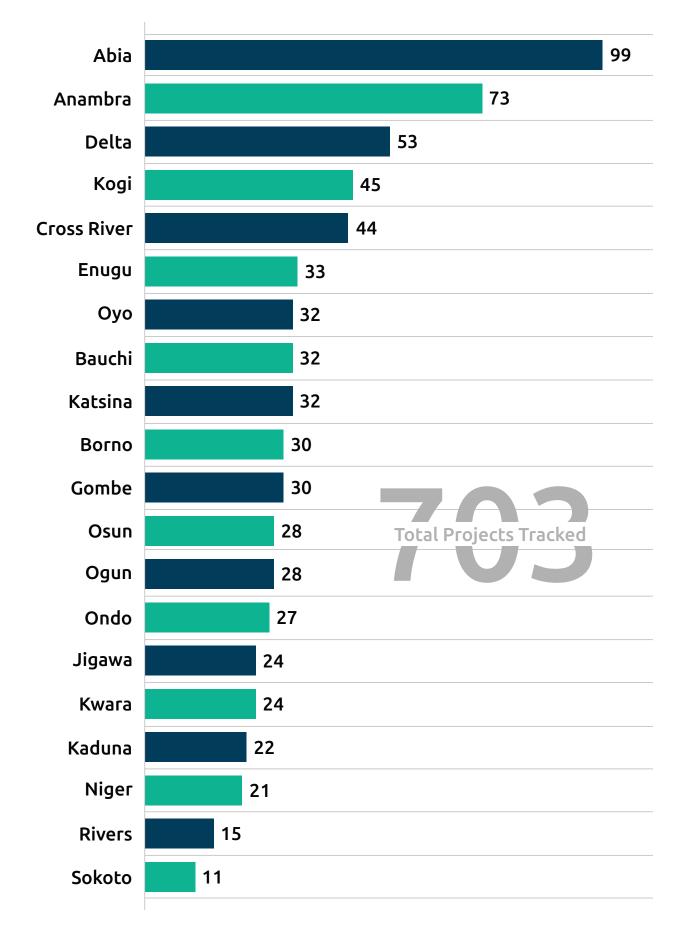




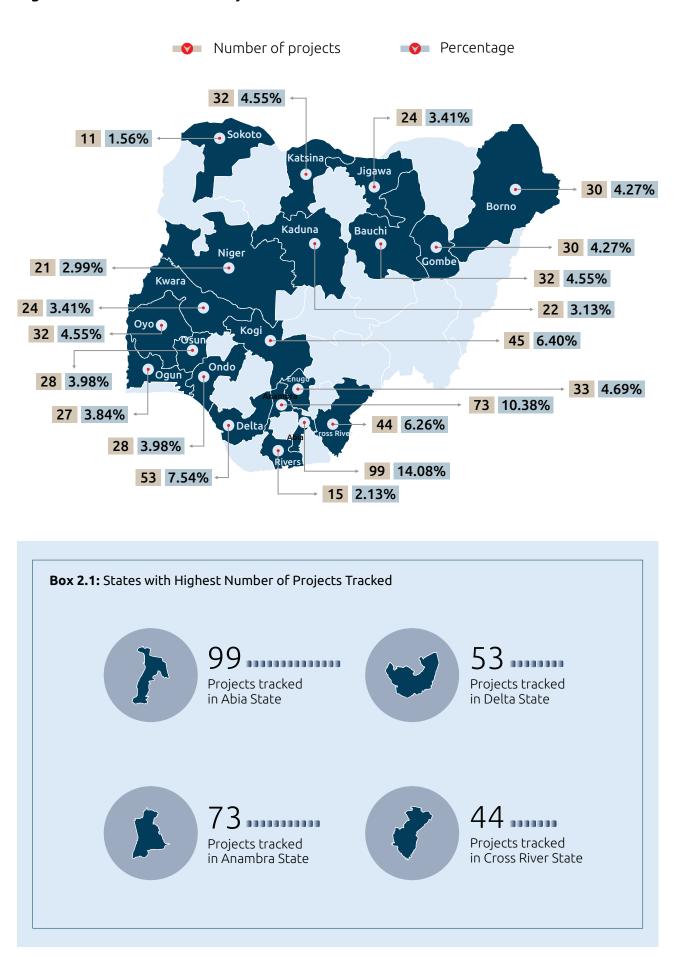


#### Figure 2.2: Distribution of Projects Tracked in Selected States

| Sector             | No. of Projects | Percentage |
|--------------------|-----------------|------------|
| South East (SE)    | 205             | 29.16%     |
| South South (SS)   | 112             | 15.93%     |
| South West SW)     | 115             | 16.36%     |
| North East (NE)    | 92              | 13.09%     |
| North West (NW)    | 89              | 12.66%     |
| North Central (NC) | 90              | 12.80%     |
| Total              | 703             |            |

#### Table 3.1: Distribution of Projects Tracked by Geo-Political Zones



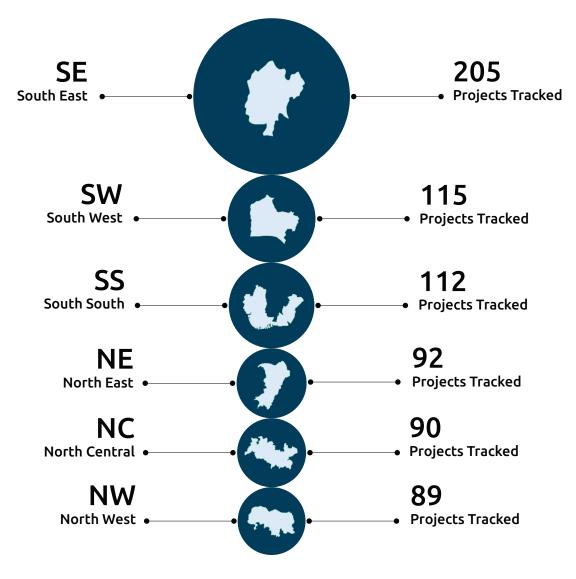


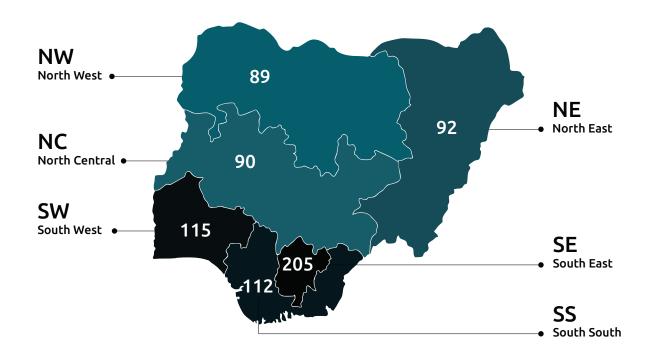


Figure 3.2: Graphical Distribution of Projects Tracked by Geo-Political Zones

Figure 3.3: Percentage of Projects Tracked by Geo-Political Zones

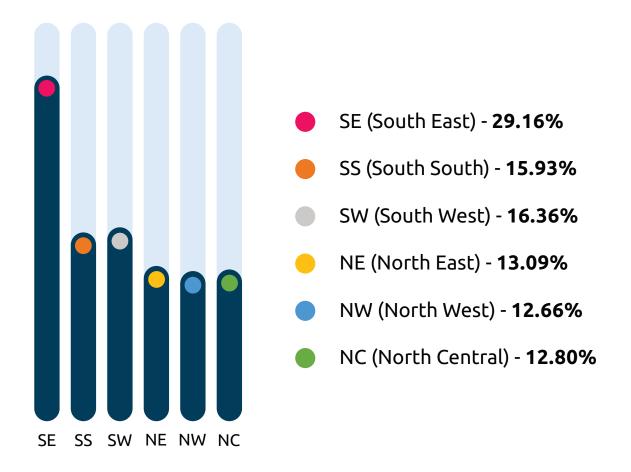

### **Highlight of Findings**

Phase 5 tracking exercise involved the selection of 712 projects scattered in 20 states cutting across the 6 geo-political zones within the established focal sectors. These include 81 petition-based projects. The states are Kaduna, Jigawa, Sokoto, Katsina, Kwara, Niger, Kogi, Cross River, Delta, Rivers, Ogun, Ondo, Osun, Oyo, Anambra, Enugu, Abia, Borno, Bauchi and Gombe States. For enhanced efficiency, trackers were taken through some online tailor-made capacity building trainings. BodyCams were deployed for use by the teams to enhance control and monitoring in addition to deployment of KoboToolBox application for data capturing and analysis.

The findings made so far are a lot similar to the findings highlighted in the previous published reports. However, it is crucial to mention here a few of the generic infractions discovered during this phase of the tracking exercise.

1. Soft Projects and Empowerment Projects as Major Conduit for Syphoning Public Resources and Money Laundering: Due to the increasing propensity of soft and intangible projects being abused and used as a vehicle for misappropriation of public funds, Phase 5 involved an increased interest in projects such as empowerment, trainings, grants etc. Because of their fluid nature and susceptibility to corruption, there has lately been an increasing number of soft projects being embedded in the budgets by project sponsors as they are more difficult to effectively track post execution. The Commission therefore increased its surveillance on such projects with an aggregate of 331 selected soft projects (47% of the all projects tracked), with contract value of N9,222,367,241.54. Consequently, there was hardly any of such projects tracked on which recoveries and or confiscation was not made as the projects were not executed in line with the Bills of Quantities.

Beneficiaries were heavily underserved whilst the funds are misappropriated. In Training Projects for instance, training exercises designed to be conducted over a period of one or two weeks were conducted in just a day and all funds assigned to all activities for the remaining 6 or 13 days as the case may be, were diverted.

In some cases, beneficiaries were recycled such that their names appeared on the lists of beneficiaries in two or more of such projects spanning different locations. Beneath the façade of contractors committing various infractions, the sponsors as well as the implementing agencies' officials were found to have committed the identified infractions or aided and abetted the commission of the infractions.

It was discovered in some cases, that the sponsors practically forced the contractors to transfer the execution of the projects to them, and the contract sum paid to the contractor transferred to the sponsors. The contractor is left with only a commission of between 5 to 10 percent. 2. Hoarding and Non-Distribution of Empowerment Items: As a campaign strategy, a larger percentage of empowerment items procured under the 2020 and 2021 Appropriations were found stashed away in warehouses or private properties of the projects sponsors. The apparent reason for this is to use the items for campaigns ahead of the 2023 elections. These were found in almost all the states visited; politicians using public funds as political capital for the 2023 elections.

In Anambra North Senatorial District, the Commission found some empowerment projects items worth about N1.1 billion procured since 2020 hidden and hoarded in the warehouse of the Senator representing the Senatorial District. So also in Cross River South Senatorial District, various undistributed items worth about a billion Naira were found. The Commission has since enforced the distributions of the items to beneficiaries within the affected Districts or Federal Constituencies.

3. Monetary Grants Projects; Vessels for Syphoning Public Funds: Grants as projects are ordinarily a means of financial empowerment where beneficiaries are given certain amount of money free as seed money for the establishment of, or improvement of existing businesses. It is designed to be a poverty fighting tool where vulnerable members of the society could access free financing for their businesses.

In tracking and investigating grant projects, Commission discovered that in

some cases, intended beneficiaries got paid far less than was provided in the BoQ. For instance, in a grant project where beneficiaries were supposed to receive N100,000 each, only N10,000-N20,000 would be given, whilst in other cases, the numbers of beneficiaries were cut down. Some beneficiaries were also recycled such that the same beneficiaries presented at various projects sites to collect the grants.

It would appear that these recycled beneficiaries were acting for the sponsors' aides or the sponsors and their aides were just populating the purported register with names of people that did not in reality benefit from the grants. In one case, a grant project of N150 million was distributed to only 10 people with each receiving between N10-15 million.

4. Project Abandonment/Refusal to Execute Contracts: Though not so rampant as discovered in previous tracking exercises, some contractors were still found to have collected funds for projects awarded to them but refused to execute and absconded with the money. Such contractors have been arrested, indicted and recommended for prosecution in addition to the recovery of the already paid sums. The projects supervisors from the executing agencies or the supervising consultant as the case may be are also cited for prosecution.

5. **Overpayment of Contract Sums:** We found in some cases particularly projects executed in Ondo North Senatorial District, the Chief Executive Officer (CEO) of Centre for Atmospheric Research, Anyingba, a subsidiary of National Space Research and Development Agency was in the habit of arbitrarily and unlawfully overpaying contractors much more than the contract sums without any approved variation. All the overpaid companies were connected in some ways to the sponsor of the projects as one of the companies belonged to the senator's biological son. The overpaid sums have been recovered and the perpetrators cited for sanctions.

6. Disparity in Project Distribution:


Studies and analysis of national budgets have exposed a glaring lop-sidedness in projects distribution across states. Senatorial Districts and Federal Constituencies represented by principal officers have far more projects than their counterparts both in terms of numbers and value irrespective of populations and needs of the constituencies. Principal Officers use their positions to appropriate resources to their constituencies at the expense of others. In spite of that, the appropriated funds are hardly properly applied for the benefit of their constituents. For instance, Anambra North Senatorial District alone was found to have over 50 projects with a cumulative value of over 9 Billion Naira in the 2022 budget alone.

| Senatorial District | No. of Projects | Value ( <del>N</del> ) | Population |
|---------------------|-----------------|------------------------|------------|
| Delta Central       | 25              | 10,924,341,066.00      | 1,957,600  |
| Gombe Central       | 13              | 4,725,000,000.00       | 993,200    |
| Niger East          | 31              | 4,650,000,000.00       | 2,264,200  |
| FCT                 | 17              | 4,500,000,000.00       | 3,067,500  |
| Katsina North       | 10              | 3,185,187,394.00       | 3,504,400  |
| Yobe East           | 15              | 2,930,000,000.00       | 1,104,300  |
| Kebbi North         | 32              | 2,849,737,873.00       | 2,113,200  |
| Osun East           | 16              | 2,815,000,000.00       | 1,407,300  |
| Kwara Central       | 2               | 2,797,854,574.00       | 1,361,100  |
| Kano North          | 17              | 2,553,704,694.00       | 3,942,300  |
| Abia North          | 18              | 2,550,000,000.00       | 1,053,900  |
| Yobe North          | 32              | 2,476,777,198.00       | 1,258,100  |
| Anambra North       | 18              | 1,457,055,400.00       | 1,388,000  |
| Kano South          | 4               | 1,450,253,101.00       | 5,004,300  |
| Edo Central         | 9               | 1,385,343,101.00       | 873,900    |
| Ogun East           | 10              | 1,250,865,515.00       | 2,126,600  |
| Cross River South   | 14              | 1,235,000,000.00       | 1,436,900  |
| Edo North           | 6               | 1,200,253,101.00       | 797,200    |
| Nasarawa South      | 3               | 1,165,000,000.00       | 1,254,800  |
| Borno Central       | 3               | 1,130,000,000.00       | 2,201,300  |

| Senatorial District | No. of Projects | Value ( <del>N</del> ) | Population   |
|---------------------|-----------------|------------------------|--------------|
| Sokoto East         | 1               | 50,000.00              | 2,558,200    |
| Benue North West    | 1               | 20,000,000.00          | 2,210,600    |
| Niger North         | 1               | 25,000,000.00          | 2,120,800    |
| Ogun West           | 1               | 32,000,000.00          | 1,892,600    |
| Plateau South       | 2               | 45,000,000.00          | 1,333,100    |
| Edo South           | 2               | 55,000,000.00          | 2,490,900    |
| Oyo South           | 3               | 55,000,000.00          | 2,526,800    |
| Osun West           | 2               | 70,000,000.00          | 1,433,400    |
| Bauchi Central      | 2               | 92,000,000.00          | 2,573,200    |
| Jigawa North West   | 1               | 100,000,000.00         | 2,838,800    |
| Anambra Central     | 4               | 110,000,000.00         | 2,093,100    |
| Jigawa South West   | 2               | 120,000,000.00         | 2,518,400    |
| Adamawa South       | 2               | 130,000,000.00         | 1,927,000    |
| Plateau North       | 3               | 130,000,000.00         | 1,968,900    |
| lmo East            | 3               | 148,000,000.00         | 1,815,900    |
| Cross River Central | 2               | 150,000,000.00         | 1,436,900    |
| Rivers South East   | 3               | 150,000,000.00         | 1,917,600    |
| Cross River North   | 2               | 165,000,000.00         | 1,413,100    |
| Imo North           | 5               | 170,000,000.00         | 1,108,400.00 |
| Borno North         | 1               | 200,000,000.00         | 2,597,100.00 |

Table 4.2: Senatorial Districts with Lowest Projects Allocations in the 2023 Budget

#### Figure 4.1: Comparative Analysis of Projects Allocations in Selected Senatorial Districts

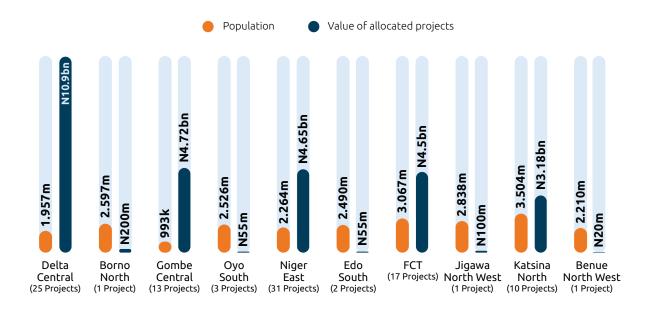

| Senatorial District           | No. of Project | s Value ( <del>N</del> ) | Population |
|-------------------------------|----------------|--------------------------|------------|
| Surulere                      | 19             | 7,433,644,286.00         | 744,400    |
| Ankpa/Omala/Olamaboro         | 7              | 3,354,684,086.00         | 717,900    |
| Owan East/Owan West           | 5              | 3,107,416,500.00         | 374,800    |
| Ikorodu                       | 6              | 2,984,203,000.00         | 781,500    |
| Damataru/Tarmuwa/Gujba/Gulani | 3              | 2,929,916,500.00         | 626,800    |
| lfe                           | 9              | 208,000,000.00           | 217,100    |
| Lere                          | 6              | 2,215,000,000.00         | 501,900    |
| Ado/Ogbadigbo/Okpokwu         | 11             | 1,652,228,441.00         | 708,800    |
| Birniwa/Guri/Kiri Kasama      | 8              | 1,560,121,857.00         | 770,300    |
| Ezza South/Ikwo               | 9              | 1,257,500,000.00         | 519,200    |
| Lokoja/Kogi                   | 4              | 1,150,000,000.00         | 420,100    |
| Wudil/Garko                   | 3              | 1,130,119,857.00         | 576,700    |
| Sabon Gari/Kaduna South       | 3              | 1,100,000,000.00         | 1,025,500  |
| Atisbo/Saki-East/Saki-West    | 3              | 1,100,000,000.00         | 703,400    |
| Nkanu East/Nkanu West         | 7              | 1,036,816,000.00         | 431,900    |
| Tsanyawa/Kunchi               | 3              | 995,000,000.00           | 440,600    |
| Ajaokuta                      | 3              | 983,000,000.00           | 165,000    |
| Ilorin East/Ilorin South      | 7              | 983,000,000.00           | 625,600    |
| Jama'are/Itas-Gadau           | 2              | 975,000,000.00           | 617,900    |
| Lavun/Mokwa/Edati             | 2              | 958,000,000.00           | 1,050,500  |

#### Table 4.3: Federal Constituencies with Highest Projects Allocations in the 2023 Budget

#### Figure 4.2: Comparative Analysis of Projects Allocations in Selected Federal Constituencies


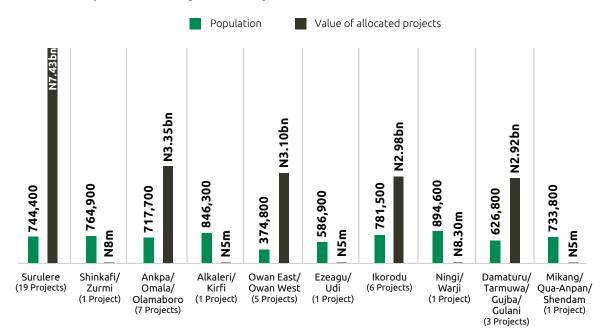


Table 4.4: Federal Constituencies with Lowest Projects Allocations in the 2023 Budget

| Senatorial District                | No. of Project | s Value ( <del>N</del> ) | Population |
|------------------------------------|----------------|--------------------------|------------|
| Awka North/Awka South              | 1              | 5,000,000.00             | 430,200    |
| Alkaleri/Kirfi                     | 1              | 5,000,000.00             | 846,300    |
| Ezeagu/Udi                         | 1              | 5,000,000.00             | 586,900    |
| Aiyedire                           | 1              | 5,000,000.00             | 99,100     |
| Boluwaduro/Ifedayo                 | 1              | 5,000,000.00             | 140,800    |
| Mikang/Qua-Anpan/Shendam           | 1              | 5,000,000.00             | 733,800    |
| Askira - Uba/Hawul                 | 1              | 7,500,000.00             | 386,900    |
| Oredo                              | 1              | 7,500,000.00             | 553,300    |
| Egbado North/Imeko- Afon           | 1              | 7,500,000.00             | 453,800    |
| Irepo/Orelope/Olorunsogo           | 1              | 7,500,000.00             | 438,100    |
| lkot Ekpene/Essien Udim/Obot Akara | 1              | 8,000,000.00             | 615,100    |
| Ogoja/Yala                         | 1              | 8,000,000.00             | 583,500    |
| Abakaliki/Izzi                     | 1              | 8,000,000.00             | 575,500    |
| Ikole/Oye                          | 1              | 8,000,000.00             | 461,500    |
| Kachia/Kagarko                     | 1              | 8,000,000.00             | 726,300    |
| Matazu/Musawa                      | 1              | 8,000,000.00             | 507,200    |
| Dunga/Takun/Ussa                   | 1              | 8,000,000.00             | 564,100    |
| Shinkafi/Zurmi                     | 1              | 8,000,000.00             | 764,900    |
| Ningi/Warji                        | 1              | 8,308,423.00             | 894,600    |
| Irepodun/Orolu/Olorunda/Osogbo     | 2              | 8,865,515.00             | 703,000    |

#### Figure 4.3: Comparative Analysis of Projects Allocations in Selected Federal Constituencies

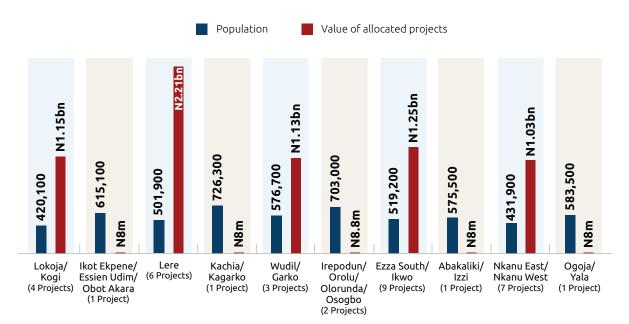

7. Underperformance in the Execution of Projects: Resulting from the effective monitoring and tracking exercise by the Commission, there has been a remarkable decrease in the volume of the infractions identified in the previous tracking phases. However, underperformance in the execution of public funded projects remains one of the biggest challenges bedevilling projects implementations in Nigeria. This generally translates to poor and substandard execution of projects, undersupplies of items specified under the projects, shortcutting the sizes, quantum and volumes of the projects etc. Underperformance of projects is usually enabled by the projects supervisors or consultants assigned by the implementing MDAs to supervise the projects. About 80% of cash recoveries (N418 million) made during this phase were as a result of projects underperformance.

Supervisors assigned to supervise empowerment projects undertake the supervision as mere spectators without checking and ensuring compliance with every line item on the BoQ. This they do negligently and sometimes deliberately because of the unprofessional and sometime intrinsic belief that it is for the sponsors of such projects to do as they deem fit without regards or recourse to the BoQ. This has in many cases enabled underperformance of projects or outright theft and misappropriation of projects items.

8. Some Sponsors Alleged to Collect Money Upfront from Would-be Contractors: Intelligence at the disposal of the Commission has established that some projects sponsors are in the habit of negotiating and receiving bribes from would-be contractors promising to tweak the system to ensure the award of the contracts to the latter on projects sponsored by the former. In such cases, competence and adherence to procurement laws and rules are compromised leading to poor execution and loss of resources.

On the other hand, and where the implementing agency refuses to bow to pressures from such compromised sponsors to award the contracts to their chosen contractors, the sponsors demand and receive such kick-backs from whichever contractor that is awarded the contract, otherwise they frustrate in many ways the implementation of the projects. The kick-backs are usually given in cash and in most cases in Dollars. In some cases, the sponsors force the contractors to transfer and submit the contracts to the sponsors for execution (which some still either fail to execute or underperform). Sponsors in this category have been cited for prosecution.

9. **Cost Padding:** Cost of goods and services for most empowerment projects appeared pegged without regards to prevailing market realities and no recourse to BPP Price Template. Rates appear arbitrarily fixed with the ultimate objective of making more money available for kickbacks. This is evident in the cost differentials across agencies for same goods and services being provided in the same location and in some cases even within the same agency thereby provoking questions on the basis for such costing. Our findings have established that most of these projects are inserted/padded projects and agencies rely on the promoters to provide insight on the concept and modalities for execution. In some cases, the production of the Bills of quantities is left entirely in the hands of the contractors, who in connivance with the projects sponsor arbitrarily allocate cost to items as they deem fit, hence the cost padding and differentials as the rates vary from one contractor to another.

10. **Projects supervisors of empowerment**: projects undertake the supervision as mere spectators without checking and ensuring compliance with every line item on the BoQ. Henceforth, supervisor must, and shall be held accountable for full and practical compliance with every item on the Bill.

The generic infractions listed above are being perpetrated by civil servants in the implementing agencies, facilitators of the projects (legislators) and contractors either as individuals or in conspiracy with one another.

### Enforcement

1. **Detentions:** No fewer than 50 people were detained during the investigations part of the exercise. This number includes legislators, staff of executing agencies, contractors and consultants. 2. **Freezing of Accounts:** In conducting the Phase 5 tracking exercise, no fewer than 200 bank accounts were frozen for one reason or the other.

3. **Return to sites:** Commission has compelled over 88 contractors to return to projects sites to complete uncompleted projects or carry out some remediation works on shoddily executed projects.

4. **Recoveries:** Recoveries and confiscations in both cash and stolen assets were made as can be seen in the Table 1.1

5. Distribution of hoarded/stolen assets: The Commission has in appropriate cases forced projects sponsors to distribute empowerment items found hoarded or misappropriated in their custody.

6. Administrative Sanctions: In appropriate cases where the indictment is not egregious, indicted staff of executing agencies were referred and cited for administrative disciplinary processes like suspension, de-ranking, dismissaletc.

7. **Prosecution:** The Commission has filed charges in court against some people that were indicted by investigations while others have been cited for prosecution. These include legislators, contractors, consultants and staff of the executing agencies.

### New Strategies

1. Disbursement of money in cash grants projects should not be handled by Disbursement Managers outside of their licensed jurisdiction and the disbursement must be done directly to all the beneficiaries and not through a third party.

2. More vigorous enforcement activities including but not limited to prosecution for infractions, recoveries, assets confiscations and forfeiture.

3. More robust engagement with the leaders and members of the National Assembly Appropriations Committees and their staff, including staff of Budget Office of the Federation.

4. Sensitize newly elected legislators on CEPTG findings.

5. Commission to focus more attention on the identified suspicious provisions in the 2023 budget, the sponsors as well as on the CEOs of the implementing agencies.

### Recommendations

1. Reform of Bureau for Public Procurement (BPP). This is because of the indiscriminate grant of approval for selective tendering, unnecessary grant of certificate of no objection without properly scrutinising the processes. Between 60% to 70% of capital procurement on tracked projects are done through selective tendering and this has enabled most of the procurement fraud being perpetrated by either the MDAs or the project sponsors. It makes it easier for MDAs to award contracts to companies nominated and presented by projects sponsors or high level officers of the procuring entity against due process and competitiveness as envisaged by the Procurement Act.

2. Commission to build a broad-based coalition against Budget Padding and Regulatory Capture.

3. Henceforth, supervisors must ensure, and shall be held accountable for full and practical compliance with every item on the Bills of Quantities/Bills of Engineering Measurement and Evaluation.

### Policy Advisory

1. Government should seek for judicial interpretation on the exact roles of the legislators in budget making particularly whether lawmakers can on their own initiate/insert projects not submitted by the Executive without recourse to the Executive Arm of Government whose responsibility it is to execute.

2. Government should institute Integrity Compliance System and measures in Procurement Evaluation and Administration.

3. Bureau for Public Procurement (BPP) should henceforth be discouraged from issuing Certificates of No Objection for Selective Tendering for constituency or padded projects except in critical or emergency situations as such issuance has been subjected to serious abuses by MDAs. There should be a well-defined, and clearly prescribed conditions/guidelines subject to third party evaluation before approval is given for selective tendering.

4. BPP should be made to review its debarment policy, rules and procedures to make it easier to blacklist egregious and recalcitrant erring contractors.

5. BPP should institute Integrity Compliance Management measures, benchmarks and platforms that contractors must measure up to, to be eligible for government contracts.


6. BPP and ICPC should collaborate with Development Partners like the World Bank, AfDB, UN, AU etc to automatically debar companies debarred by them from being eligible for government contracts for a determined period of time upon meeting prescribed conditions or in perpetuity. 7. Contractor companies should be encouraged to always undertake third party due diligence before subletting any part of the contract to a third party.

8. Government should institute incentives and reward system for contractors that expose illicit demands or transactions in contract evaluation and administration.

9. The Commission should create a whistleblower mechanism for contractors to report illicit demands or transactions.

10. Government must institute a system and mechanism that will ensure community involvement in Budget planning and administration to serve as checks on abuses and ensure the needs of benefiting communities are properly captured in the projects.

11. Projects sponsoring legislators must be made to make open disclosure of "no private interest" in all projects they are facilitating as a condition for such project being captured in the budget.

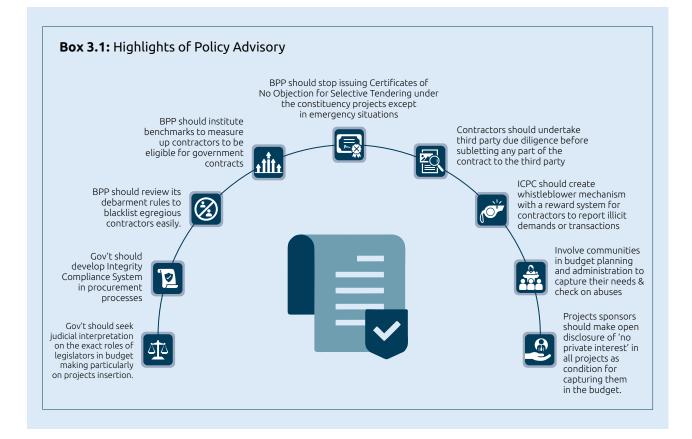

### **Contractors That Returned To Site**

#### Table 4.5: List of Contractors Compelled to Return to Site

| S/N | Project<br>Description   | Contract<br>Sum ( <del>N</del> ) | Name of<br>Contractor                     | Reason for Going<br>Back To Site  | Status/Remark  |
|-----|--|----------------------------------|---|---|--|
| 1   | RENOVATION OF THREE<br>CLASSROOM BLOCK AT OBOE HI<br>PRIMARY SCHOOL UMUNNACHI,<br>DUNUKOFIA LGA, ANAMBRA STATE   | 8,750,000                        | BRAMWELL<br>ELECTRICAL NIGERIA<br>LIMITED | POOR EXECUTION OF<br>WORKS  | THE CONTRACTOR HAS NOT<br>GONE BACK TO SITE BUT WE ARE<br>WORKING ON RECOVERING THE<br>BALANCE OF FUNDS ON WORK<br>NOT EXECUTED.   |
| 2   | NOTIFICATION OF AWARD OF<br>CONTRACT OF THE<br>CONSTRUCTION OF NEW SOLAR<br>POWERED BOREHOLES IN JIGAWA<br>NORTH WEST SENATORIAL<br>DISTRICT, JIGAWA STATE         | 163,967,013.08                   | S. TABAWA NIGERIA<br>LTD                  | NON-COMPLETION OF<br>WORKS ON SITE  | THE CONTRACTOR IS STILL ON<br>PROJECT SITE.  |
| 3   | NOTIFICATION OF AWARD FOR THE<br>CONTRACT OF THE<br>CONSTRUCTION OF MINI<br>COMPUTER VILLAGE AND GSM<br>SALE AND REPAIRS IN HADEJIA.                               | 58,862,396.43                    | STRUCTURAL<br>SKYLINE LTD                 | WORK EXECUTED NOT<br>ACCORDING TO<br>SPECIFICATION/POOR<br>EXECUTION.   | THE PROJECT HAS BEEN<br>COMPLETED AS SPECIFIED.  |
| 4   | AWARD OF CONTRACT FOR THE<br>CONSTRUCTION AND<br>INSTALLATION OF HANDPUMP<br>BOREHOLES AT VARIOUS<br>LOCATIONS IN<br>KANKIA/KUSADA/INGAWA FEDERAL<br>CONSTITUENCY. | N29,176,548.13                   | PEE CEE ESS<br>PROJECTS LTD               | 1. TO CORRECT THE<br>DEFECTS IN THE<br>BOREHOLE AT BARERUWA<br>DAJI.<br>2. TO INSPECT REMAINING<br>FIVE (5) BOREHOLES<br>WHEN THE SECURITY<br>SITUATION IMPROVES IN<br>THE AREAS.   | <ol> <li>THE DEFECTS IN THE<br/>BOREHOLE AT BARERUWA DAJI<br/>HAVE BEEN CORRECTED BY THE<br/>CONTRACTOR AS DIRECTED AND<br/>THE BOREHOLE IS NOW ON TRIAL<br/>USAGE. THE TEAM IS YET TO VISIT<br/>THE SITE FOR CONFIRMATION.</li> <li>THE TEAM IS YET TO VISIT THE<br/>SITES OF THE REMAINING FIVE (5)<br/>BOREHOLES AS THE SECURITY<br/>SITUATION HAS NOT IMPROVED.</li> </ol>   |
| 5   | AWARD OF CONTRACT FOR THE<br>CONSTRUCTION OF<br>ENTREPRENEURSHIP<br>DEVELOPMENT CENTRES IN<br>KATSINA SOUTH SENATORIAL<br>DISTRICT, KATSINA STATE                  | N168,846,700.06                  | MUNTASRAB<br>GLOBAL CONCEPT<br>LTD        | <ol> <li>THE CONTRACT SUM IS<br/>ABOVE THE<br/>APPROPRIATED AMOUNT,<br/>AND PAYMENT MADE WAS<br/>MORE THAN THE<br/>CONTRACT SUM.</li> <li>AS AT THE TIME OF THE<br/>TRACKING EXERCISE, THE<br/>CONTRACT EXECUTION<br/>WAS ONGOING.</li> </ol> | 1. THE DIRECTOR OF FINANCE     AND ACCOUNTS, AND DIRECTOR     OF PROCUREMENT OF NBRRI     WERE INVITED IN VIEW OF THE     RECOMMENDATION FROM     HEADQUARTERS BUT SENT THE     PROJECT OFFICER WHO COULD     NOT EXPLAIN THE GAPS     IDENTIFIED IN THE CONTRACT.     2. THE CONTRACTOR HAS     INFORMED THE TRACKING TEAM     THAT THE PROJECT HAS BEEN     COMPLETED. THE TEAM IS YET TO     VISIT THE SITE FOR     CONFIRMATION. |
| 6   | SUPPLY OF TVS MOTORCYCLES TO<br>JIBIA/KAITA FEDERAL<br>CONSTITUENCY, KATSINA STATE.  | N39,971,250.00                   | MASUKA<br>WORLDWIDE<br>SERVICES NIG LTD   | TO ENSURE DISTRIBUTION<br>OF THE MOTORCYCLES<br>AND OTHER ITEMS TO THE<br>INTENDED BENEFICIARIES.   | THE TVS MOTORCYCLES AND<br>OTHER ITEMS EARLIER SEALED IN<br>THE STORE HAVE BEEN<br>DISTRIBUTED TO BENEFICIARIES<br>UNDER THE SUPERVISION OF THE<br>TRACKING TEAM AS DIRECTED BY<br>THE HEADQUARTERS. THE TEAM<br>IS YET TO GET ALL THE LIST OF<br>THE BENEFICIARIES FROM THE<br>SPONSOR.   |
| 7   | AWARD OF CONTRACT FOR<br>STRATEGIC EMPOWERMENT<br>PROGRAMME IN KATSINA SOUTH<br>SENATORIAL DISTRICT, KATSINA<br>STATE (PURCHASE OF PICK-UP<br>TOYOTA HILUX)        | N28,499,999.02                   | DADAMAN GLOBAL<br>INVESTMENT LTD          | TO ENSURE HANDOVER<br>OF THE VEHICLES TO THE<br>BENEFICIARIES UNDER<br>THE SUPERVISION OF<br>ICPC.  | FURTHER INVESTIGATION<br>REVEALED THAT THE PROJECT<br>SPONSOR DOES NOT INTEND TO<br>RELEASE THE VEHICLE FOR<br>EMPOWERMENT PROGRAMME<br>AND THERE WAS NO BENEFICIARY<br>MEANT TO RECEIVE THE VEHICLE<br>AS AT THE TIME OF THE EXERCISE.<br>THEREFORE, THE TEAM<br>RECOMMENDED FOR FORFEITURE<br>OF THE VEHICLE TO THE FEDERAL<br>GOVERNMENT.   |

| S/N | Project<br>Description  | Contract<br>Sum ( <del>N</del> )   | Name of<br>Contractor             | Reason for Going<br>Back To Site  | Status/Remark   |
|-----|---|--|-----------------------------------|---|---|
| 8   | AWARD OF CONTRACT FOR THE<br>PROVISION OF STRATEGIC<br>EMPOWERMENT PROGRAMME<br>(VULCANIZING) FOR YOUTH AT<br>FUNTUA/DANDUME FEDERAL<br>CONSTITUENCY.                                   | N16,178,150.00<br>(FIRST AWARD);<br>N9,984,600.00<br>(SECOND<br>AWARD)     | MANAJEE ENERGY<br>LTD             | TO ENSURE DISTRIBUTION<br>OF THE VULCANIZING<br>MACHINES AND OTHER<br>ITEMS TO BENEFICIARIES.   | THE VULCANIZING MACHINES AND<br>OTHER ITEMS EARLIER SEALED<br>HAVE BEEN DISTRIBUTED TO<br>BENEFICIARIES UNDER THE<br>SUPERVISION OF THE TRACKING<br>TEAM AS DIRECTED BY THE<br>HEADQUARTERS. THE TEAM IS<br>YET TO GET THE FULL LIST OF THE<br>BENEFICIARIES FROM THE<br>SPONSOR. |
| 9   | AWARD OF CONTRACT FOR THE<br>PROVISION OF STRATEGIC<br>EMPOWERMENT PROGRAMME<br>(GRINDING MACHINES) FOR<br>WOMEN AT FUNTUA/DANDUME<br>FEDERAL CONSTITUENCY.                             | N13,128,437.50<br>(FIRST AWARD);<br>N8,081,866.12<br>(SECOND<br>AWARD)     | GUEDEST<br>INVESTMENT LTD         | TO ENSURE DISTRIBUTION<br>OF THE GRINDING<br>MACHINES AND OTHER<br>ITEMS TO BENEFICIARIES.  | THE GRINDING MACHINES AND<br>OTHER ITEMS EARLIER SEALED<br>HAVE BEEN DISTRIBUTED TO<br>BENEFICIARIES UNDER THE<br>SUPERVISION OF THE TEAM AS<br>DIRECTED BY THE<br>HEADQUARTERS. THE TEAM IS<br>YET TO GET THE FULL LIST OF THE<br>BENEFICIARIES FROM THE<br>SPONSOR.             |
| 10  | AWARD OF CONTRACT FOR THE<br>SUPPLY OF MOTORCYCLES IN<br>FUNTUA/DANDUME FEDERAL<br>CONSTITUENCY.  | N20, 125,209.38<br>(FIRST AWARD);<br>N12, 677,558. 31<br>(SECOND<br>AWARD) | ALFARU GLOBAL<br>SERVICES NIG LTD | TO ENSURE DISTRIBUTION<br>OF THE MOTORCYCLES<br>AND OTHER ITEMS TO<br>BENEFICIARIES.  | THE MOTORCYCLES AND OTHER<br>ITEMS EARLIER SEALED HAVE<br>BEEN DISTRIBUTED TO<br>BENEFICIARIES UNDER THE<br>SUPERVISION OF THE TEAM AS<br>DIRECTED BY THE<br>HEADQUARTERS. THE TEAM IS<br>YET TO GET THE FULL LIST OF THE<br>BENEFICIARIES FROM THE<br>SPONSOR.                   |
| 11  | AWARD OF CONTRACT FOR THE<br>SUPPLY OF MOTORCYCLES TO<br>MASHI/DUTSI FEDERAL<br>CONSTITUENCY, KATSINA STATE.<br>(LOT A 52)  | N24,187,500.00   | SIZE ONE CONCEPTS                 | TO RECOVER THE<br>MOTORCYCLES AND<br>MONITOR THEIR<br>DISTRIBUTION TO<br>BENEFICIARIES OR<br>ENFORCE TOTAL<br>RECOVERY OF THE<br>MONETARY VALUE FROM<br>THE SPONSOR.        | THE SPONSOR HAS OBTAINED A<br>COURT ORDER STOPPING THE<br>COMMISSION AND ITS<br>OPERATIVES FROM FURTHER<br>ACTION ON THE MATTER. THE<br>CASE IS ONGOING AT THE HIGH<br>COURT OF KATSINA STATE.  |
| 12  | SUPPLY OF TRICYCLES TO<br>MASHI/DUTSI FEDERAL<br>CONSTITUENCY, KATSINA STATE<br>NORTH WEST ZONE   | N24,800,250.00   | KARNATI LTD                       | TO RECOVER THE<br>TRICYCLES AND MONITOR<br>THEIR DISTRIBUTION TO<br>BENEFICIARIES OR<br>ENFORCE TOTAL<br>RECOVERY OF THE<br>MONETARY VALUE FROM<br>THE SPONSOR.             | THE SPONSOR HAS OBTAINED A<br>COURT ORDER STOPPING THE<br>COMMISSION AND ITS<br>OPERATIVES FROM FURTHER<br>ACTION ON THE MATTER. THE<br>CASE IS ONGOING AT THE HIGH<br>COURT OF KATSINA STATE.  |
| 13  | SUPPLY OF MOTORCYCLES AND<br>TRICYCLES IN<br>KANKIA/KUSADA/INGAWA FEDERAL<br>CONSTITUENCY, KATSINA STATE.   | N17,718,500.00<br>(FIRST AWARD);<br>N5,836,500.00<br>(SECOND<br>AWARD)     | CHANJI GLOBAL<br>RESOURCES LTD    | TO OBTAIN THE LIST OF<br>BENEFICIARIES OF 12<br>TRICYCLES OR RECOVER<br>THE MONETARY VALUE OF<br>THE TRICYCLES FROM THE<br>SPONSOR.   | THE EXECUTING AGENCY AND THE<br>SPONSOR HAVE BEEN<br>CONTACTED TO PROVIDE THE LIST<br>OF BENEFICIARIES AS DIRECTED.<br>HOWEVER, THE TEAM IS YET TO<br>OBTAIN THE LIST IN VIEW OF THE<br>THEN ONGOING ELECTIONEERING<br>CAMPAIGN.  |
| 14  | SUPPLY OF GRINDING MACHINES IN<br>KANKIA/KUSADA/INGAWA FEDRAL<br>CONSTITUENCY, KATSINA STATE.   | N10,692,000.00<br>(FIRST AWARD);<br>N3,682,800.00<br>(SECOND<br>AWARD)     | DE-GODF ALLIED LTD                | TO OBTAIN THE LIST OF<br>BENEFICIARIES OF 133<br>GRINDING MACHINES OR<br>RECOVER THE MONETARY<br>VALUE OF THE MACHINES<br>FROM THE SPONSOR.                                 | THE EXECUTING AGENCY AND THE<br>SPONSOR HAVE BEEN<br>CONTACTED TO PROVIDE THE LIST<br>AS DIRECTED. HOWEVER, THE<br>TEAM IS YET TO OBTAIN THE LIST<br>DUE TO THE ONGOING<br>ELECTIONEERING CAMPAIGNS.  |
| 15  | AWARD OF CONTRACT FOR THE<br>CONSTRUCTION OF A PRIMARY<br>HEALTH CARE CENTRE (LEVEL 3) AT<br>MASHI IN KATSINA NORTH<br>SENATORIAL DISTRICT OF KATSINA<br>STATE (LOT: NPHCDA/ 2020/1437) | N113,371,402.75  | HADMAN<br>RESOURCES               | TO COMPEL THE<br>CONTRACTOR TO SUPPLY<br>THE MISSING ITEMS ON<br>THE BILL OF QUANTITY<br>AND LIAISE WITH<br>RELEVANT AGENCIES SO<br>THAT THE FACILITY CAN BE<br>PUT TO USE. | THE TEAM HAS CONTACTED THE<br>CONTRACTOR AND THE<br>CONSULTANT TO SUPPLY THE<br>MISSING ITEMS. THE TEAM IS ALSO<br>TRYING TO REACH OUT TO THE<br>RELEVANT AUTHORITIES TO<br>ENSURE THAT THE FACILITY IS<br>IMMEDIATELY PUT TO USE.  |

| S/N | Project<br>Description  | Contract<br>Sum ( <del>N</del> ) | Name of<br>Contractor                        | Reason for Going<br>Back To Site   | Status/Remark   |
|-----|---|----------------------------------|--|--|---|
| 16  | RURAL ELECTRIFICATION IN PERO-<br>CHONGE, KALTUNGO/SHANGOM<br>FEDERAL CONSTITUENCY, GOMBE<br>STATE  | N29,579,000                      | PINNATECH<br>ENGINEERING<br>NIGERIA LIMITED  | THE QS VALUED THE<br>UNEXECUTED PART OF<br>THE CONTRACT AT<br>N14,723,937.83   | THE CONTRACTOR WAS SENT<br>BACK TO SITE TO COMPLETE THE<br>PROJECT. |
| 17  | AWARD OF CONTRACT FOR THE<br>CONSTRUCTION AND EQUIPPING<br>OF VOCATIONAL TRAINING CENTRE<br>AT DIRECT LABOUR AGENCY ROAD,<br>ASABA, DELTA STATE                                     | 89, 180, 185.00                  | GROVEDALES<br>LIMITED                        | WORK NOT DONE<br>ACCORDING TO<br>SPECIFICATION.  | AWAITING RESPONSE OF THE<br>SUPERVISING AGENCY .                    |
| 18  | AWARD OF CONTRACT FOR THE<br>CONSTRUCTION AND EQUIPPING<br>OF VOCATIONAL TRAINING CENTRE<br>AT ANWA EXPRESS ROAD, ASABA,<br>DELTA STATE   | 183, 372, 750.00                 | REALAND<br>STANDARD<br>INVESTMENT<br>LIMITED | WORK NOT DONE<br>ACCORDING TO<br>SPECIFICATION.  | AWAITING RESPONSE OF THE<br>SUPERVISING AGENCY .                    |
| 19  | AWARD OF CONTRACT FOR THE<br>CONSTRUCTION OF 10 TOWN HALL<br>BUILDING PROJECTS IN VARIOUS<br>LOCATIONS IN ANIOCHA OSHIMILI<br>DELTA STATE (LOT W071)                                | 350, 000, 000.00                 | KENVIC MOORE BIZ<br>VENTURE LIMITED          | MINOR DEFECTS<br>IDENTIFIED.   | AWAITING RESPONSE OF THE<br>SUPERVISING AGENCY                      |
| 20  | NOTIFICATION OF AWARD OF<br>CONTRACT FOR THE<br>CONSTRUCTION OF 3 TOWN HALL<br>BUILDING PROJECTS IN VARIOUS<br>LOCTIONS IN ANIOCHA OSHIMILI<br>FEDERAL CONSTITUENCY, DELTA<br>STATE | 100, 000, 000.00                 | MULARABS<br>INVESTMENT<br>LIMITED            | WORK DONE WAS NOT IN<br>TANDEM WITH THE<br>SPECIFICATION.<br>DEFECTS WERE FOUND IN<br>THE ROOFING.   | AWAITING RESPONSE OF THE<br>SUPERVISING AGENCY.                     |
| 21  | AWARD OF CONTRACT FOR W14B:<br>CONSTRUCTION AND EQUIPPING<br>OF A CIVIC CENTRE AT IBUSA<br>ANIOCHA/OSHIMILI FEDERAL<br>CONSTITUENCY, DELTA STATE                                    | 87, 180, 714.06                  | HEATLAND<br>ASSOCIATES LIMITED               | WORK DONE WAS NOT UP<br>TO SPECIFICATION.<br>WATER WAS FOUND TO<br>HAVE OOZED OUT FROM<br>THE FLOOR.   | AWAITING RESPONSE OF THE<br>SUPERVISING AGENCY.                     |
| 22  | AWARD OF CONTRACT FOR W14C:<br>CONSTRUCTION AND EQUIPPING<br>OF A CIVIC CENTRE AT OGWASHI<br>UKU, ANIOCHA/OSHIMILI FEDERAL<br>CONSTTITUENCY, DELTA STATE                            | 87, 219, 781.26                  | STONEEDGE<br>PREMIUM SERVICES<br>LIMITED     | WORK DONE WAS NOT AS<br>SPECIFIED.<br>THE CONTRACTOR TO<br>BACKFILL THE SEPTIC<br>TANK AND MEND THE<br>ROOF.   | AWAITING RESPONSE OF THE<br>SUPERVISING AGENCY.                     |
| 23  | AWARD OF CONTRACT FOR W14D:<br>CONSTRUCTION AND EQUIPPING<br>OF A CIVIC CENTRE AT UBULU-UKU<br>ANIOCHA/OSHIMILI FEDERAL<br>CONSTITUENCY, DELTA STATE                                | 87, 250, 320.04                  | MUSTY ONE<br>INNOVATION<br>LIMITED           | WORK DONE WAS NOT UP<br>TO THE SPECIFICATION.<br>THE CONTRACTOR MUST<br>FIX CRACKED WALLS AND<br>BACKFILL SEPTIC TANK.   | AWAITING RESPONSE OF THE<br>SUPERVISING AGENCY.                     |
| 24  | AWARD OF CONTRACT FOR W14A:<br>CONSTRUCTION AND EQUIPPING<br>OF A CIVIC CENTRE AT OBOMKPA<br>ANIOCHA/OSHIMILI FEDERAL<br>CONSTITUENCY, DELTA STATE                                  | 87, 284, 431.31                  | CWM CONTRACTING<br>LTD                       | WORK DONE WAS NOT TO<br>SPECIFICATION.<br>DEFECTS WERE FOUND IN<br>THE ROOFING.  | AWAITING RESPONSE OF THE<br>SUPERVISING AGENCY.                     |
| 25  | AWARD OF CONTRACT FOR THE<br>RENOVATION OF ST. PAULS<br>ANGLICAN PRIMARY SCHOOL,<br>ARAROMI IDO LGA, OYO SOUTH<br>SENATORIAL DISTRICT, OYO STATE                                    | 11,875,000.00                    | FON APPLE<br>INTEGRATED<br>SERVICES LTD      | THE TRACKING TEAM<br>INITIALLY CONCLUDED<br>THAT NO RENOVATION<br>WAS DONE IN THE SITE<br>VISITED. BUT WHEN THE<br>CONTRACTOR WAS<br>INVITED, WE GOT TO<br>KNOW THAT THERE WERE<br>TWO SCHOOLS WITH<br>SAME NAME WITHIN THAT<br>LOCAL GOVERNMENT. SO,<br>WE REVISITED THE<br>PROJECT TO ASCERTAIN<br>THAT THE PROJECT WAS<br>DONE AND COMPLETED. | THE RENOVATION WAS<br>COMPLETELY DONE.                              |

| S/N | Project<br>Description   | Contract<br>Sum ( <del>N</del> ) | Name of<br>Contractor                    | Reason for Going<br>Back To Site  | Status/Remark   |
|-----|--|----------------------------------|--|---|---|
| 26  | PROCUREMENT AND INSTALLATION<br>OF 500KVA TRANSFORMER, SOLAR<br>STREET LIGHTS IN OYO SOUTH<br>SENATORIAL DISTRICT, OYO STATE                     | 49,982,179.20                    | MESSRS PRIMEVIEW<br>CO.NIG. LTD          | THE S00KVA<br>TRANSFORMER IN<br>QUESTION WAS SUPPLIED<br>BUT NOT CONNECTED TO<br>POWER GRID AT THE TIME<br>OF TRACKING. THE<br>CONTRACTOR AND THE<br>PROJECT SUPERVISOR<br>WERE THUS INVITED. THEY<br>STATED THAT THE<br>TRANSFORMER WAS<br>CONNECTED TO POWER<br>GRID JUST A WEEK AFTER<br>THE TRACKING EXERCISE,<br>THE TEAM REVISITED THE<br>SITE TO CONFIRM THE<br>CLAIM. | BOTH THE 500KVA<br>TRANSFORMER AND SOLAR<br>LIGHTS HAVE BEEN COMPLETE<br>AND WER BEING PUT TO USE.  |
|     |  |                                  |  | ALSO, 30 SOLAR LIGHTS<br>WERE BUDGETED FOR IN<br>THE BOQ, BUT WHILE WE<br>WERE TRACKING THE<br>PROJECT, WE COULD<br>ONLY SIGHT 20. THIS LED<br>TO THE PROJECT<br>SUPERVISOR AND THE<br>CONTRACTOR BEING<br>INVITED TO ACCOUNT FOR<br>THE REMAINING 10 SOLAR<br>LIGHTS. THE TRACKING<br>TEAM WERE LATER TAKEN<br>TO THE SITES WHERE THE<br>REMAINING 10 WERE<br>MOUNTED.       |   |
| 27  | NOTIFICATION OF AWARD OF<br>CONTRACT FOR THE<br>CONSTRUCTION OF MOTORIZED<br>BOREHOLES ACROSS KOGI<br>CENTRAL SENATORIAL DISTRICT,<br>KOGI STATE | ₦39,553,477.51                   | POWER UP<br>PROJECTS INT`L<br>LIMITED    | WE RECOMMENDED<br>RECOVERY OF THE SUM<br>OF N2,250,000.00 BASED<br>ON THE QS REPORT.  | THE TEAM IS WAITING FOR<br>EVIDENCE OF PAYMENT FROM<br>THE CONTRACTOR.  |
| 28  | GRANT DISBURSEMENT TO<br>UNEMPLOYED YOUTHS IN IJUMU<br>LGA, KOGI STATE   | ₩38,000,000                      | MICROVIS<br>MICROFINANCE<br>BANK LIMITED | THERE WAS NO EVIDENCE<br>TO SHOW THAT THE<br>CONTRACT WAS<br>EXECUTED. THE PROJECT<br>SUPERVISOR FAILED TO<br>SHOW UP DURING<br>TRACKING. NO LIST OF<br>BENEFICIARIES IN THE<br>PROJECT FILE.   | THE PROJECT SUPERVISOR AND<br>CONTRACTOR WERE INVITED FOR<br>INTERVIEW BUT THEY FAILED TO<br>SHOW UP WITHOUT ANY<br>EXPLANATION.                      |
| 29  | GRANT DISBURSEMENT TO<br>UNEMPLOYED WOMEN IN IJUMU<br>LGA, KOGI STATE  | ₩38,000,000                      | MICROVIS<br>MICROFINANCE<br>BANK LIMITED | THERE IS NO EVIDENCE TO<br>SHOW THAT THE<br>CONTRACT WAS<br>EXECUTED. THE PROJECT<br>SUPERVISOR FAILED TO<br>SHOW UP DURING<br>TRACKING. NO LIST OF<br>BENEFICIARIES ON THE<br>FILE.  | THE PROJECT SUPERVISOR AND<br>CONTRACTOR WERE INVITED FOR<br>INTERVIEW BUT THEY FAILED TO<br>SHOW UP WITHOUT ANY<br>EXPLANATION.                      |
| 30  | LETTER OF AWARD OF CONTRACT<br>FOR THE TRAINING OF WOMEN<br>AND YOUTHS IN SOAP MAKING IN<br>LOKOJA-KOTO FEDERAL<br>CONSTITUENCY, KOGI STATE      | ₩37,805,600.00                   | FUNMIAYINKE NIG<br>LIMITED               | THE CONTRACT WAS NOT<br>EXECUTED TO<br>SPECIFICATIONS.  | THE CONTRACTOR IS SCHEDULED<br>TO APPEAR BEFORE THE TEAM IN<br>COMMISSION'S OFFICE, ABUJA.  |
| 31  | AWARD OF CONTRACT FOR THE<br>TRAINING AND EMPOWERMENT OF<br>YOUTHS IN AGRICULTURE IN IDAH<br>LGA, KOGI EAST SENATORIAL<br>DISTRICT, KOGI STATE   | ₩49,969,225.00                   | ALTITUDE GLOBAL<br>LINKS LIMITED         | THE CONTRACT WAS NOT<br>EXECUTED ACCORDING TO<br>SPECIFICATIONS.  | THE CONTRACTOR HAS<br>APPEARED BEFORE THE TEAM<br>AND SUBMITTED DOCUMENTS<br>AND RECEIPTS. WE ARE YET TO<br>AGREE ON THE ACTUAL AMOUNT<br>TO RECOVER. |
| 32  | AWARD OF CONTRACT FOR THE<br>TRAINING AND EMPOWERMENT OF<br>YOUTHS IN AGRICULTURE IN ANKPA<br>LGA, KOGI EAST SENATORIAL<br>DISTRICT, KOGI STATE  | ₩49,970,300.00                   | QUATRO ELEMENTS<br>CONSULTS LIMITED      | THE CONTRACT WAS NOT<br>EXECUTED ACCORDING TO<br>SPECIFICATIONS.  | THE CONTRACTOR HAS<br>APPEARED BEFORE THE TEAM<br>AND SUBMITTED DOCUMENTS<br>AND RECEIPTS. WE ARE YET TO<br>AGREE ON THE ACTUAL AMOUNT<br>TO RECOVER. |

| S/N | Project<br>Description  | Contract<br>Sum ( <del>N</del> ) | Name of<br>Contractor                    | Reason for Going<br>Back To Site  | Status/Remark   |
|-----|---|----------------------------------|--|---|---|
| 33  | AWARD OF CONTRACT FOR THE<br>TRAINING AND EMPOWERMENT OF<br>YOUTHS IN AGRICULTURE IN<br>DEKINA LGA, KOGI EAST<br>SENATORIAL DISTRICT, KOGI STATE  | ₩49,976,750.00                   | AMBIENCE IDEAL<br>INNOVATIONS<br>LIMITED | THE CONTRACT WAS NOT<br>EXECUTED IN<br>ACCORDANCE TO<br>SPECIFICATIONS.           | THE CONTRACTOR HAS<br>APPEARED BEFORE THE TEAM<br>AND SUBMITTED DOCUMENTS<br>AND RECEIPTS. WE ARE YET TO<br>AGREE ON THE ACTUAL AMOUNT<br>TO RECOVER. |
| 34  | NOTIFICATION OF AWARD OF<br>CONTRACT UNDER THE 2020<br>CONSTITUENCY PROJECTS: SUPPLY<br>OF INSTRUCTIONAL MATERIALS,<br>EQUIPMENT AND NOTEBOOKS TO<br>UBE JUNIOR SECONDARY SCHOOL,<br>ODEKE, IBAJI LGA, KOGI STATE           | ₩4,275,000.00                    | IGABY LUSY NIG<br>LIMITED                | THERE IS NO EVIDENCE TO<br>SHOW THAT THE ITEMS<br>WERE SUPPLIED TO THE<br>SCHOOL. | THE CONTRACTOR`S<br>APPEARANCE IS BEING AWAITED.  |
| 35  | NOTIFICATION OF AWARD OF<br>CONTRACT UNDER THE 2020<br>CONSTITUENCY PROJECTS: SUPPLY<br>OF INSTRUCTIONAL MATERIALS,<br>EQUIPMENT AND NOTEBOOKS AT<br>ISLAMIYA ALLOMA IN OFU LGA,<br>KOGI STATE                              | ₩4,275,000.00                    | RAGAL CONSULT<br>LIMITED                 | SOME OF THE ITEMS WERE<br>NOT SUPPLIED.   | THE CONTRACTOR`S<br>APPEARANCE IS BEING AWAITED.  |
| 36  | NOTIFICATION OF AWARD OF<br>CONTRACT UNDER THE 2020<br>CONSTITUENCY PROJECTS: SUPPLY<br>OF INSTRUCTIONAL MATERIALS,<br>EQUIPMENT AND NOTEBOOKS TO<br>UBIAJA EJULE PRIMARY SCHOOL,<br>UBIAJA EJULE IN OFU LGA, KOGI<br>STATE | ₩4,850,000.00                    | MC TOGAD LIMITED                         | THERE IS NO EVIDENCE TO<br>SHOW THAT THE ITEMS<br>WERE SUPPLIED TO THE<br>SCHOOL. | THE CONTRACTOR`S<br>APPEARANCE IS BEING AWAITED.  |
| 37  | NOTIFICATION OF AWARD OF<br>CONTRACT UNDER THE 2020<br>CONSTITUENCY PROJECTS: SUPPLY<br>OF INSTRUCTIONAL MATERIALS,<br>EQUIPMENT AND NOTEBOOKS TO<br>LGEA ODOLU SCHOOL 1, ODOLU IN<br>IGALAMELA/ODOLU LGA, KOGI<br>STATE    | ₩8,550,000.00                    | CHIMATHOLA INT`L<br>LIMITED              | THERE IS NO EVIDENCE TO<br>SHOW THAT THE ITEMS<br>WERE SUPPLIED TO THE<br>SCHOOL. | THE CONTRACTOR`S<br>APPEARANCE IS BEING AWAITED.  |
| 38  | NOTIFICATION OF AWARD OF<br>CONTRACT UNDER THE 2020<br>CONSTITUENCY PROJECTS: SUPPLY<br>OF INSTRUCTIONAL MATERIALS,<br>EQUIPMENT AND NOTEBOOKS TO<br>LGEA PRIMARY SCHOOL,<br>OJIGAGALA IN IDAH LGA, KOGI<br>STATE           | <b>₦</b> 4,850,000.00            | BENGNER<br>ENGINEERS LIMITED             | THERE IS NO EVIDENCE TO<br>SHOW THAT THE ITEMS<br>WERE SUPPLIED TO THE<br>SCHOOL. | THE CONTRACTOR`S<br>APPEARANCE IS BEING AWAITED.  |
| 39  | NOTIFICATION OF AWARD OF<br>CONTRACT UNDER THE 2020<br>CONSTITUENCY PROJECTS: SUPPLY<br>OF INSTRUCTIONAL MATERIALS,<br>EQUIPMENT AND NOTEBOOKS TO<br>ST BONIFACE PRIMARY SCHOOL 1,<br>IDAH IN IDAH LGA, KOGI STATE          | <b>₦</b> 4,275,000.00            | TOMOL COMPANY<br>LIMITED                 | MOST OF THE ITEMS WERE<br>NOT RECEIVED BY THE<br>HEAD TEACHER.                    | THE CONTRACTOR`S<br>APPEARANCE IS BEING AWAITED.  |
| 40  | NOTIFICATION OF AWARD OF<br>CONTRACT UNDER THE 2020<br>CONSTITUENCY PROJECTS: SUPPLY<br>OF INSTRUCTIONAL MATERIALS,<br>EQUIPMENT AND NOTEBOOKS TO<br>ST BONIFACE PRIMARY SCHOOL 1,<br>IDAH IN IDAH LGA, KOGI STATE          | ₩4,850,000.00                    | TOMOL COMPANY<br>LIMITED                 | THE ITEMS WERE NOT<br>SUPPLIED TO THE SCHOOL.                                     | THE CONTRACTOR`S<br>APPEARANCE IS BEING AWAITED.  |
| 41  | NOTIFICATION OF AWARD OF<br>CONTRACT UNDER THE 2020<br>CONSTITUENCY PROJECTS: SUPPLY<br>OF INSTRUCTIONAL MATERIALS,<br>EQUIPMENT AND NOTEBOOKS TO<br>UBIAJA EJULE PRIMARY SCHOOL,<br>UBIAJA EJULE IN OFU LGA, KOGI<br>STATE | ₩8,550,000.00                    | MC TOGAD LIMITED                         | PART OF THE ITEMS WERE<br>NOT SUPPLIED.   | THE CONTRACTOR`S<br>APPEARANCE IS BEING AWAITED.  |

| S/N | Project<br>Description  | Contract<br>Sum ( <del>N</del> ) | Name of<br>Contractor               | Reason for Going<br>Back To Site  | Status/Remark  |
|-----|---|----------------------------------|-------------------------------------|---|--|
| 42  | NOTIFICATION OF AWARD OF<br>CONTRACT UNDER THE 2020<br>CONSTITUENCY PROJECTS:<br>PROVISION OF INSTRUCTIONAL<br>MATERIALS, TEXTBOOKS AND BAGS<br>FOR RCM PRIMARY SCHOOL,<br>MAGONGO IN OGORI/MAGONGO<br>LGA, KOGI STATE. | ₩4,750,000.00                    | KINZA DESIGN<br>CONCEPTS LIMITED    | PART OF THE ITEMS WERE<br>NOT SUPPLIED.   | THE CONTRACTOR`S<br>APPEARANCE IS BEING AWAITED.   |
| 43  | NOTIFICATION OF AWARD OF<br>CONTRACT UNDER THE 2020<br>CONSTITUENCY PROJECTS: SUPPLY<br>OF INSTRUCTIONAL MATERIALS,<br>EQUIPMENT AND NOTEBOOKS TO<br>UBE JUNIOR SECONDARY SCHOOL,<br>OBALE IN IBAJI LGA, KOGI STATE     | <b>₩</b> 4,275,000.00            | ZUBYTE<br>ETHERWORX<br>LIMITED      | THERE IS NO EVIDENCE TO<br>SHOW THAT THE ITEMS<br>WERE SUPPLIED TO THE<br>SCHOOL.   | THE CONTRACTOR APPAERED<br>BEFORE THE TEAM ON<br>02/03/2023. HE STATED THAT THE<br>ITEMS WERE PROCURED AND<br>HANDED OVER TO THE SPONSOR.  |
| 44  | AWARD OF CONTRACT FOR THE<br>CONSTRUCTION OF ALL-IN-ONE<br>SOLAR STREETLIGHTS AT IDAH<br>FEDERAL CONSTITUENCY, KOGI<br>STATE  | ₩50,349,948.00<br>(TWO AWARDS)   | ZUBYTE<br>ETHERWORX<br>LIMITED      | THE TEAM DID NOT SIGHT<br>12 UNITS OF ALL-IN-ONE<br>SOLAR STREETLIGHTS<br>DURING THE TRACKING<br>EXERCISE.  | THE CONTRACTOR AND THE<br>PROJECT SUPERVISOR APPAERED<br>BEFORE THE TEAM ON<br>02/03/2023. HE STATED THAT ALL<br>THE ITEMS WERE SUPPLIED AND<br>THAT HE WOULD TAKE THE TEAM<br>TO WHERE THE REMAINING 12<br>UNITS WERE INSTALLED. THE<br>TEAM IS YET TO FIX THE DATE FOR<br>THE INSPECTION OF THE 12 UNITS<br>OF SOLAR LIGHTS. |
| 45  | CONSTRUCTION OF SPORTS<br>CENTRE IN UKWA EAST/WEST<br>FEDERAL CONSTITUENCY, ABIA<br>STATE   | N78,041,565.00                   | JOETEX STANDARD<br>CO. NIG. LTD     | THE PROJECT IS STILL<br>ONGOING BUT THE WORK<br>IS POORLY EXECUTED. THE<br>QS IN HIS REPORT RAISED A<br>LOT OF DIFFERENCES IN<br>COST OF EXECUTION.   | THE CONTRACTOR WAS SENT<br>BACK TO SITE TO COMPLETE THE<br>PROJECT AND CORRECT THE<br>SHORT-COMINGS AND FAULTS<br>IDENTIFIED.  |
| 46  | CONSTRUCTION OF A PRIMARY<br>CARE CENTRE (LEVEL 2) IN<br>MAKARFI LOCAL GOVERNMENT<br>AREA OF KADUNA STATE   | N35,512,738.62                   | KAINATOCHI<br>INVESTMENT<br>LIMITED | THAT CONTRACT WAS<br>SHODDILY EXECUTED, AND<br>SOME ITEMS IN THE BILL OF<br>QUANTITY WERE NOT<br>SUPPLIED AND INSTALLED<br>ACCORDINGLY.   | THE CONTRACTOR HAS<br>REFUNDED THE SUM OF<br>N1,227,200, AND THE TEAM IS<br>FIXING A DATE TO VISIT THE SITE<br>WITH THE CONTRACTOR IN<br>ORDER TO DIRECT HIM ON THE<br>RENOVATIONS TO EMBARK ON .  |
| 47  | AWARD OF CONTRACT FOR<br>CONTINUATION OF WORK ON<br>CONSTRUCTION OF AKAMKPA<br>INTERNAL ROADS (DEEPER LIFE<br>ROAD) AKAMKPA LGA, CROSS<br>RIVER STATE.  | <b>₩</b> 89,983,195.52           | DOVITOM POWER<br>& ENERGY LIMITED   | <ol> <li>TO COVER THE<br/>FIELD AREA OF<br/>5,110.00m<sup>2</sup> AS<br/>SPECIFIED IN THE<br/>BOQ.</li> <li>TO LAY PRIME<br/>COAT<br/>BITUMINOUS<br/>SURFACING MC1<br/>AS SPECIFIED IN<br/>THE BOQ.</li> </ol>  | AWAITING RESPONSE FROM THE<br>EXECUTING AGENCY.  |
| 48  | AWARD OF CONTRACT FOR<br>CONSTRUCTION OF CLASSROOM<br>BLOCK AT BELINGE PRIMARY<br>SCHOOL, BECHEVE WARD,<br>BEKWARA, OBANLIKU & OBUDU<br>LGAS FEDERAL CONSTITUENCY,<br>CROSS RIVER STATE.                                | ₩15,680,450.75                   | JJO MARITIME<br>VENTURES LIMITED    | <ol> <li>TO PERFECT ALL<br/>ROOF LEAKAGES.</li> <li>TO COMPLETE<br/>THE INSTALLATION<br/>OF THE REMAINING<br/>3WCs, 3WASH<br/>HAND BASINS<br/>AND 3 TISSUE<br/>HOLDERS.</li> <li>TO INSTALL ALL<br/>THE ELECTRICAL<br/>WORK AS SPECIFIED<br/>IN THE BOQ.</li> </ol> | AWAITING RESPONSE FROM THE<br>EXECUTING AGENCY.  |
| 49  | AWARD OF CONTRACT FOR<br>CONSTRUCTION OF COMMUNITY<br>TOWN HALL AT ADIM, BIASE LGA,<br>CROSS RIVER STATE.   | <b>₩</b> 44,167,715.55           | DOVELINE<br>INVESTMENT<br>LIMITED   | <ol> <li>TO COMPLETE<br/>THE<br/>INSTALLATION OF<br/>THE REMAINING<br/>EIGHT (8) CEILING<br/>FANS.</li> <li>TO COMPLETE<br/>THE TILING WORK.</li> </ol>   | AWAITING RESPONSE FROM THE<br>EXECUTING AGENCY.  |

| S/N | Project<br>Description  | Contract<br>Sum ( <del>N</del> ) | Name of<br>Contractor                            | Reason for Going<br>Back To Site   | Status/Remark                                   |
|-----|---|----------------------------------|--|--|---|
| 50  | AWARD OF CONTRACT FOR<br>CONSTRUCTION OF CIVIC CENTRE<br>IN ABIJANG COMMUNITY ETUNG<br>LGA, CROSS RIVER STATE<br>SENATORIAL DISTRICT, CROSS<br>RIVER STATE.   | <b>№</b> 6,574,661.00            | M. E. UDUEZUE &<br>SONS ENT. LIMITED             | <ol> <li>TO COMPLETE<br/>THE<br/>CONSTRUCTION<br/>OF THE SOAK<br/>AWAY SYSTEM.</li> <li>TO INSTALL THE<br/>ONE (1) WC AND<br/>ONE (1) WASH<br/>HAND BASIN AS<br/>STATED IN THE<br/>BOQ.</li> </ol>   | PROJECT COMPLETED.                              |
| 51  | AWARD OF CONTRACT FOR THE<br>CONSTRUCTION OF 3 NOS<br>CLASSROOM BLOCKS IN ST. PAUL'S<br>PRIMARY SCHOOL, JJEGU, YALA<br>LGA, CROSS RIVER NORTH<br>SENATORIAL DISTRICT, CROSS<br>RIVER STATE.           | ₩15,750,000.00                   | LILY OF VALLEY<br>CORPORATE<br>CONCERNS LIMITED. | TO RECTIFY ALL THE<br>ISSUES RAISED TO<br>CONFORM TO ALL THE<br>SPECIFICATIONS IN THE<br>BOQ.<br>1. INSTALL THE<br>REMAINING FIVE<br>(5) DOORS<br>2. INSTALL THE<br>PROJECT SIGN<br>POST<br>3. INTSTALL<br>TERRAZZO<br>FLOORING<br>4. INSTALL<br>ASBESTOS<br>CEILING<br>5. FIX THE CRACKS<br>ON THE WALLS. | AWAITING RESPONSE FROM THE<br>EXECUTING AGENCY. |
| 52  | AWARD OF CONTRACT FOR THE<br>CONSTRUCTION OF 3 NOS<br>CLASSROOM BLOCKS IN ST.<br>JOSEPH'S PRIMARY SCHOOL,<br>OKUKU, YALA LGA, CROSS RIVER<br>NORTH SENATORIAL DISTRICT,<br>CROSS RIVER STATE (ZONAL). | <b>₩</b> 14,962,500.00           | SOMCHI MEGA<br>SOLUTIONS LIMITED                 | TO INSTALL THE<br>REMAINING FIVE (5)<br>DOORS.   | AWAITING RESPONSE FROM THE<br>EXECUTING AGENCY. |
| 53  | NOTIFICATION OF AWARD OF<br>CONTRACT FOR THE<br>CONSTRUCTION OF 2NOS SCHOOL<br>BLOCKS IN BOKI/IKOM FEDERAL<br>CONSTITUENCY, CROSS RIVER<br>STATE (ZONAL).   | ₩27,945,386.00                   | RYTE REASONS<br>LIMITED                          | <ol> <li>TO PROPERLY<br/>PAINT THE<br/>BUILDING AS<br/>SPECIFIED IN<br/>BOQ.</li> <li>TO COMPLETE<br/>THE ELECTRICAL<br/>WORKS NOT<br/>DONE IN THE<br/>BUILDING.</li> <li>TO PROVIDE AND<br/>INSTALL THE WHITE<br/>MARKER BOARDS.</li> </ol>   | AWAITING RESPONSE FROM THE<br>EXECUTING AGENCY. |
| 54  | NOTIFICATION OF AWARD OF<br>CONTRACT FOR THE<br>CONSTRUCTION OF 2NOS SCHOOL<br>BLOCKS IN BOKI/IKOM FEDERAL<br>CONSTITUENCY, CROSS RIVER<br>STATE (ZONAL).   | <b>₩</b> 11,976,594.00           | RYTE REASONS<br>LIMITED                          | <ol> <li>TO PROPERLY<br/>PAINT THE<br/>BUILDING AS<br/>SPECIFIED IN<br/>BOQ.</li> <li>TO COMPLETE<br/>THE ELECTRICAL<br/>WORKS NOT<br/>DONE IN THE<br/>BUILDING.</li> <li>TO PROVIDE<br/>AND INSTALL<br/>THE WHITE<br/>MARKER<br/>BOARDS.</li> </ol>   | AWAITING RESPONSE FROM THE<br>EXECUTING AGENCY. |

| S/N | Project<br>Description   | Contract<br>Sum ( <del>N</del> ) | Name of<br>Contractor                               | Reason for Going<br>Back To Site  | Status/Remark  |
|-----|--|----------------------------------|---|---|--|
| 55  | CONTRACT FOR CONSTRUCTION<br>OF MODERN SPORT AND EVENT<br>CENTRE IN ILUTITUN, OKITIPUPA<br>LGA, ONDO STATE.  | <b>₩</b> 70,993,920.23           | MESSRS HEF<br>CONSULTING<br>LIMITED                 | THE CONTRACTOR WAS<br>FOUND NOT TO HAVE<br>DELIVERED FOUR ITEMS: 6<br>STANDING ACS, 4 FIRE<br>EXTINGUISHERS, 6 SOLAR<br>PANELS AND FOUR SOLAR<br>INDEPENDENT SECURITY<br>LIGHTS.  | THE CONTRACTOR HAS COMPLIED<br>AND ALL ITEMS HE DID NOT<br>PROVIDE WERE SUPPLIED AND<br>INSTALLED.   |
| 56  | PROVISION OF 1 NO SOLAR<br>POWERED GRID & 7 NO SOLAR<br>STREET LIGHT IN NYSC, IKARE,<br>AKOKO, ONDO STATE.   | <b>№</b> 14,660,635              | MESSRS AUWAL<br>BAMANGA<br>ENTERPRISES LTD          | AT THE POINT OF<br>TRACKING, THE TEAM DID<br>NOT KNOW BETWEEN<br>THIS CONTRACTOR AND Q<br>ASSOCIATES WHOSE GRID<br>HAD FAILED HENCE HE<br>WAS TOLD TO GO BACK<br>TO SITE.   | IT WAS FOUND THAT THE NON-<br>PERFORMING GRID WERE FOR<br>ANOTHER CONTRACTOR. HIS<br>PROJECTS ARE FUNCTIONING<br>PROPERLY.   |
| 57  | NOTIFICATION OF AWARD OF<br>CONTRACT FOR THE PROPOSED<br>PROCUREMENT AND EQUIPMENT<br>AND MATERIALS FOR TRAINING<br>FOR CAPACITY BUILDING IN<br>LEATHER IN OKA AKOKO, ONDO<br>STATE. | ₩39,783,783.38                   | MESSRS<br>FORTIFIED CITY<br>TECHNOLOGIES<br>NIG LTD | THE LIST OF<br>BENEFICIARIES /<br>PARTICIPANTS WAS NOT<br>ATTACHED.   | THE CONTRACTOR HAS SUBMITTED<br>THE LIST OF THE BENEFICIARIES AS<br>REQUESTED.   |
| 58  | CONTRACT FOR THE COMPLETION<br>OF SPORT PAVILION IN ODIGBO<br>TOWN IN ILE-<br>OLUJI/OKEIGBO/ODIGBO FEDERAL<br>CONSTITUENCY, ONDO STATE.  | ₩27,609,304.01                   | MESSRS FUNSIM<br>GLOBAL LTD                         | THE PERIMETER FENCE<br>WAS NOT COMPLETED<br>AND A PORTION OF IT HAS<br>ALREADY FALLEN OFF.<br>THE PAVILION IS<br>EXPECTED TO BE FITTED<br>WITH SEATS BUT WAS NOT<br>DONE.<br>THE TEAM OBSERVED<br>UNDULATING AND SLOPPY<br>PLAYING PITCH. | THE CONTRACTOR IS ALREADY ON<br>SITE AND HE IS FIXING THE<br>IDENTIFIED FAULTS AS HE WAS<br>DIRECTED.  |
| 59  | AWARD OF CONTRACT FOR<br>GRADING AND PROVISION OF<br>ACCESS ROADS IN ILE-<br>OLUJI/OKEIGBI/ ODIGBO FEDERAL<br>CONSTITUENCY OF ONDO STATE   | N29,981,025.00                   | MESSRS HEF<br>CONSULTING<br>LIMITED                 | SOME PORTIONS OF THE<br>GRADED ROADS AND<br>ACCESS ROADS<br>DEGENERATED DUE TO<br>PERSISTENT RAINS.   | THE CONTRACTOR REMOBILISED TO<br>SITE FROM 20 <sup>TH</sup> -25 <sup>TH</sup> JANUARY, 2023<br>AND HAS COMPLETED THE PROJECT.  |
| 60  | AWARD OF CONTRACT FOR THE<br>PERIMETER <i>FENCING</i> OF MUSLIM<br>SCHOOL, ILEPA IKARE, ONDO<br>STATE.   | N40,113,858.27                   | MESSRS VIRGRISS<br>RESOURCES<br>LIMITED             | THE DOOR TO THE<br>SECURITY HOUSE AND THE<br>GATE WERE<br>CONSTRUCTED WITH<br>INFERIOR MATERIALS.   | THE CONTRACTOR HAS<br>REPORTEDLY FIXED THE TWO ITEMS<br>AND HAS ALSO REPAINTED THE<br>FENCE. WE ONLY SAW THE PICTURE<br>TO THAT EFFECT.  |
| 61  | AWARD OF CONTRACT FOR THE<br>CONSTRUCTION OF ROAD WITH<br>DRAINAGES IN OWASE<br>COMMUNITY, ONDO NORTH<br>SENATORIAL DISTRICT, ONDO<br>STATE.   | N153,592,398.75                  | MESSRS TROIS<br>ASSOCIATES<br>LIMITED               | THE TWO-KILOMETRE<br>ROAD PROJECT AWARDED<br>IN 2020 OUGHT TO HAVE<br>BEEN COMPLETED. AS AT<br>THE TIME OF TRACKING<br>THE PERFORMANCE LEVEL<br>WAS LESS THAN ONE<br>KILOMETRE.   | THE AGENCY 'S SUPERVISOR<br>INFORMED THE TEAM IN HIS<br>STATEMENT THAT THE CONTRACTOR<br>HAS DONE THE WORK FOR WHICH<br>MONEY WAS PAID WAS CLAIMING HE<br>RAN OUT OF MONEY. WHILE<br>ASSURING THE TEAM THAT THE<br>INSTITUTE (EMDI) HAD RECEIVED ALL<br>THE CONTRACT SUM, HE STATED<br>THAT THE CONTRACTOR WAS THE<br>ONE THAT WAS NOT FORTH<br>COMING. HE HAS HOWEVER FILED<br>FOR VARIATION WHICH THE<br>INSTITUTE WAS CONSIDERING.  |
| 62  | AWARD OF CONTRACT FOR THE<br>PROVISION OF 1NO. SOLAR GRID<br>AND 7NO, STREET LIGHTS IN NYSC<br>CAMP, AREA 2, IKARE AAKOKO,<br>ONDO STATE.  | N17,135,622.55                   | MESSRS Q<br>ASSOCIATES<br>LIMITED                   | THE SOLAR POWERED<br>GRID CEASED TO<br>FUNCTION SHORTLY<br>AFTER IT WAS INSTALLED.  | THE CONTRACTOR CLAIMED IN HIS<br>STATEMENT THAT THE GRID WAS<br>FUNCTIONING WHEN HE WAS PAID<br>RETENTION FEES. THE TEAM CALLED<br>HIS ATTENTION TO THE FACT THAT<br>THE GRID INSTALLED BY THE OTHER<br>CONTRACTOR WAS FUNCTIONING<br>AND THERE WAS NO VALUE FOR<br>MONEY ON HIS PROJECT. HE SAID<br>HE WAS ARRANGING FOR A MEETING<br>WITH NYCS, ECN FOR $8^{TH}$ OF MARCH,<br>2023 AND HE REQUESTED THE TEAM<br>TO BE PART OF THE MEETING. HE<br>SAID IF IT IS FOUND THAT HE IS AT<br>FAULT HE WILL FIX THE PROBLEM. |

| S/N | Project<br>Description   | Contract<br>Sum ( <del>N</del> )  | Name of<br>Contractor                                       | Reason for Going<br>Back To Site   | Status/Remark  |
|-----|--|---|---|--|--|
| 63  | AWARD OF CONTRACT FOR THE<br>CONSTRUCTION OF GARI<br>PROCESSING FACTORY IN OGBAGI,<br>ONDO NORTH SENATORIAL<br>DISTRICT OF ONDO STATE  | N178,101,170.56<br>(CONTRACT<br>SUM)<br>N21,065,705.49<br>(CONSULTANCY) | MESSRS<br>FORTIFIED CITY<br>TECHNOLOGIES<br>NIGERIA LIMITED | THE CONTRACTOR WAS<br>ON SITE AS AT THE TIME<br>OF TRACKING.   | THE TEAM ADVISED THE<br>CONTRACTOR TO HASTEN UP THE<br>WORK ON SITE.<br>THE FIRST PHASE WORTH<br>N84,200.721 HAS BEEN COMPLETED.   |
| 64  | PURCHASE OF EMPOWERMENT<br>MATERIALS FOR YOUTHS AND<br>WOMEN IN AKOKO NORTH/EAST<br>AND NORTH/WEST FEDERAL<br>CONSTITUENCY, ONDO STATE,  | N88,236,000.00  | MESSRS RAY<br>MARTINS<br>BUSINESS<br>SOLUTION<br>LIMITED    | THERE WAS NO LIST OF<br>BENEFICIARIES.   | THE CONTRACTOR, THE SPONSOR<br>OF THE PROJECT AND THE<br>AGENCY'S SUPERVISOR STATED<br>THAT THEY DID NOT RECORD THE<br>BENEFICIARIES HENCE THERE IS NO<br>LIST OF THE BENEFICIARIES.   |
| 65  | AWARD OF CONTRACT FOR THE<br>CONSTRUCTION OF 40 UNITS OF<br>MARKETS STALL IN ISUWA, ONDO<br>NORTH SENATORIAL DISTRICT,<br>ONDO STATE.  | <b>₩</b> 69,945,649.00  | MESSRS HASADEL<br>INTERNATIONAL<br>CONCEPT LTD              | DETAILED INFORMATION<br>ABOUT PAYMENTS, TAX<br>CONSULTANCY WERE NOT<br>PROVIDED.<br>THE DETAILS OF THE FUND<br>RELEASED NEED MORE<br>CLARIFICATION FROM THE<br>AGENCY. | THE TEAM DID NOT SEE EVIDENCE<br>OF TAX PAYMENT FOR THIS PROJECT<br>EXCEPT A CERTIFICATE OF TAX<br>CLEARANCE FROM FIRS. THE<br>CONTRACTOR HAS PROMISED TO<br>SEND EVIDENCE OF TAX DEDUCTION<br>TO THE TEAM. MEANWHILE THE<br>STORES HAVE BEEN ALLOCATED<br>AND EVIDENCE OF ALLOTMENTS<br>SENT TO TEAM. |
| 66  | AWARD OF CONTRACT FOR THE<br>CONSTRUCTION OF A BLOCK OF 3<br>CLASS ROOMS EACH IN SELECTED<br>PRIMARY SCHOOLS IN BOSSO LGA<br>OF BOSSO/PAIKORO FEDERAL<br>CONSTITUENCY, NIGER STATE   | N28,860,000   | ZEPPELIN<br>INTENATIONAL<br>CONCEPTS<br>LIMITED             | TO REPLACE LEAKED<br>ROFING AND DAMAGED<br>CEILLING SHEETS.  | THE FAULTS HAVE BEEN FIXED.<br>THE CONTRACTOR REFUNDED<br>N500,000 MEANT FOR ELECTRICAL<br>FITTINGS.   |
| 67  | AWARD OF CONTRACT FOR<br>CONSTRUCTION OF HEALTH CARE<br>CENTERS AT MUNYA AND BOSSO<br>LGAS IN NIGER EAST SENATORIAL<br>DISTRICT, NIGER STATE   | N97,622,631.25  | SELSA LOGISTICS<br>SERVICES LIMITED                         | TO COMPLETE DRILLING<br>OF TWO BOREHOLES AT<br>THE HEALTH CENTERS.   | PROJECT COMPLETED.   |
| 68  | AWARD OF CONTRACT FOR<br>PROVISION OF 20 NO. HAND PUMP<br>BOREHOLES IN NIGER EAST<br>SENATORIAL DISTRICT (SULEJA,<br>TAFA, GURARA, PAIKORO,<br>CHANCHAGA LGAS)   | N39,791,240.00  | OCEANIC WORLD<br>SYSTEM SERVICES<br>LTD                     | TO COMPLETE DRILLING<br>OF TWO HAND PUMP<br>BOREHOLES.   | PROJECT COMPLETED.   |
| 69  | AWARD OF CONTRACT FOR THE<br>CONSTRUCTION OF EASTERN<br>(NGWAMATSE) AND WESTERN<br>(UMARU MAIDUBU) CITY GATES IN<br>KONTAGORA TO PROMOTE<br>TOURISM AND YOUTH<br>EEMPOWERMENT IN NIGER NORTH<br>SENATORIAL DISTRICT, NIGER<br>STATE. | N41,129,500.00  | MA-BINDIGA &<br>SONS NIG. LTD                               | TO COMPLETE SOME<br>ELEMENTS OF THE<br>PROJECT THAT WERE NOT<br>EXECUTED.  | CONTRACTOR YET TO RETURN TO<br>SITE.   |
| 70  | RE-CONSTRUCTION OF 20<br>KILOMETER NEW-BUSSA TOWNSHIP<br>ROAD, NIGER STATE   | N180,109,161.05   | HIKAM<br>ENGINEERING &<br>CONSULTANCY<br>LTD                | FILLING OF PORTHOLES.  | PROJECT COMPLETED.   |

| S/N | Project<br>Description   | Contract<br>Sum ( <del>N</del> ) | Name of<br>Contractor                           | Reason for Going<br>Back To Site  | Status/Remark   |
|-----|--|----------------------------------|---|---|---|
| 71  | AWARD OF CONTRACT FOR THE<br>COMPLETION OF THE<br>CONSTRUCTION OF MINI STADIUM<br>FACILITIES IN NDEABOH, ANINRI<br>LGA, ENUGU STATE"   | ₩57,000,000.00                   | MESSRS KANOSKY<br>ENTERPRISES LTD               | FUNDS RELEASED TO THE<br>CONTRACTOR BY THE<br>EXECUTING AGENCY WAS<br>INSUFFICIENT.   | THE CONTRACTOR AGREED TO<br>COMPLETE THE OUTSTANDING<br>JOB WITHIN 3 MONTHS.<br>EXECUTING AGENCY-SDG YET TO<br>RELEASE THE REMAINING<br>BALANCE.  |
| 72  | PROVISION OF MOTORISED<br>BOREHOLE EACH AT UMOBOSI-<br>IGBERE SECONDARY SCHOOL<br>EZEUKEU, OKAGBUE ITEM IN<br>BENDE ABIA NORTH SENATORIAL<br>DISTRICT ABIA STATE             | N37,497,478.13                   | Messrs; UNFURLS<br>UMUEGEDE<br>LIMITED          | THE TEAM TRACKED THE<br>PROJECT AT THE 3<br>LOCATION AND IDENTIFIED<br>SOME WORKS TO BE<br>CORRECTED ACCORDING TO<br>QS REPORT.   | THE CONTRACTOR AND PROJECT<br>SUPERVISOR WERE ASKED TO<br>RETURN TO SITE FOR<br>AMENDMENT OF WORK<br>RECOMMENDED IN THE QS<br>REPORT.   |
| 73  | AWARD OF CONTRACT FOR THE<br>PART-REHABILITATION OF 2<br>PRIMARY SCHOOL BLOCKS IN<br>OHAFIA LGA, ABIA NORTH<br>SENATORIAL DISTRICT, ABIA STATE<br>(BUDGET CODE: 2020ZIPO948) | N20,000,000.00                   | Messrs;<br>CAVERNOUS<br>COUNTY LIMITED          | THAT THE PROJECT WAS<br>EXECUTED EXCEPT SOME<br>MINOR DEFECTS, HOWEVER,<br>THE CONTRACTOR WAS<br>DIRECTED TO RETURN TO<br>SITE TO MEND THE<br>IDENTIFIED MINOR DEFECTS.   | THE CONTRACTOR AND PROJECT<br>SUPERVISOR WERE ASKED TO<br>RETURN TO SITE TO MEND SOME<br>DEFECTS AS INDICTAED IN THE QS<br>REPORT.  |
| 74  | AWARD OF CONTRACT FOR THE<br>CONSTRUCTION OF 8KM ROAD<br>(2KM PHASE 1) WITH ASPHALT AND<br>DRAINAGE AT BENDE LGA, ABIA<br>NORTH SENATORIAL DISTRICT, ABIA<br>STATE           | N240,000.000.00                  | Messr; JERRON<br>AND PARTNERS<br>INTEGRATED LTD | THAT THE CONTRACT FOR<br>THE CONSTRUCTION OF<br>(2KM PHASE 1) WAS<br>EXECUTED WITH LOTS OF<br>DEFECTS.  | THE CONTRACTOR AND PROJECT<br>SUPERVISOR WERE ASKED TO<br>RETURN TO SITE MEND<br>THE IDENTIFIED DEFECTS.  |
| 75  | AWARD OF CONTRACT FOR THE<br>CONSTRUCTION OF WATER<br>RELATED PROJECTS IN THE SOUTH<br>EAST GEOPOLITICAL ZONE: 2020<br>APPROPRIATION ACT                                     | N20,000,000.00                   | Messr;<br>INSPIRATIONS<br>FUNCTION<br>LIMITED   | THAT THE 3 <sup>RD</sup> TRANSFORMER<br>WAS NOT TRACKED DUE TO<br>LACK OF LEAD TO THE<br>LOCATION AS NEITHER THE<br>CONTRACTOR NOR THE<br>EXECUTING AGENCY<br>SHOWED UP AT THE<br>PROJECT SITE , MORESO;<br>THAT ENGR. BONA IWUEKE<br>(PRINCIPAL ELECTRICAL<br>ENGINEER) WITH THE<br>EXECUTING AGENCY<br>ALONGSIDE THE<br>CONTRACTOR TO EXPLAIN<br>WHAT HAPPENDED WITH<br>THE THIRD TRANSFORMER,<br>WHETHER IT EXISTS OR NOT. | THE THIRD TRANSFORMER WAS<br>PROVIDED AND THE<br>CONTRACTOR IS ON SITE<br>WORKING ON THE INSTALLATION.  |
| 76  | AWARD OF CONTRACT FOR THE<br>INSTALLATION AND REPAIRS OF<br>INSTALLED SOLAR POWER STREET<br>LIGHT IN ABIA SOUTH SENATORIAL<br>DISTRICT, ABIA STATE                           | N100,000,000.00                  | Messrs; UG<br>INTEGRATED<br>CONCEPTS LTD        | THE CONTRACTOR WAS<br>DIRECTED TO RETURN TO<br>SITE FOR THE INSTALLATION<br>OF 11 SOLAR LIGHT OR<br>REFUND ITS VALUE TO THE<br>COMMISSION BEFORE CLOSE<br>OF THE PROJECT FILE.  | THE CONTRACTOR WAS ASKED<br>TO RETURN TO SITE.  |
| 77  | AWARD OF CONTRACT FOR THE<br>INSTALLATION AND REPAIRS OF<br>INSTALLED SOLAR POWER STREET<br>LIGHT IN ABIA SOUTH SENATORIAL<br>DISTRICT, ABIA STATE                           | N100,000,000.00                  | Messrs A4A<br>INTERNATIONAL<br>LIMITED          | THAT REVIEW OF THE<br>PROJECT BE DONE<br>THROUGH THE QS REPORT<br>TO DETERMINE THE QUALITY<br>OF SOLAR LIGHTS INSTALLED<br>AND WHY SOME ARE NOT<br>FUNCTIONING WHILE THEY<br>WERE RECENTLY INSTALLED<br>BY THE CONTRACTOR.  | THE CONTRACTOR WAS ASKED<br>TO RETURN TO SITE.  |
| 78  | DRILLING HANDPUMPS IN VARIOUS<br>COMMUNITIES IN GAMAWA<br>FEDERAL CONSTITUENCY, BAUCHI<br>STATE  | N17,476,640.00                   | EMMA VENTURES<br>INVESTMENT<br>NIGERIA LIMITED  | SHODDY EXECUTION OF THE<br>CONTRACT AS ONLY 4 OUT<br>OF THE 10 BOREHOLES<br>WERE SIGHTED AND THOSE<br>FOUR WERE POORLY<br>CONSTRUCTED.  | 1. THE CONTRACTOR AND<br>SUPERVISOR FROM THE<br>EXECUTING AGENCY WERE<br>DIRECTED TO RETURN TO SITE<br>AND WORK ON THE HANDPUMPS<br>ACCORDING TO THE<br>SPECIFICATIONS.<br>2. THEY REPORTED THAT THEY<br>HAVE GONE BACK TO ALL THE<br>SITES AND HAVE PUT THE<br>PROJECT IN ORDER. THE TEAM<br>HAS NOT GONE FOR<br>CONFIRMATORY VISIT YET. |

| S/N | Project<br>Description  | Contract<br>Sum ( <del>N</del> ) | Name of<br>Contractor                    | Reason for Going<br>Back To Site   | Status/Remark   |
|-----|---|----------------------------------|--|--|---|
| 79  | PROVISION OF HEALTH CENTRE IN<br>OGUN CENTRAL SENATORAL<br>DISTRICT, OGUN STATE.<br>OPS/CEPTD/LG/009  | 39,996,000.00                    | GGB NOYCEE<br>NIGERIA LIMITED            | CONTRACTOR TO FIX THE<br>BOREEHOLE AND CONNECT<br>IT TO THE HEALTH CENTRE.   | THE CONTRACTOR AND PROJECT<br>SUPERVISOR WERE ASKED TO<br>RETURN TO SITE TO FIX THE<br>BOREHOLE AND LINK IT TO THE<br>HEALTH CENTRE AS DIRECTED BY<br>THE TRACKING TEAM.                |
| 80  | AWARD OF CONTRACT FOR THE<br>CONSTRUCTION OF AKO<br>COMMUNITY HALL, AKO-MATOOLE,<br>AGO-IWOYE, IJEBU NORTH LGA,<br>OGUN STATE   | 48,121,506.40                    | BIZERVE NIGERIA<br>LIMITED               | PROJECT TO BE FURTHER<br>MONITORED AS IT WAS<br>ONGOING AS AT THE TIME<br>OF TRACKING.<br>WORKERS/LABOURERS<br>WERE SEEN WORKING AT<br>THE PROJECT SITE.                         | PROJECT IS STILL ONGOING  |
| 81  | AWARD OF CONTRACT FOR THE<br>CONTRUCTION OF MINI SPORT<br>CENTRE AT OBAFEMI OWODE<br>HEADQUARTERS, ABEOKUTA<br>NORTH, OBAFEMI OWODE/ODEDA<br>FEDERAL CONSTITUENCY, OGUN<br>STATE.   | 84,588,261.10                    | ABLOOM TRUST<br>NIGERIA LIMITED          | THAT THE CONTRACTOR BE<br>DIRECTED TO RETURN TO<br>SITE. THE APPROPRIATED<br>AMOUNT FOR YEAR 2021<br>WAS (N41,500,000.00)<br>LOWER THAN THE<br>CONTRACT SUM<br>(N84,588,261.10). | THE CONTRACTOR HAS SINCE<br>RETURNED TO SITE AND WORK IS<br>ONGOING.  |
| 82  | AWARD OF CONTRACT FOR<br>FURNISHING OF A BLOCK OF THREE<br>(3) CLASSROOM WITH OFFICE AND<br>STORE AT COMPREHENSIVE<br>COLLEGE, FREDERICK ADEOYE<br>ESTATE, OBOLO ROAD, IMEKO,<br>IMEKO-AFON LOCAL GOERNMENT<br>AREA, OGUN STATE | 24,000,000.00                    | DUTCHE PORT<br>GLOBAL SERVICES<br>LIMTED | THE CONTRACTOR TO SHOW<br>EVIDENCE OF<br>EXECUTION/IMPLEMENTATIO<br>N OF THE PROJECT.  | THE PROJECT SUPERVISOR AND<br>THE CONTRACTOR WERE AT THE<br>COMMISSION'S LAGOS OFFICE ON<br>12 <sup>TH</sup> JANUARY, 2023 TO PRESSENT<br>EVIDENCE OF IMPLEMENTATION<br>OF THE PROJECT. |
| 83  | AWARD OF CONTRACT FOR SDGs<br>ZONAL INTERVENTION PROJECT<br>FOR THE SUPPLY OF 244 NOS<br>SEWING MACHINES TO OGUN WEST<br>SENATORIAL DISTRICT, OGUN STATE  | 19,567,000.00                    | ARSHOS NIGERIA<br>LIMITED                | THE TEAM WAS TO GET<br>PHONE NUMBERS OF THE<br>NAMES ON THE BENEFICIARY<br>LIST AND ASCERTAIN IF THEY<br>REALLY GOT THE ITEMS.   | TEAM PUT CALLS THROUGH TO<br>SOME OF THE BENEFICIARIES AND<br>THEY CONFIRMED BENEFFITING<br>FROM THE EMPOWERMENT<br>PROGRAMME.  |
| 84  | GRANTS FOR PROMOTION OF<br>AGRICULTURAL BUSINESS IN IJEBU-<br>ODE/ODOGBOLU/IJEBU NORTH-<br>EAST FEDERAL CONSTITUENCY,<br>OGUN STATE.  | 47,500,000.00                    | GOBARAU MICRO<br>FINANCE BANK<br>LIMITED | FURTHER INVESTIGATION<br>RECOMMENDED. TEAM<br>SHOULD OBTAIN LIST OF<br>BENEFIICIARIES AND<br>CONFIRM HOW MUCH THEY<br>WERE PAID AND THROUGH<br>WHICH MEANS.                      | TEAM TRACED PART OF THE<br>MONEY TO SOME COMPANIES<br>AND THE HONOURABLE'S<br>ACCOUNT. THE HONOURABLE<br>HAS BEEN INVITED.  |
| 85  | GRANTS FOR PROMOTION OF<br>SMALL-SCALE BUSINESS IN IJEBU-<br>ODE/ODOGBOLU/IJEBU NORTH-<br>EAST FEDERAL CONSTITUENCY,<br>OGUN STATE.   | 47,500,000.00                    | GOBARAU MICRO<br>FINANCE BANK<br>LIMITED | FURTHER INVESTIGATION<br>RECOMMENDED. TEAM<br>SHOULD OBTAIN LIST OF<br>BENEFICIARIES AND<br>CONFIRM HOW MUCH THEY<br>WERE PAID AND THROGH<br>WHICH MEANS.                        | TEAM TRACED PART OF THE<br>MONEY TO SOME COMPANIES<br>AND THE HONOURABLE'S<br>ACCOUNT. THE HONOURABLE<br>HAS BEEN INVITED FOR<br>INTERVIEW.   |
| 86  | GRANTS FOR NEW BUSINESS<br>INITIATIVES AND SUSTAINTABILITY<br>IN IFO/EWEKORO FEDERAL<br>CONSTITUENCY, OGUN STATE.   | 42,750,000.00                    | GOBARAU MICRO<br>FINANCE BANK<br>LIMITED | FURTHER INVESTIGATION<br>RECOMMENDED. TEAM<br>SHOULD OBTAIN LIST OF<br>BENEFICIARIES AND<br>CONFIRM HOW MUCH THEY<br>WERE PAID AND THROGH<br>WHICH MEANS.                        | TEAM TRACED PART OF THE<br>MONEY TO SOME COMPANIES<br>AND THE HONOURABLE'S<br>ACCOUNT. THE HONOURABLE<br>HAS BEEN SUMMONED.   |
| 87  | GRANTS FOR PROMOTION OF<br>SMALL-SCALE BUSINESS IN<br>EWEKORO LOCAL GOVERNMENT<br>AREA, IFO/EWEKORO FEDERAL<br>CONSTITUENCY, OGUN STATE.  | 45,600,000.00                    | GOBARAU MICRO<br>FINANCE BANK<br>LIMITED | FURTHER INVESTIGATION<br>RECOMMENDED. TEAM<br>SHOULD OBTAIN LIST OF<br>BENEFICIARIES AND<br>CONFIRM HOW MUCH THEY<br>WERE PAID AND THROGH<br>WHICH MEANS.                        | TEAM TRACED PART OF THE<br>MONEY TO SOME COMPANIES<br>AND THE HONOURABLE'S<br>ACCOUNT. THE HONOURABLE<br>HAS BEEN INVITED.  |
| 88  | GRANTS FOR YOUTHS AND<br>WIDOW/WIDOWER<br>EMPOWERMENT IN ADO-ODO/ OTA<br>FEDERAL CONSTITUENCY, OGUN<br>STATE.   | 38,000,000.00                    | HAMADA MFBANK<br>LIMITED                 | FURTHER INVESTIGATION<br>RECOMMENDED. TEAM<br>SHOULD OBTAIN LIST OF<br>BENEFICIARIES AND<br>CONFIRM HOW MUCH THEY<br>WERE PAID AND THROGH<br>WHICH MEANS.                        | TEAM TRACED PART OF THE<br>MONEY TO SOME COMPANIES<br>AND THE HONOURABLE'S<br>ACCOUNT. THE HONOURABLE<br>HAS BEEN INVITED.  |
|     | TOTAL   | 3,540,829                        | ,993                                     |  |   |

### NOTE

| <br> |
|------|
|      |
|      |
|      |
|      |
|      |
|      |

The Constituency and Executive Project Tracking Exercise - Phase 5 report is online at: **www.icpc.gov.ng/downloads** 

Plot 802 Constitution Avenue, Zone A9, Central Business District, PMB 535, Abuja, Nigeria.

Tel: 08076369259, 08076369260

The ICPC is a government agency charged with the mandate to receive and investigate reports of corruption and in appropriate cases prosecute the offender(s), to examine, review and enforce the correction of corruption prone systems and procedures of public bodies, with a view to eliminating corruption in public life, and to educate and enlighten the public on and against corruption and related offences with a view to enlisting and fostering public support for the fight against corruption.

For more information on ICPC: info@icpc.gov.ng or visit www.icpc.gov.ng



### www.icpc.gov.ng
