



# Sustaining Community Development

*through public funded  
projects tracking*



REPORT OF ICPC CONSTITUENCY & EXECUTIVE  
PROJECTS TRACKING EXERCISE - PHASE VI

Report of ICPC Constituency and Executive  
Projects Tracking Exercise - Phase VI

# Sustaining Community Development

through public funded  
projects tracking



**Independent Corrupt Practices and  
Other Related Offences Commission**



HIS EXCELLENCY  
**BOLA AHMED TINUBU** GCFR  
PRESIDENT, COMMANDER-IN-CHIEF  
OF THE ARMED FORCES  
FEDERAL REPUBLIC OF NIGERIA



**DR. MUSA ADAMU ALIYU** SAN  
HON. CHAIRMAN, INDEPENDENT CORRUPT PRACTICES  
AND OTHER RELATED OFFENCES COMMISSION

This report is a product of the Independent Corrupt Practices & Other Related Offences Commission (ICPC). The ICPC is a government agency charged with the mandate to receive and investigate reports of corruption and in appropriate cases prosecute the offender(s); to examine, review and enforce the correction of corruption prone systems and procedures of public bodies, and to educate and enlighten the public on and against corruption and related offences with a view to enlisting and fostering public support for the fight against corruption.

**For inquiries about the report contact:**

ICPC Headquarters  
Plot 802 Constitution Avenue,  
Zone A9, Central Business District,  
PMB 535, Abuja, Nigeria.

+2348076369259, +2348076369260

[info@icpc.gov.ng](mailto:info@icpc.gov.ng)

[www.icpc.gov.ng](http://www.icpc.gov.ng)

    @ICPCNigeria

 0800-CALL-ICPC (0800-2255-4272)

ISBN: 978-978-768-236-4

# Contents

Tables and Figures	_____	vi
Abbreviations	_____	vii
Foreword	_____	viii
Introduction	_____	01
Objectives	_____	02
Project Tracking	_____	02
Phase VI Tracking Exercise	_____	04
Summary of Tracked Projects	_____	06
Highlights of Findings	_____	15
Contractors That Returned to Sites	_____	19
Policy Advisory	_____	34

# Table and Figures

## Tables

- Table 1.1: Appropriations of Tracked Projects
- Table 1.2: Sectorial Distribution of Projects Tracked
- Table 2.1: Distribution of Projects Tracked by States
- Table 2.2: Distribution of Projects Tracked by Geo-Political Zones
- Table 3.1: List of Contractors Compelled to Return to Site

## Figures

- Figure 1.1: Phase VI Tracking Activities
- Figure 1.2: Status of Projects Tracked
- Figure 1.3: Types of Projects Tracked
- Figure 2.1: Budget Highlights of Projects Tracked
- Figure 2.2: Appropriations of Tracked Projects in Chart
- Figure 2.3: Sectors with Higher Number of Projects Tracked in Chart
- Figure 3.1: Distribution of Projects Tracked by States
- Figure 3.2: Distribution of Projects Tracked in Selected States
- Figure 3.3: Top Three States with Highest Number of Tracked Projects
- Figure 3.4: Graphical Distribution of Projects Tracked by Geo-Political Zones

# Abbreviations

BOF	Budget Office of the Federation
BOQ	Bill of Quantity
BPP	Bureau of Public Procurement
CEPTG	Constituency and Executive Projects Tracking Group
CEPTI	Constituency and Executive Projects Tracking Initiative
COPROA	Corrupt Practices and Other Related Offences Act
CSOs	Civil Society Organizations
EFO	Ecological Fund Office
FCT	Federal Capital Territory
HYPPADEC	Hydroelectric Power Producing Areas Development Commission
MDAs	Ministries, Department and Agencies
NDDC	Niger Delta Development Commission
NDE	National Directorate of Employment
NEDC	North East Development Commission
NHIA	National Health Insurance Authority
NIQS	Nigerian Institute of Quantity Surveyors
NSITF	Nigeria Social Insurance Trust Fund
OAGF	Office of the Accountant General of the Federation
OAugF	Office of the Auditor General of the Federation
PAP	Presidential Amnesty Program
QS	Quantity Surveyor
SPV	Special Purpose Vehicle
TETFUND	Tertiary Education Trust Fund



# Foreword

To achieve sustainable development goals, government must invest in infrastructural development of all sectors of the economy as these investments in infrastructure enhances citizens' socio economic well-being and ensures good governance on the nation. Meanwhile, proper implementation of budget in the form of project execution is a necessity for good governance and the delivery of government mandate of providing security and welfare of the citizenry as well as promoting economic growth.

Budget implementation has a symbiosis relationship with project execution as both involves process of putting government planned expenditure and revenue activities into action, and encompasses executing the policies and programs outlined in the budget through the allocation and disbursement of funds to specific government agencies and departments for projects execution.

However, for far too long, fiscal allocations of resources for growth and development of the communities have been distorted, misapplied, misappropriated and this has led to a huge deficit in infrastructural development and increasing poverty level amongst the Nigerian citizens despite abundant resources. As budgetary allocations do not translate to tangible development, the Commission therefore decided to fill in the gap created by the dearth of infrastructure across the nation through the Commission's initiative of the Constituency and Executive Projects Tracking.

The Constituency and Executive Project Tracking Initiative (CEPTI) is an intervention initiative conceived to engender good governance, prevent corruption and enhance transparency and accountability on government funded projects, through the annual analysis national budgets to flag seeming irregularities such as duplicated projects across MDAs, highlighting inserted projects and projects that MDAs do not have the human resources or skill set to execute as well as monitoring budget performance and projects execution to ensure value for money.

The Phase 6 tracking exercise provided another opportunity for the Commission to among others track selected projects across 176 MDAs and ensure adequate and effective project implementation, while enforcing necessary sanctions on various infractions observed during the exercise which spanned from November 2023 to May 2024.

While the exercise was limited to 26 states across the 6 Geo Political Zones, the report of the exercise as presented shows that a total of 1721 government funded projects with total value standing at N284,602,881,868.57 was tracked. The tracking exercise revealed several infractions ranging from project underperformance, non-distribution of empowerment items, project abandonment amongst others.

In the course of the tracking exercise, 163 contractors whose projects execution were found not in compliance with the Bill of Quantities or who had abandoned their projects were compelled to return to project sites, and the value of such projects stood at N30,260,788,929.77. Investigations are still ongoing on some of the infractions detected.

Constituency and Executive Project Tracking Initiative in the last five years has engendered socio economic development of the citizens, and created awareness around government projects for the citizens to demand accountability on the part of their leaders. Besides the enforcement activities which led to recoveries of unearned government funds, a clear message is being sent out that government funds are to be applied strictly to the business of governance. The Commission shall continue to hold MDAs and project facilitators accountable for government funds domiciled under their custody.

**Dr. Musa Adamu Aliyu, SAN**

Chairman, ICPC

July, 2024

# Introduction

The Constituency and Executive Project Tracking Initiative (CEPTI) was conceived by the Commission as an intervention and preventive initiative to, engender good governance through corruption prevention initiatives which include preventing fund mismanagement and enhancing transparency and accountability on government-funded projects.

Proper implementation and execution of government-funded projects facilitate good governance as investments in infrastructure enhance citizens' socio-economic development and attainment of sustainable development goals. In a nutshell, corruption-free project implementation is a necessity for good governance which is essential in the government's delivery of its mandate of security and welfare of its citizens and promoting sustainable development and economic growth.

However, a key factor of the budgeting process is budget implementation which if skewed from the inception, will affect project execution. Budget implementation involves the process of putting a government's planned expenditure and revenue activities into action. This also involves, executing the policies and programs outlined in the budget through the allocation and disbursement of funds to specific government agencies and departments. The implementation of a budget encompasses a range of activities including budget planning, resource mobilization, expenditure, tracking and reporting. These activities and steps are crucial when projects are being tracked across the country as they affect the implementation or non-implementation of projects.

Essentially, budget implementation is a crucial phase of the budgetary process because it is a determinant of whether the government will achieve its budget objectives or not. Proper budget implementation leads to better service delivery, improved infrastructure, and increased economic growth and development; while ineffectual budget implementation results in waste and corruption making the government fall short of its planned objectives.

In order to ensure proper project delivery and value for money, the Commission initiated the Constituency and Executive Project Tracking which aims to bring sanity, integrity and accountability in the execution of public-funded projects. The initiative derives its mandate from Section 6 a-f of the Corrupt Practices and Other Related Offences Act (COPROA), 2000.

For wider acceptance and transparency, the Commission brought together state and non-state actors as stakeholders, to serve as Special Purpose Vehicle (SPV) for driving the initiative. These stakeholders include the Bureau of Public Procurement (BPP), Office of the Accountant General of the Federation (OAGF), Office of the Auditor General of the Federation (OAuGF), Budget Office of the Federation (BOF), Nigerian Institute of Quantity Surveyors (NIQS), Civil Society Organizations (CSOs) and the Media (local and national).

# Objectives

The objectives of the initiative among others are to:

- a) Ensure diligent and satisfactory execution of public-funded projects,
- b) Ensure that the public gets value for every fund expended from the treasury,
- c) Curb abuses, strengthen project delivery process,
- d) Galvanize public awareness and participation in the project delivery chains as well as sanction both criminal and administrative transgressions.



Full execution of  
public projects



Ensure value  
for money



Reduce corruption  
and abuses



Increase public  
participation

# Project Tracking

The focus of this report is on the projects tracked during the Phase VI project tracking exercise covering the Health, Agriculture, Education, Water Resources and Power sectors. The report showcased the tracking activities, the findings, the percentages of projects completed and those that were abandoned.


Preparatory to the tracking exercise, the National Budget for the years 2020, 2021 and 2022 appropriations were analyzed and projects were selected therein. The project selection was restricted to projects within 2020, 2021 and 2022 appropriations. 1000 Executive projects were selected across 26 states. While 80 TETFUND-funded projects were also selected at 4 projects per state in 20 States cutting across Public Universities, Polytechnics and Colleges of Education. Special focus was also placed on projects of some intervention agencies of government such as the North East Development Commission (NEDC), Ecological Fund Office (EFO), Presidential Amnesty Program (PAP), Niger Delta Development Commission (NDDC), Nigeria Social Insurance Trust Fund (NSITF), and National Health Insurance Authority (NHIA).

The total appropriation for the tracked projects amounts to **N219,843,922,945.48** (Two Hundred and Nineteen Billion, Eight Hundred and Forty-Three Million, Nine Hundred and Twenty-Two Thousand, Nine Hundred and Forty-Five Naira, Forty-Eight Kobo). The selected projects cut across 176 Ministries, Departments and Agencies.

The Phase VI tracking exercise took place in 26 focal states and the FCT across the 6 Geopolitical Zones: **North Central:** Nasarawa, Niger, Benue, Kwara, Kogi, Plateau and the FCT; **North East:** Adamawa, Borno, Bauchi, Gombe, Taraba and Yobe; **North West:** Kano, Katsina, Kebbi and Sokoto; **South East:** Anambra, Enugu, Ebonyi and Imo; **South-South:** Akwa Ibom, Bayelsa, and Edo; **South West:** Ekiti, Lagos, and Ondo States.



*Tracked the provision of solar-powered borehole in Funtua Local Government Area of Katsina State*

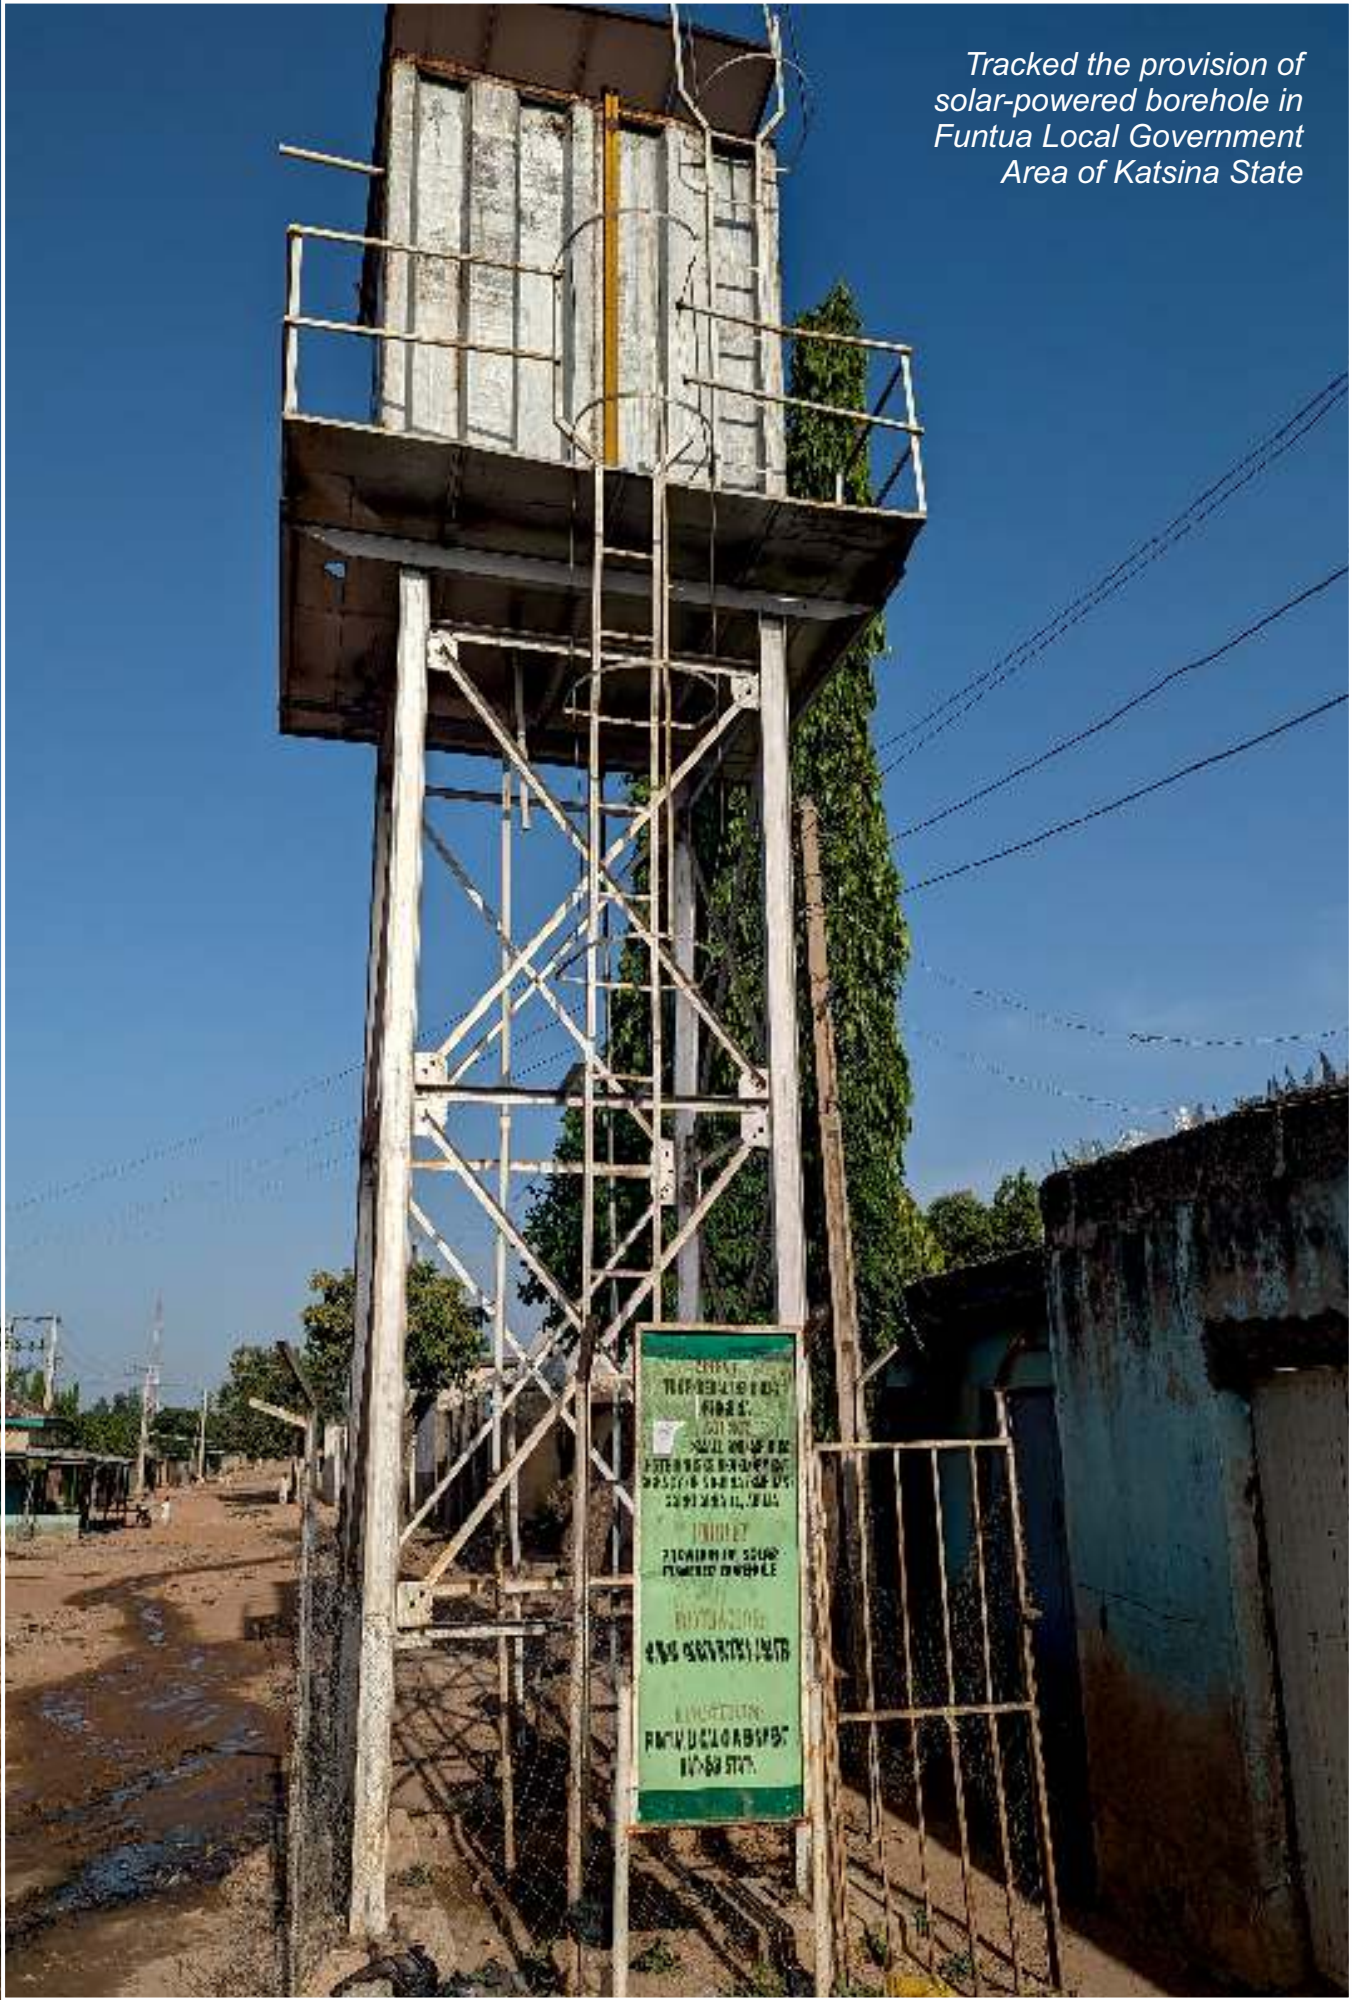

# Phase VI Tracking Exercise

## Parameters and Outcomes

As usual, the National Budgets for the years under focus are obtained for analysis in conjunction with the CEPTI Steering Committee. The Committee selects projects to be tracked and investigated based on the established parameters. The Commission deploys its officers to lead other members of the tracking teams which include, Quantity Surveyors nominated by the NIQS, CSOs and the media, to the sites of each of the selected projects.

Parameters for selection and tracking include the following: a) National spread, b) Monetary value of the project, and c) Intended and potential benefits of the project to the local communities. The CEPTI's focus is essentially on those sectors that have the most beneficial impact on the most vulnerable members of our societies such as education, agriculture, potable water, healthcare, power, rural infrastructures and now “empowerment”.

While it is the remit of the officers of the Commission on the team to handle all the investigative activities, the QS provides the professional valuation of the projects in terms of quality and quantities and advises on cost inflation, the CSOs on each team monitor the transparency of the tracking processes and give feedback to the communities on projects tracked while the media give the entire processes the needed publicity which help to galvanize the public interests, create the much-needed awareness and ensure the participation of the benefitting communities towards achieving the objectives of the initiative.

At the end of the field tracking exercise, different issues pertaining to shoddy execution, non-execution or partial execution of projects were discovered. These discoveries necessitated the Commission to amongst others direct further investigations on issues uncovered, resulting in the recovery of cash and assets; compelling contractors back to sites to remedy shoddily executed projects; and to enforce the distribution of hoarded items to the intended beneficiaries.

Furthermore, the Commission issued policy advisories to guide concerned agencies on project implementation; and policy directives to agencies on administrative sanctions of their staff found to have colluded with either the contractors or the project facilitators. The CEPTI also recommended some cases for prosecutions pertaining to project mismanagement or non-execution. These cases are already being prosecuted in various courts of law.

These CEPTI undertakings have resulted in the public obtaining benefits in terms of socio-economic development, having the needed infrastructural projects meant for them and value for money for every public fund spent.

---

***“...discoveries necessitated the Commission to amongst others direct further investigations on issues uncovered, resulting in the recovery of cash and assets; compelling contractors back to sites to remedy shoddily executed projects; and to enforce the distribution of hoarded items to the intended beneficiaries.”***






*Contractor compelled to return to site to remedy a failed borehole in a community in Yobe State.*



# Summary of Tracked Projects


Figure 1.1: Phase VI Tracking Activities

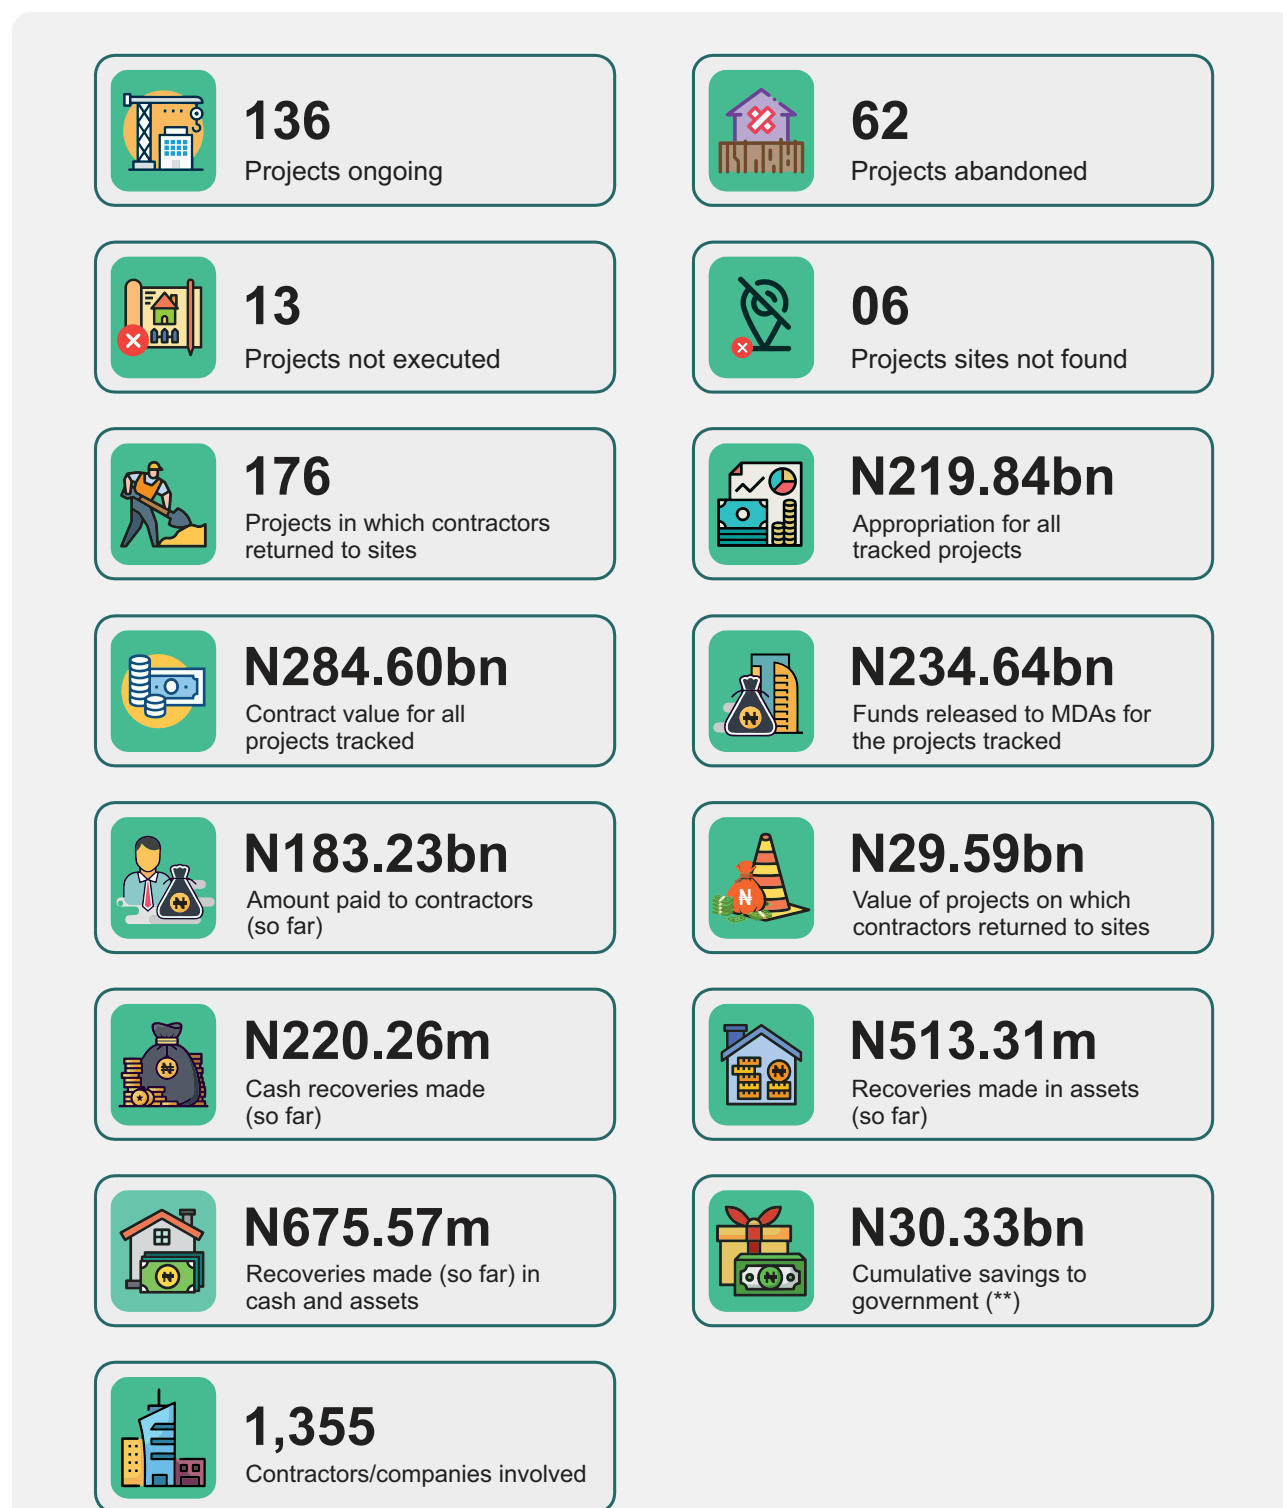


## Notes

\*\* Cumulative savings for the Government is the sum total of our recoveries and the estimated value of those projects on which contractors were compelled back to sites as a result of the CEPTG activities. These amounts were computed as savings for the Government. These are monies that would have been lost/misappropriated save for the Commission's intervention. The valuation Reports being awaited from the assigned QS will provide a definite value when received.

**Figure 1.2: Status of Projects Tracked**

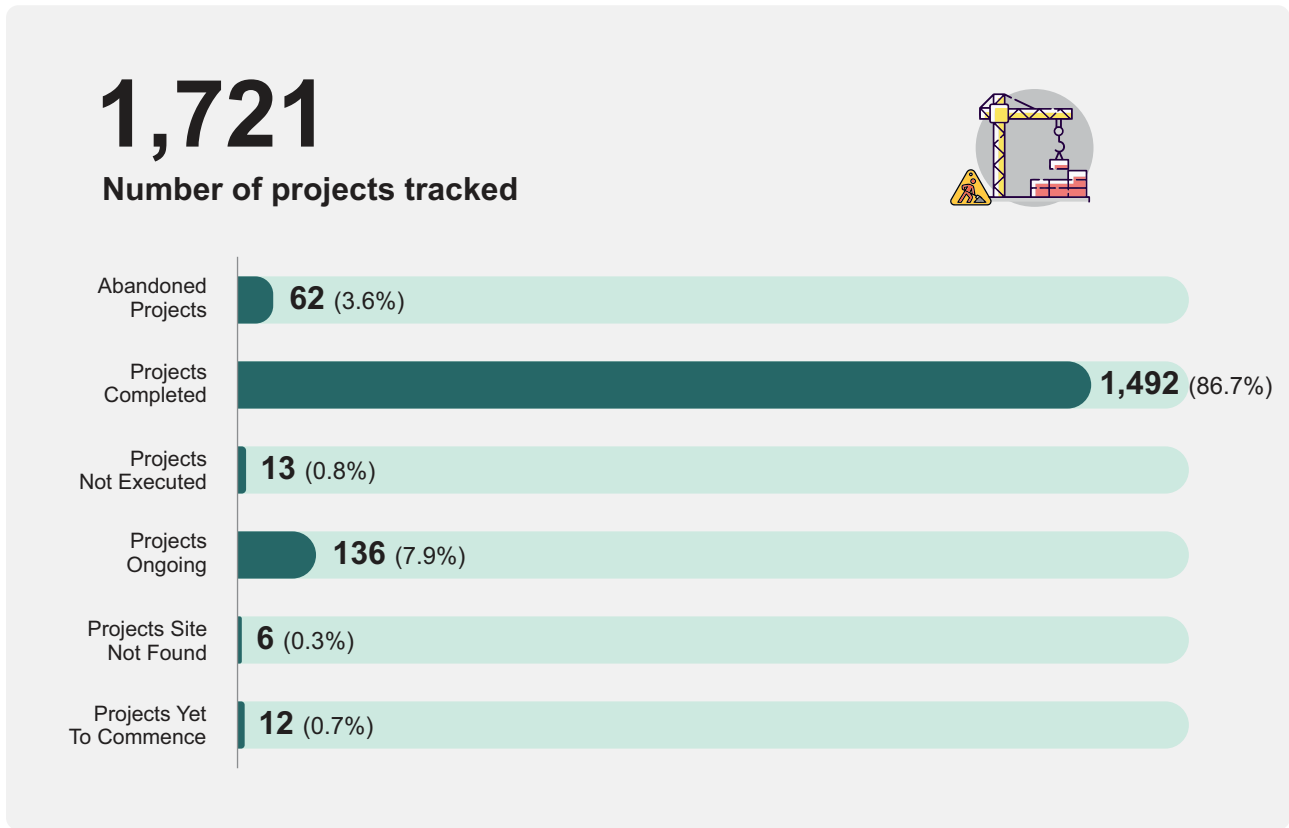

**Figure 1.3: Types of Projects Tracked**

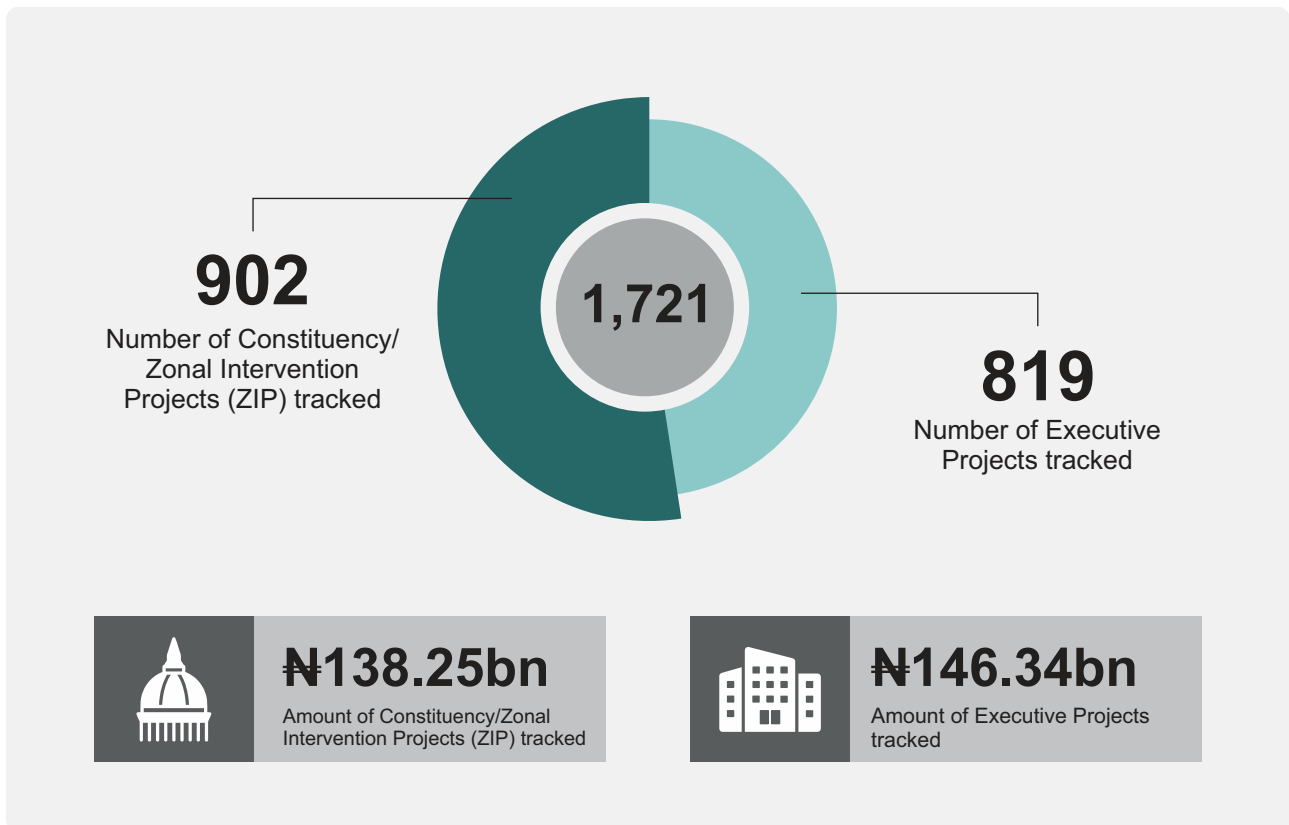






*Tracked the construction and equipping of a Primary Healthcare Centre in Tafashiya, Kankia Local Government Area of Katsina State*




**Figure 2.1: Budget Highlights of all Tracked Projects**

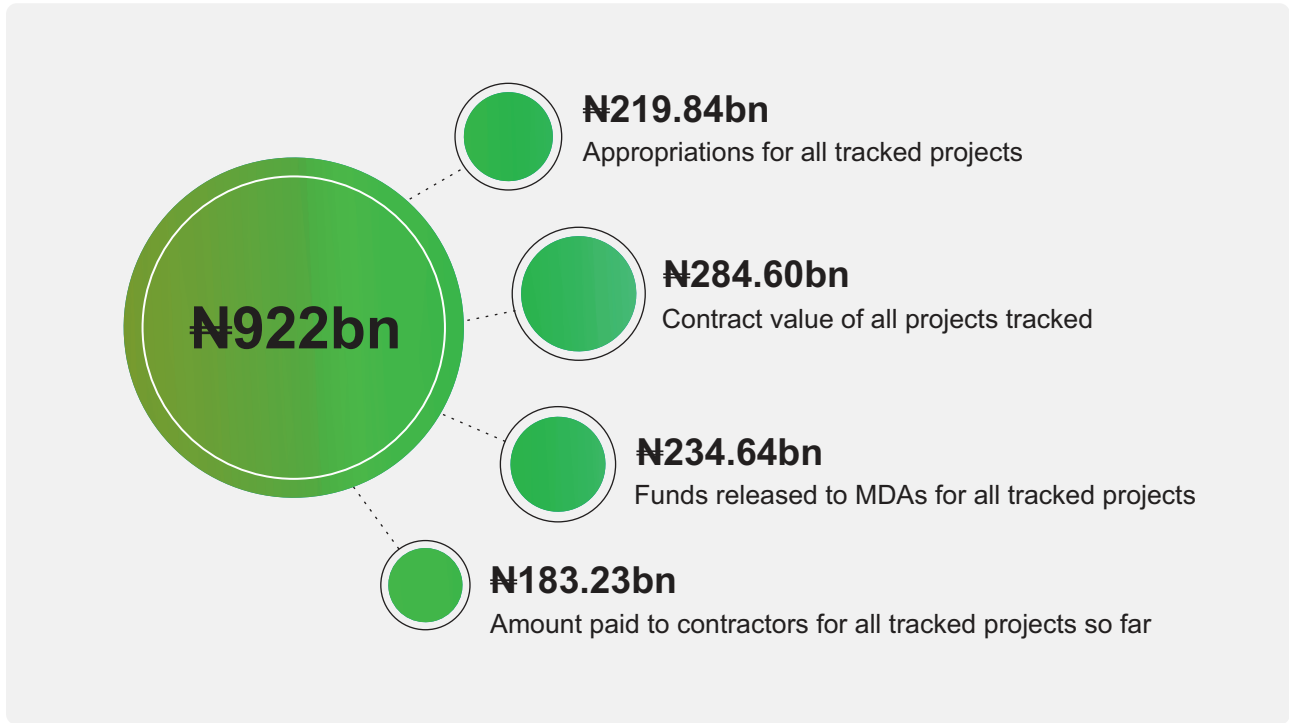

**Table 1.1: Appropriations of Tracked Projects**

Year	Amount	Percentage
2020	N19,548,779,110.38	9%
2021	N92,719,470,751.24	42%
2022	N107,575,673,083.86	49%
<b>Total</b>	<b>N219,843,922,945.48</b>	


**Figure 2.2: Appropriations of Tracked Projects in Chart**

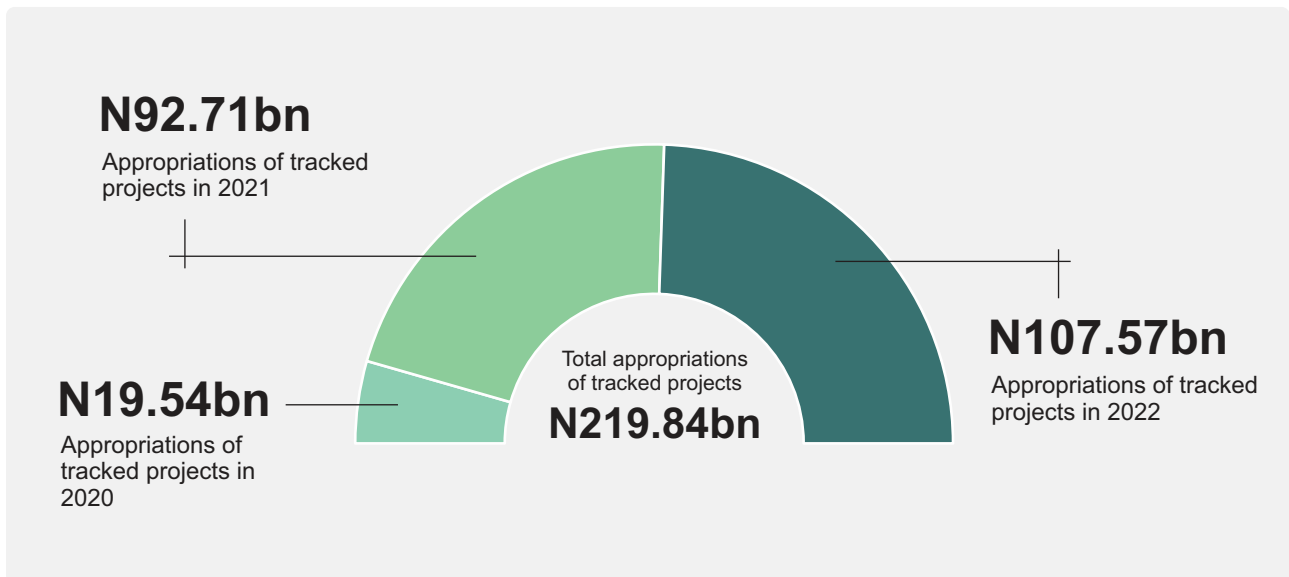


**Table 1.2:** Sectorial Distribution of Projects Tracked

MDA	Contract Value	No. of Projects	% of No. of Projects by Sectors
Empowerment	N35.58bn	449	26.1%
Education	N35.77bn	335	19.5%
Power	N17.60bn	227	13.2%
Road Infrastructure	N91.20bn	173	10.1%
Healthcare	N29.02bn	161	9.4%
Agriculture	N9.25bn	109	6.3%
Housing	N30.61bn	72	4.2%
Water	N6.52bn	72	4.2%
Env. & Natural Res.	N20.78bn	32	1.9%
Trade & Investment	N2.54bn	29	1.7%
ICT	N889.44m	21	1.2%
Transportation	N932.16m	10	0.6%
Law Enf./Security	N638.34m	7	0.4%
Solid Minerals	N710.14m	7	0.4%
Science & Tech	N483.11m	5	0.3%
Sport Recreation	N831.28m	5	0.3%
Art & Culture	N415.26m	4	0.2%
Infrastructure/Equip.	N773.76m	3	0.2%

**Figure 2.3:** Sectors with Higher Number of Projects Tracked in Chart

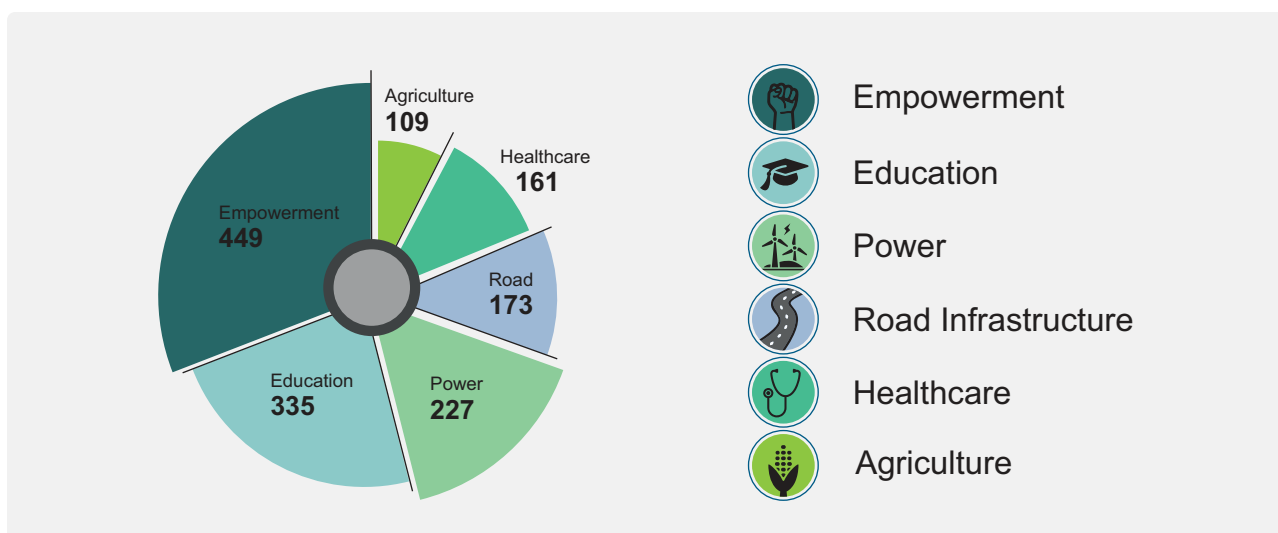


**Figure 3.1: Distribution of Projects Tracked by States**

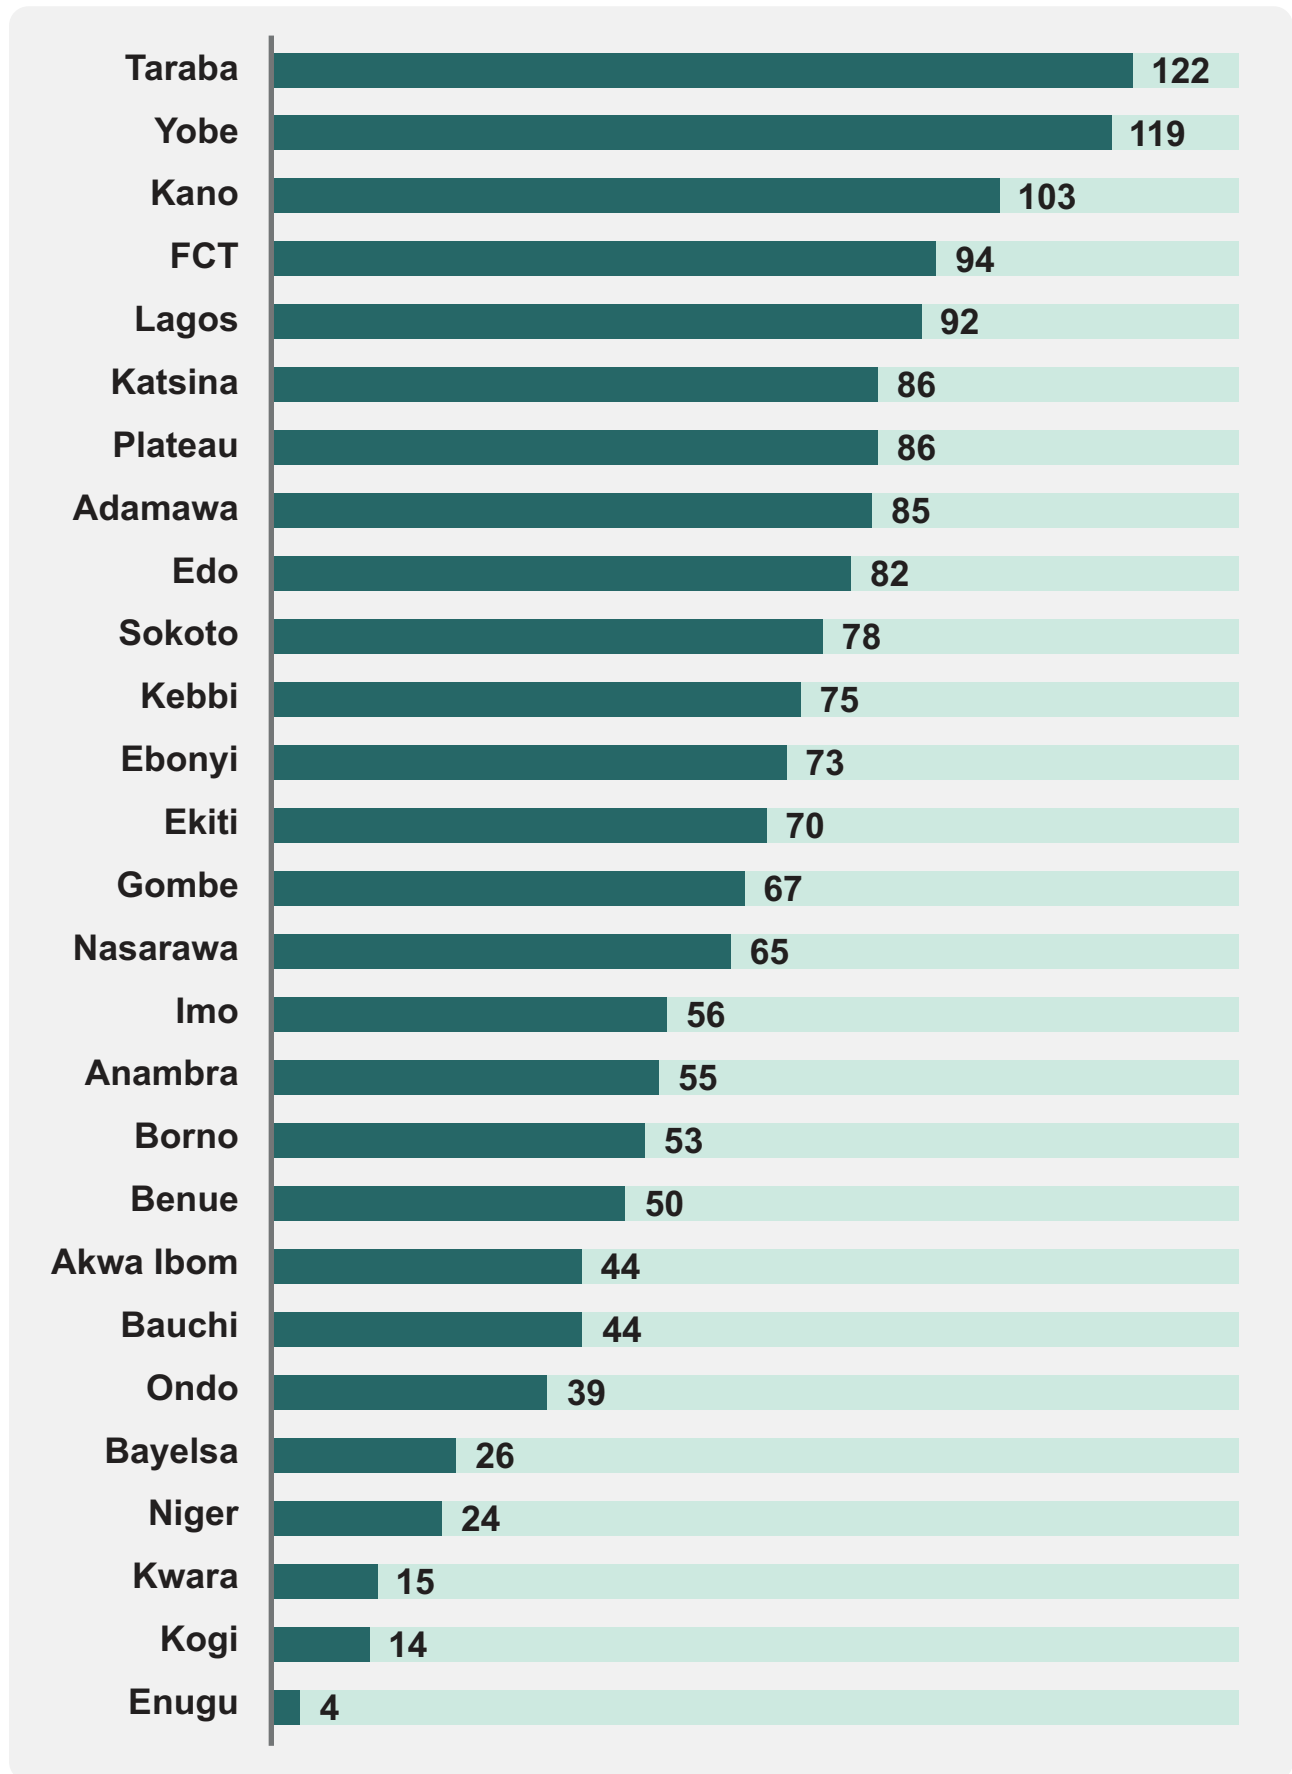





**Figure 3.2:** Distribution of Projects Tracked in Selected States

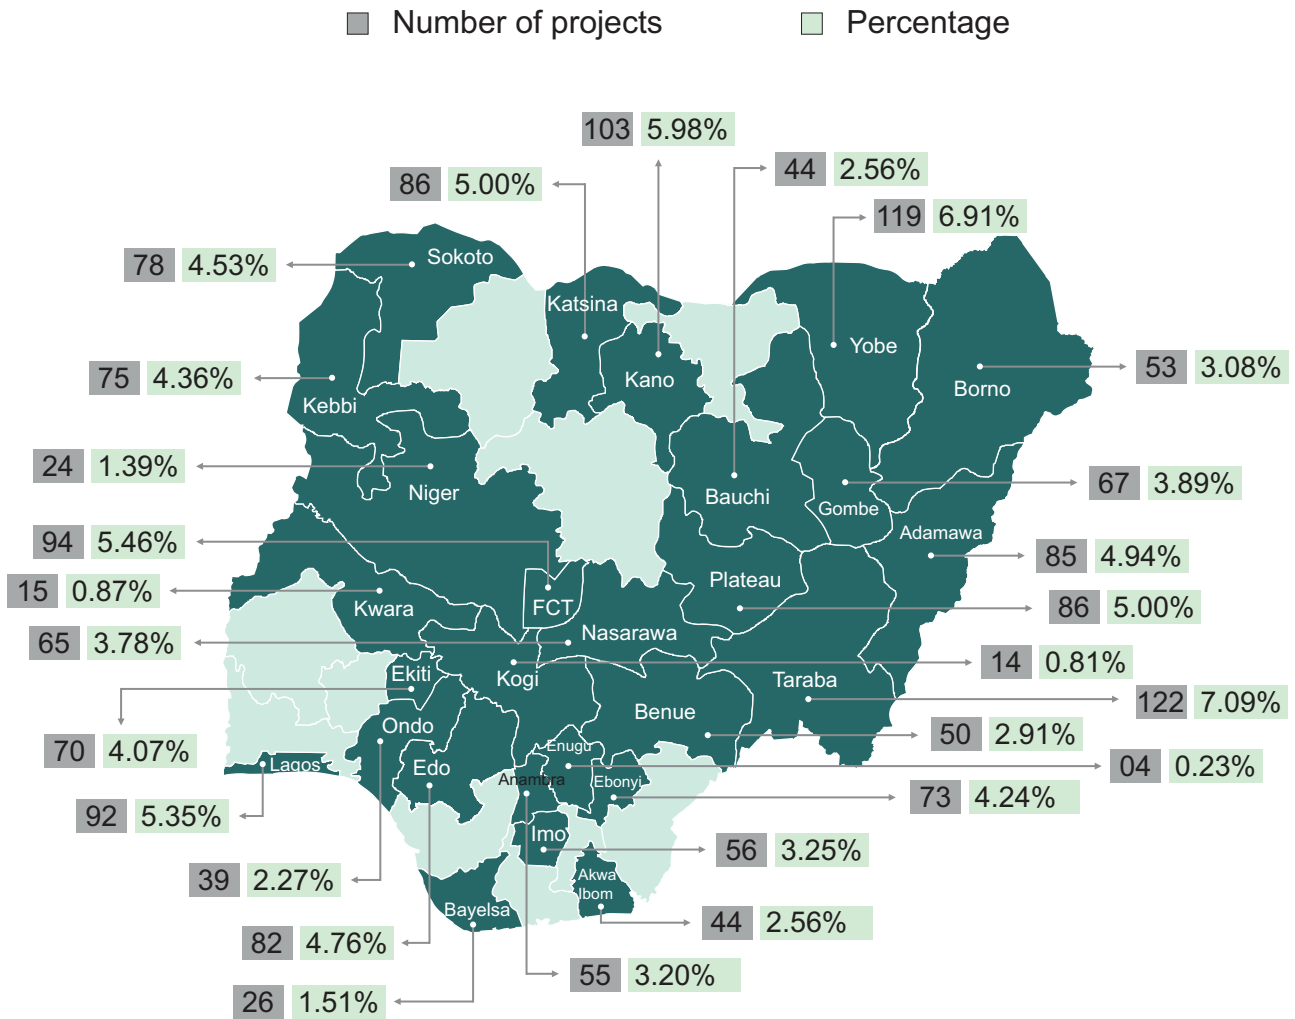

**Figure 3.3:** Top Three States with Highest Number of Tracked Projects

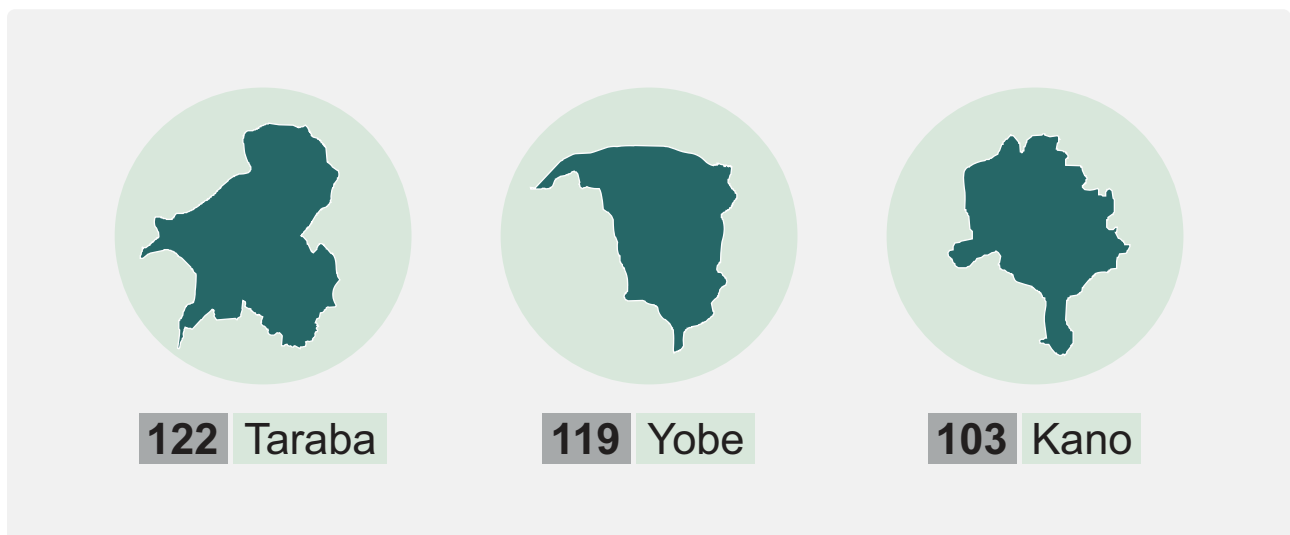

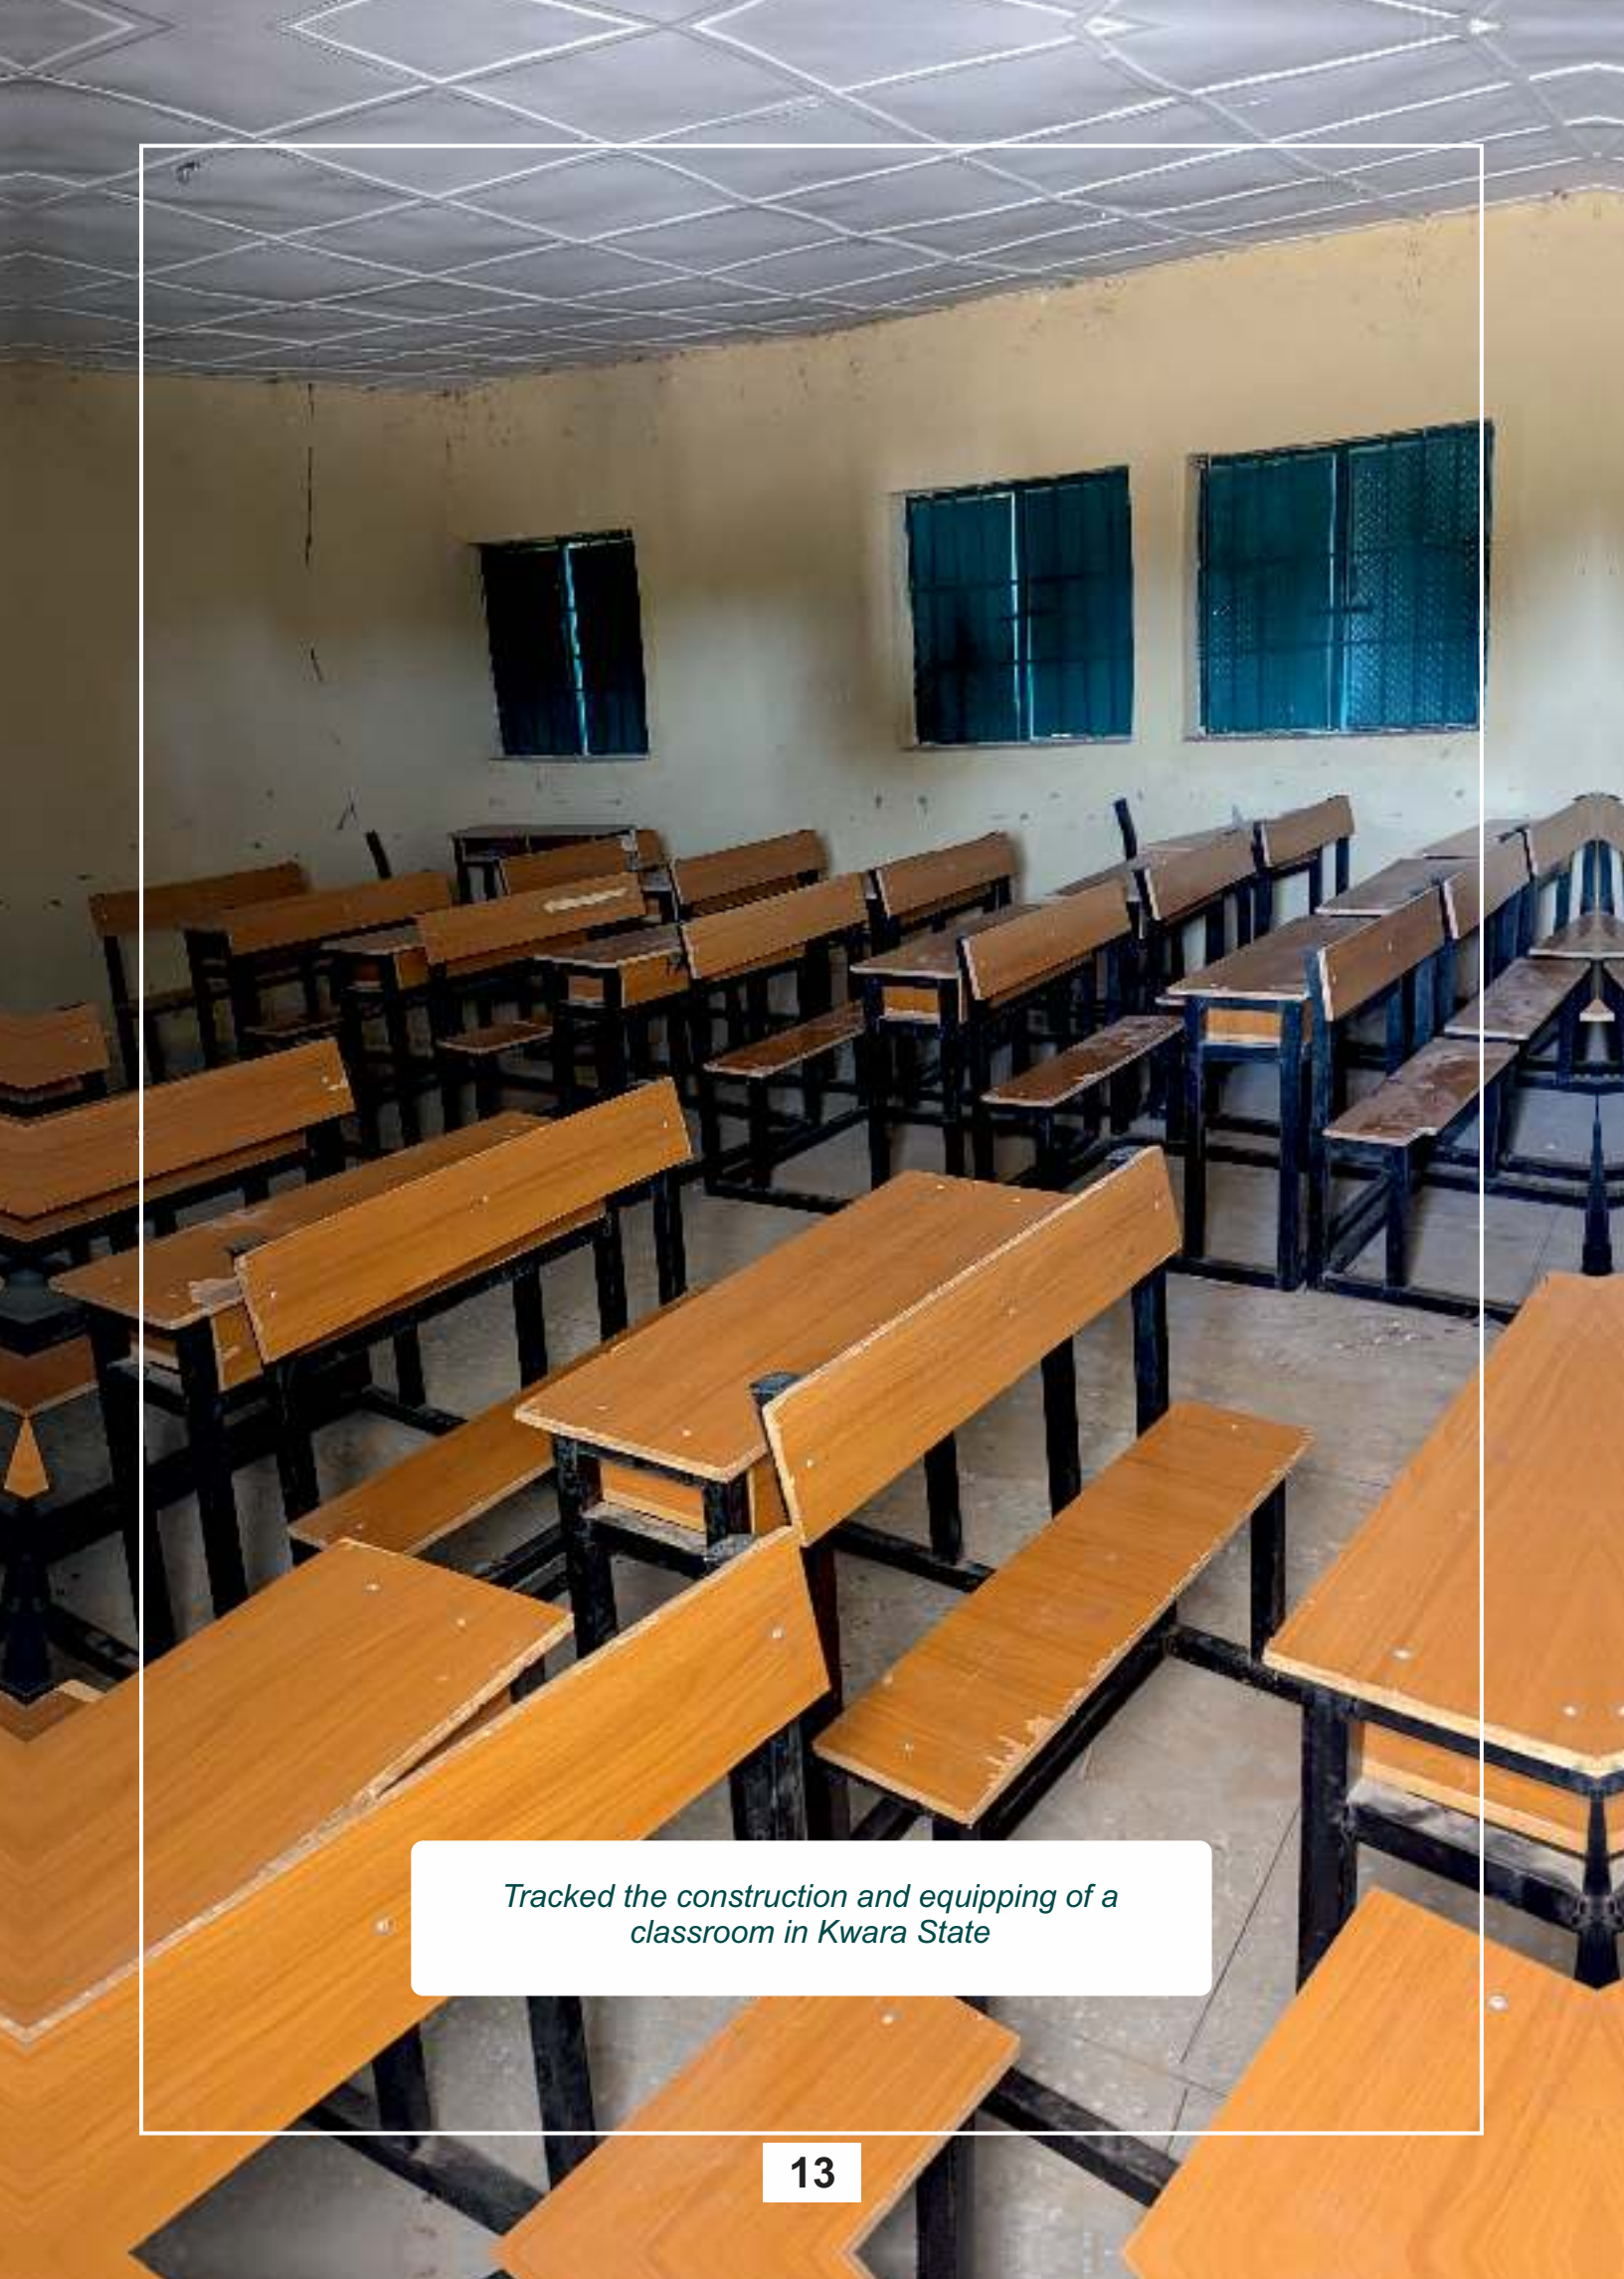


*Tracked the construction and equipping of a classroom in Kwara State*

**Table 2.1:** Distribution of Projects Tracked by Geo-Political Zones

Zone	No. of Projects	Percentage
South East (SE)	188	10.92%
South South (SS)	152	8.83%
South West (SW)	201	11.68%
North East (NE)	490	28.47%
North West (NW)	342	19.87%
North Central (NC)	348	20.22%
<b>Total</b>	<b>1,721</b>	

**Figure 3.4:** Graphical Distribution of Projects Tracked by Geo-Political Zones

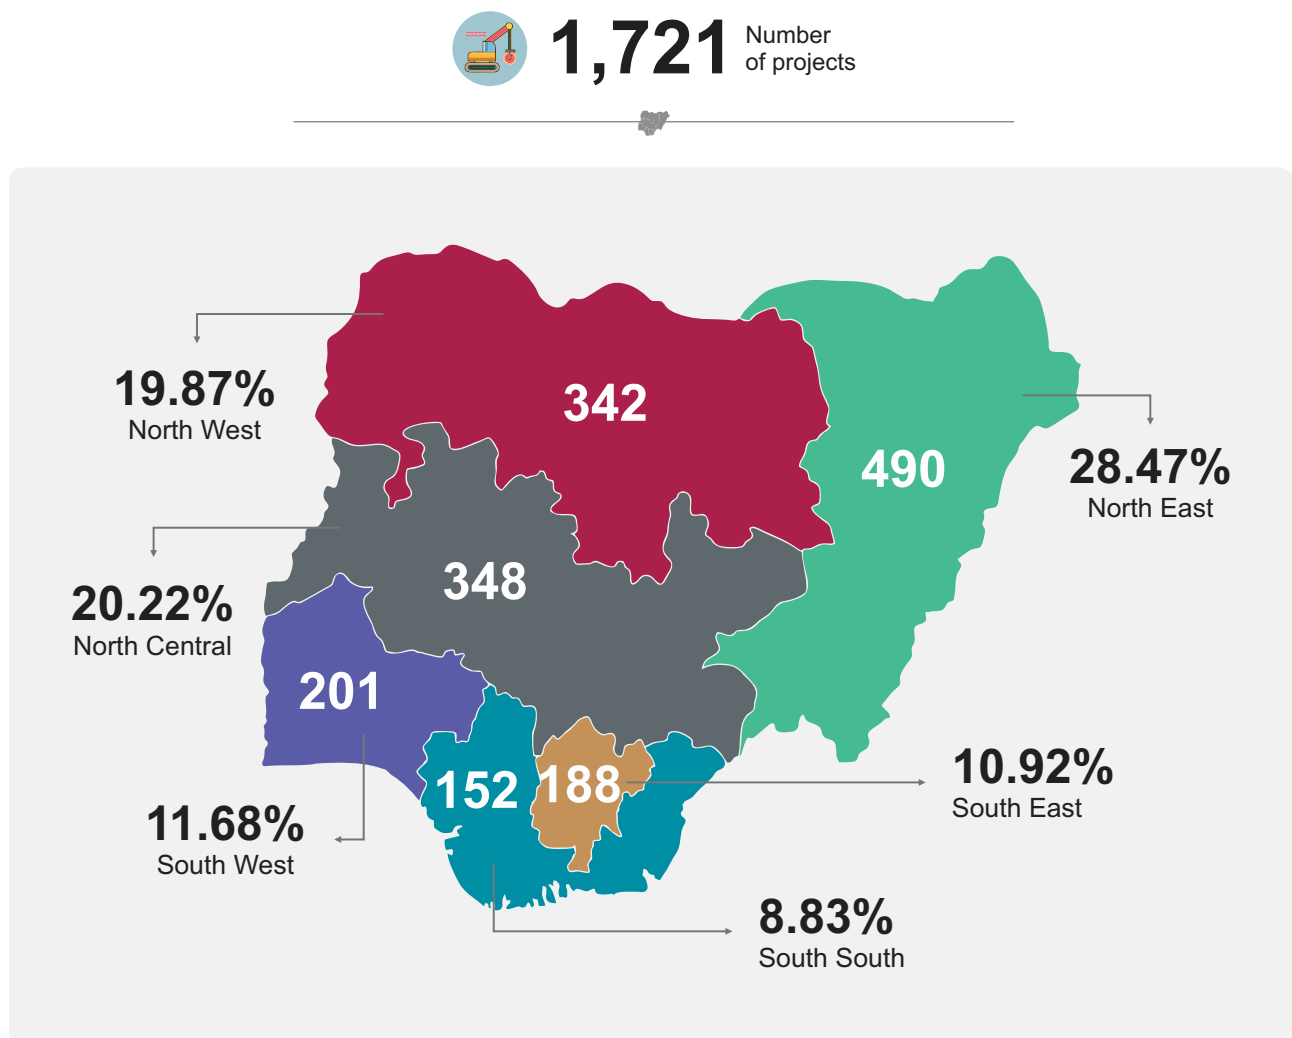

# Highlights of Findings

A total of 1721 government-funded projects were tracked within the Phase VI tracking cycle in five focal sectors, including projects from six (6) intervention agencies (North East Development Commission (NEDC), Ecological Fund Office (EFO), Presidential Amnesty Program (PAP), Niger Delta Development Commission (NDDC), Nigeria Social Insurance Trust Fund (NSITF), and National Health Insurance Authority (NHIA).

For efficient and cutting-edge tracking exercises, the tracking teams were made to go through some tailor-made capacity-building trainings before deployment to the field, while on the field Body Cams were deployed for use by the teams for enhanced control and monitoring in addition to the deployment of the KoboToolBox application for data capturing and analysis.


The number of projects completed under this phase was higher (1,492 projects amounting to 86.7%), although findings in terms of connivance between staff of MDAs and contractors are a lot similar to the findings highlighted in the previously published reports. Some of the findings during the Phase VI exercise are highlighted below. These infractions were found perpetrated by project facilitators or contractors in collaboration with some staff of executing agencies.

1. Non-Distribution of Empowerment Items: empowerment items are meant to be distributed to intended beneficiaries to empower them or to serve as poverty alleviation items. These items were procured but hoarded by the project facilitators possibly for electoral campaign activities.
2. Sharing of empowerment items through proxies. It was observed that some agencies particularly were in the habit of handing over empowerment items to stakeholders for onward distribution to the intended beneficiaries. This practice has encouraged hoarding and politicization of the empowerment-sharing processes, especially within NEDC and HYPPADEC.
3. We found in NEDC centralisation of store records and administrative bottleneck which has led to delay and expiration of the stored items before distribution and also leading to wastage of government funds.
4. NEDC, NDE and EPO make use of consultants without adequate manpower and competence to supervise projects. It is observed that agencies are employing the use of consultants without requisite capacities for project supervision thereby leading to the delivery of poor-quality projects.
5. Under-performance and non-adherence to specification in project execution. This has been observed in numerous projects that were tracked, and formed the basis for fund recoveries from some contractors and also are the basis on which some contractors were compelled to return to project sites to complete abandoned projects or to remedy shoddily executed projects.





*Tracked projects for erosion & flood control in Ado-Ekiti, Ekiti South-West, and Ilejemeje Local Government Areas of Ekiti State*

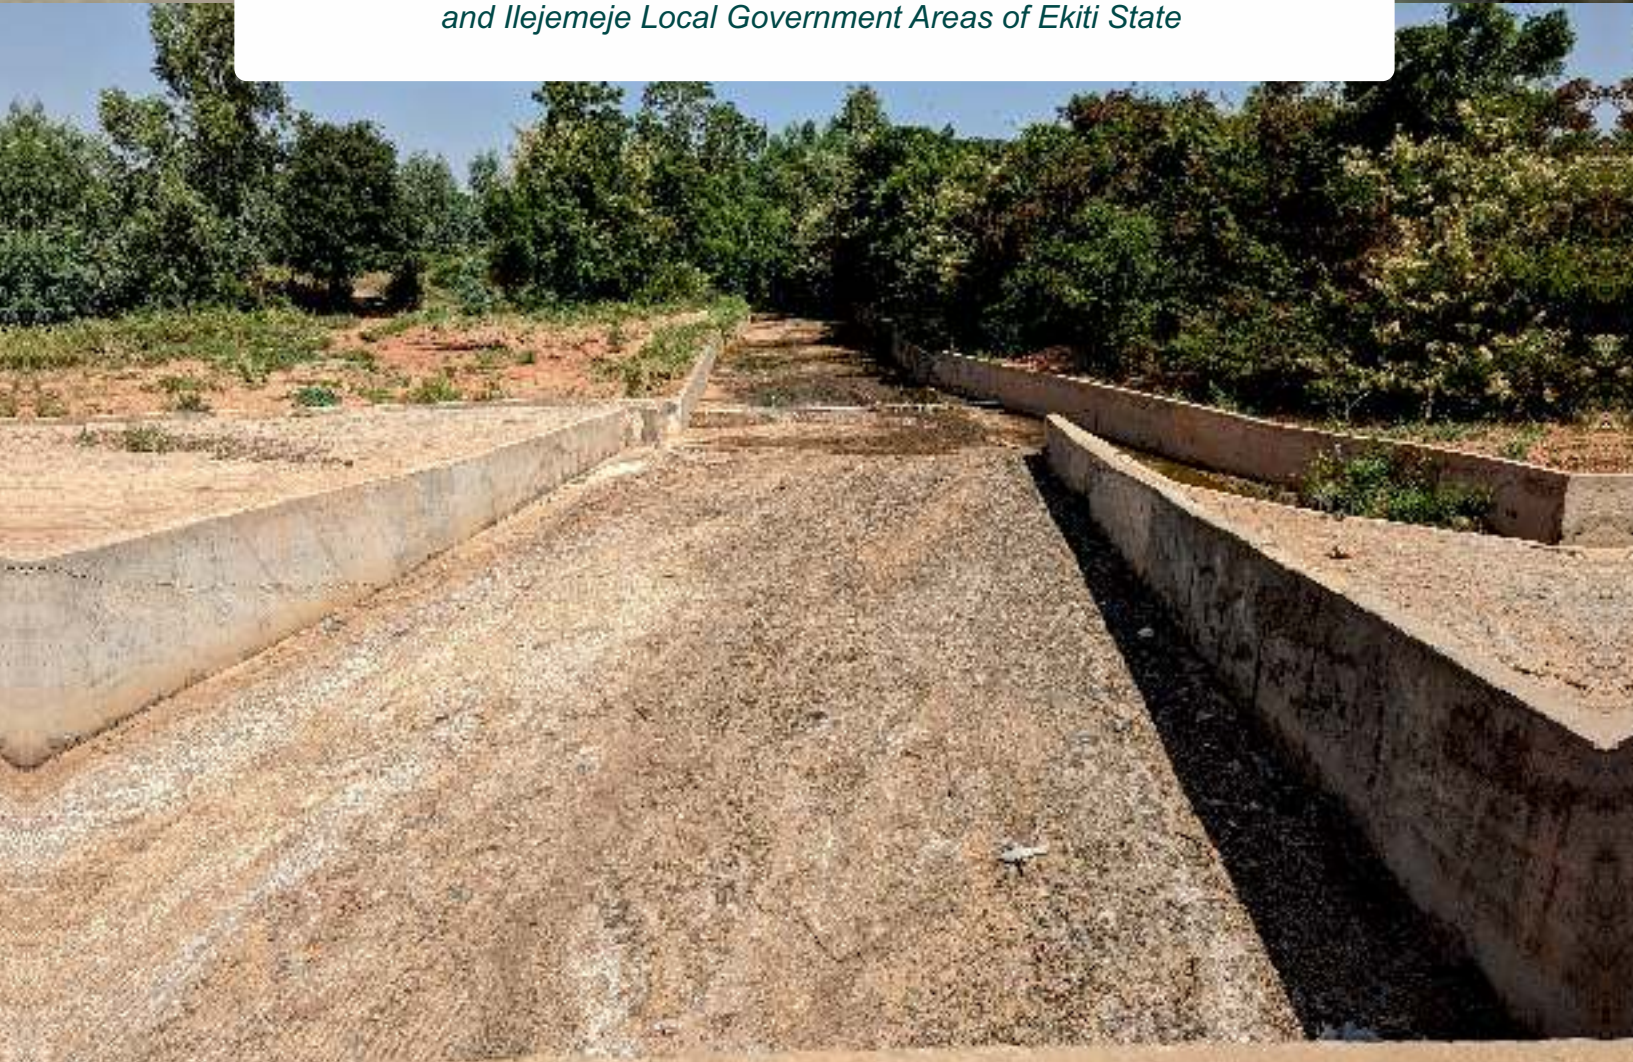



6. Store officers issuing Store Receipt Vouchers (SRV) for supply contracts without actual receipt of the supply items into stores. With regard to empowerment items it was discovered that some store officers connived with contractors by issuing SRV even when there was no supply of items to the store.
7. Non-occupation and utilisation of completed projects. It is observed that some completed projects are not put to use by the supposed benefiting institutions and communities thereby raising questions on the need for such infrastructure. One example of such is the TETFUND projects in Federal University, Gashua, completed but not utilized and cattle market in Soro, Bauchi State executed by NEDC.
8. Abuse of the selective tendering process. Most intervention agencies appeared to be using only selective tendering processes under the guise of 'emergency' in their procurement process. This practice if not checked, will stifle competition, engender favouritism and lack of value for money in project implementation.
9. Non-completion of projects and poor funding of initiated projects thereby leading to project abandonment and request for project variation.
10. Large-scale soft/fluid projects and empowerment projects as major conduits for syphoning public resources: Empowerment/soft projects deserve special attention in this report in view of their increasing propensity within the budget as more project sponsors now prefer to embed such projects for execution in the budget. In the course of Phase VI project tracking, it was discovered that the aggregate number of empowerment projects tracked amounts to 449 empowerment projects (26.1% of the total tracked projects), while the aggregate sum/value of contract award on empowerment projects is N35,585,340,728.91. In all the shenanigans found in the course of tracking empowerment projects, contractors, project facilitators as well as the executing agencies staff cannot be excused of gross connivance. Meanwhile, the Commission has since enforced the distribution of the recovered items to the beneficiaries.
11. Meanwhile, to stem the tide of empowerment items being converted to personal use or for personal aggrandisement, pre-execution tracking is most ideal to engender value for money on government funds as well as for impactful socio-economic development of the citizenry. In view of the Commission's advocacy and advisories to MDAs, relevant MDAs have started inviting the Commission to monitor the distribution of empowerment items on their budget.
12. Other highlights of issues found in the tracked construction/Physical projects of NEDC include:
  - i. Under-priced Bill of Quantity for the 500 Mass Housing Scheme in the North Eastern States.
  - ii. High number of abandoned and incomplete projects were found across all states tracked.



- iii. Absence of a Housing Scheme Layout for the site of the Mass Housing Project. The following were identified by the tracking team in Bauchi at the time of the tracking exercise:
- a. That the houses were sited without consideration of the estate road network.
  - b. That no channels were created for the passage of groundwater.
  - c. Completed houses at the sites of the Mass Housing Projects were found unoccupied.
  - d. Ineffective monitoring of projects by the consultants contracted to supervise its projects in the North Eastern States. Each state, had one consultant supervising the entire projects of the state which was seen in the poor quality of projects tracked to be inadequate.
13. Other forms of infraction discovered during the exercise include but not limited to the following:
- i. Under-performance on project execution: Under performance of projects still remains one of the greatest challenges in the execution of Zonal Intervention Projects:
  - ii. Generally poor and substandard execution of projects,
  - iii. Cost padding, etc.





# Contractors That Returned to Sites

**Table 3.1:** List of Contractors Compelled to Return to Sites

S/N	PROJECT DESCRIPTION	CONTRACT SUM (₦)	NAME OF CONTRACTOR	REASON FOR GOING BACK TO SITE	STATUS/REMARK
1	CONTRACT FOR THE REHABILITATION OF ROADS IN ALIMOSHO FEDERAL CONSTITUENCY, LAGOS STATE	165,215,220.35	JOTAFAB RESOURCES LIMITED	THE REPAIR OF THE EXISTING DRAINAGE DID NOT COVER THE NUMBER OF METRES PROVIDED IN THE BOQ.	ONGOING
2	CONTRACT FOR THE SUPPLY AND INSTALLATION OF 8-PERSON CAPACITY ELEVATOR FOR THE NEWLY BUILT PCN LAGOS ZONAL OFFICE	63,013,666.25	SAUKI GROUP OF COMPANIES LIMITED	THE ELEVATOR WAS NOT FUNCTIONING. THE CONTRACTOR WAS COMPELLED TO REPAIR IT.	COMPLETED
3	CONSTRUCTION OF A 2KM ACCESS ROAD FOR LOCAL FARMERS AND ITS FARM IN OJO, LAGOS STATE	62,700,000.00	PECABRY CONSTRUCTIONS LTD	SEVERAL FAILED PORTIONS ON THE ROAD	ONGOING
4	PROVISION AND INSTALLATION AND INSTALLATION OF SOLAR STREET LIGHT IN DALA FEDERAL CONSTITUENCY, KANO STATE	99,880,460.00	MESSRS HOUSTAN INTERNATIONAL LTD	MANY OF THE STREETLIGHTS. WERE NOT FUNCTIONING	COMPLETED
5	CONSTRUCTION OF MALE AND FEMALE WARDS AT TUDUN WADA DANKADAI GENERAL HOSPITAL, KANO STATE	49,673,163.76	DANEJO NIG. LTD	ELECTRICAL AND PLUMBING ITEMS NOT FIXED	COMPLETED
6	RENOVATION OF PRIMARY HEALTH ENTRE AT RIRIWAI IN DOGUWA LOCAL GOVERNMENT OF KANO STATE	43,216,660.04	SAMEMA INVESTMENT LTD	MOST ITEMS WERE NOT PROVIDED AS CAPTURED IN THE BOQ	COMPLETED
7	CONSTRUCTION OF 2NOS. MINI BRIDGES ON JELI AND ANGUWAN MADAKI RURAL ACCESS ROADS OF TUDUN WADA LOCAL GOVERNMENT AREA OF KANO MOTORIZED BOREHOLES IN KANO MUNICIPAL.	246,928,859.17	S. TABAWA NIGERIA LTD	THERE IS NO STONE PITCHING TO PROTECT THE CONSTRUCTION.	ONGOING
8	CONSTRUCTION OF CLASSROOMS WITH FURNITURE IN GUZAWA/GABASAWA FEDERAL CONSTITUENCY, KANO STATE	35,000,000.00	MUFSAA FURNITURE LTD	THE ROOF WAS LEAKING ROOF, THE CLASSROOMS WERE NOT PAINTED, AND FURNITURE WERE NOT PROVIDED.	COMPLETED
9	CONTRACT FOR CONSTRUCTION AND INSTALLATION OF 28NOS SOLAR STREETLIGHT IN GEZAWA/GABASAWA FED. CONSTITUENCY, KANO STATE	12,294,721.32	ENGINEERING AFORTH DIMENSION LTD	TO RELABEL AND NUMBER THE STREETLIGHTS, AND ALSO TO CORRECT UNFUNCTIONED STREETLIGHTS.	NOT YET COMPLETED
10	CONTRACT FOR CONSTRUCTION AND INSTALLATION OF 28NOS SOLAR STREETLIGHT IN GEZAWA/GABASAWA FED. CONSTITUENCY, KANO STATE	12,294,721.32	BJAY GLOBAL RESOURCES LTD	TO RELABEL AND NUMBER THE STREETLIGHTS, AND REPAIR THE MALFUNCTIONING STREETLIGHTS.	NOT YET COMPLETED

S/N	PROJECT DESCRIPTION	CONTRACT SUM (N)	NAME OF CONTRACTOR	REASON FOR GOING BACK TO SITE	STATUS/REMARK
11	CONTRACT FOR CONSTRUCTION AND INSTALLATION OF 28NOS SOLAR STREETLIGHT IN GEZAWA/GABASAWA FED. CONSTITUENCY, KANO STATE	12,294,721.32	GENTRAX VENTURES LTD	TO RELABEL AND NUMBER THE STREETLIGHTS, AND REPAIR THE MALFUNCTIONING STREETLIGHTS	ONGOING
12	CONTRACT FOR CONSTRUCTION AND INSTALLATION OF 28NOS SOLAR STREETLIGHT IN GEZAWA/GABASAWA FED. CONSTITUENCY, KANO STATE	12,294,721.32	HABMIN GLOBAL RESOURCE LTD	STREETLIGHT NOT FUNCTIONING.	ONGOING
13	CONTRACT FOR CONSTRUCTION AND INSTALLATION OF 28NOS SOLAR STREETLIGHT IN GEZAWA/GABASAWA FED. CONSTITUENCY, KANO STATE	12,294,721.32	HOPE GROUP LTD	THE STREETLIGHTS, NOT FUNCTIONING	COMPLETED
14	CONTRACT FOR CONSTRUCTION AND INSTALLATION OF 343NOS SOLAR STREETLIGHT IN GEZAWA/GABASAWA FED. CONSTITUENCY, KANO STATE	150,610,336.17	GALAXY GLOBAL CRYSTALS NIG. LTD	STREETLIGHTS NOT WORKING.	COMPLETED
15	SUPPLY & INSTALLATION OF KIDNEY TRANSPLANT EQUIPMENT	249,407,170.54	CANVY INTEGRATED SOLUTIONS LTD.	TO CONDUCT THE NECESSARY TRAINING AS CAPTURED IN THE BOQ	ONGOING
16	CONTRACT FOR THE CONSTRUCTION OF CLASSROOMS AND FURNITURE IN GARO MARIRI AND TRANSFORMERS IN UNGUWAR KWARI CHIRANCHI IN KUMBOTSO LGA, KANO STATE	49,500,000.00	MESSRS A.D.A. INTEGRATED SERVICES LIMITED	THE CLASSROOMS WERE LEAKING	ONGOING
17	CONTRACT FOR THE CONSTRUCTION OF FIVE (5) BLOCKS (76-80) OF FOUR (4) UNITS OF TWO (2) BEDROOM HOUSES IN GOMBE STATE	110,486,957.55	SHANUMA NIGERIA LIMITED	DEFECTS ON THE CONSTRUCTION	COMPLETED
18	CONTRACT FOR THE PROVISION OF BOREHOLES	93,100,000	HOUSTAN INT'L LTD	THREE OUT OF FIVE BOREHOLES WERE NOT FUNCTIONING.	ONGOING
19	CONTRACT FOR THE CONSTRUCTION OF FIVE (5) BLOCKS (21-25) OF FOUR (4) UNITS OF TWO (2) BEDROOMS HOUSES IN GOMBE STATE	165,215,220.35	AUTONORTHS LIMITED	THE PROJECT WAS ABANDONED	ONGOING
20	CONTRACT FOR THE DRILLING OF 6" DIAMETER (350M) API BOREHOLE WITH SOLAR HYBRID ACCESSORIES, CONSTRUCTION OF OVERHEAD TANK AND PROVISION OF WATER POINTS ON CONCRETE SLAB IN AKKO LGA, GOMBE STATE	39,391,222	BAKORI BUSINESS MODEL LIMITED	THE BOREHOLE WAS NOT FUNCTIONAL.	COMPLETED
21	CONTRACT FOR THE CONSTRUCTION OF FIVE (5) BLOCKS (111-115) OF FOUR (4) UNITS OF TWO (2) BEDROOMS HOUSES IN GOMBE STATE	62,700,000.00	BAYSLINE NIGERIA	SEVERAL FAILED PORTIONS NOTICED ON THE ROAD	ONGOING

S/N	PROJECT DESCRIPTION	CONTRACT SUM (N)	NAME OF CONTRACTOR	REASON FOR GOING BACK TO SITE	STATUS/REMARK
22	CONTRACT FOR THE CONSTRUCTION OF FIVE (5) BLOCKS (116-120) OF FOUR (4) UNITS OF TWO (2) BEDROOMS HOUSES IN GOMBE STATE	49,673,163.76	ABY ENERGY & ENGINEERING LTD	THE PROJECT WAS ABANDONED	ONGOING
23	CONTRACT FOR THE CONSTRUCTION OF FIVE (5) BLOCKS (6-10) OF FOUR (4) UNITS OF TWO (2) BEDROOMS HOUSES IN GOMBE, GOMBE STATE	49,673,163.76	DARA HOUSE LIMITED	PROJECT UNCOMPLETED, AND THE CONTRACTOR WAS DIRECTED TO RETURN TO SITE	ONGOING
24	CONTRACT FOR THE CONSTRUCTION OF FIVE (5) BLOCKS (26-30) OF FOUR (4) UNITS OF TWO (2) BEDROOMS HOUSES IN GOMBE, GOMBE STATE	49,673,163.76	GRACEMADE PROJECTS & INVESTMENT LIMITED	THE PROJECT WAS ABANDONED AT THE LINTEL PHASE.	ONGOING
25	CONTRACT FOR THE CONSTRUCTION OF FIVE (5) BLOCKS (121-125) OF FOUR (4) UNITS OF TWO (2) BEDROOMS HOUSES IN GOMBE, GOMBE STATE	49,673,163.76	SIMA INTEGRATED INVESTMENT LIMITED	THE PROJECT WAS ABANDONED.	ONGOING
26	CONTRACT FOR THE CONSTRUCTION OF FIVE (5) BLOCK (101-105) OF FOUR (4) UNIT OF 2 BEDROOM IN BAUCHI STATE	110,486,957.55	PLOWSHAREEDGE NIGERIA LIMITED	DEFECTS WERE NOTED IN THE WORK.	ONGOING
27	CONTRACT FOR THE CONSTRUCTION OF FIVE (5) BLOCKS (21-25) OF FOUR (4) UNITS OF TWO (2) BEDROOM HOUSES IN BAUCHI STATE	110,486,957.55	ABA GWANA LIMITED	DEFECTS TO THE STRUCTURES.	COMPLETED
28	CONTRACT FOR THE CONSTRUCTION OF ONE STOREY STUDENT HOSTEL COMPRISING FURNISHING, INSTALLATION OF AIR CONDITIONING AND BOREHOLE AT THE FEDERAL POLYTECHNIC BALI, TARABA STATE	499,845,867.50	MAI-ULU NIGERIA LTD	24 NOS. SOLAR STREETLIGHTS WERE NOT INSTALLED BY THE CONTRACTOR	ONGOING
29	CONTRACT FOR THE CONSTRUCTION OF ACCESS ROAD, EROSION CONTROL AND DRAINAGE IN SELECTED COMMUNITIES OF JALINGO LGA, TARABA STATE	445,688,190.55	AHMZAK CONSOLIDATED ENERGY LTD	NO GUARD RAILS ON THE SIDE WALLS OF THE BRIDGE	ONGOING
30	CONTRACT FOR THE PROVISION AND INSTALLATION OF 250 NOS. SOLAR STREET LIGHT IN TARABA SENATORIAL DISTRICT PHASE 2, TARABA STATE	248,800,200.40	ARCHIG CONS. NIGERIA LTD	CONCRETE BASES NOT IN ACCORDANCE WITH THE BOQ	ONGOING
31	CONTRACT FOR THE CONSTRUCTION OF 5 BLOCKS (16-20) OF 4 UNITS OF 2 BEDROOMS HOUSES IN JALINGO, TARABA STATE	97,040,911.30	TERRAZZO GENERAL SERVICES LTD	WORK IN PROGRESS	ONGOING
32	CONTRACT FOR THE CONSTRUCTION OF 5 BLOCKS (112-116) OF 4 UNITS OF 2 BEDROOMS HOUSES IN SARDAUNA LGA TARABA STATE	97,040,911.30	BARGE & BEDROCK LTD	WORK IN PROGRESS	ONGOING

S/N	PROJECT DESCRIPTION	CONTRACT SUM (N)	NAME OF CONTRACTOR	REASON FOR GOING BACK TO SITE	STATUS/REMARK
33	CONTRACT FOR THE CONSTRUCTION OF 2 BLOCKS OF 12 CLASSROOMS EACH FOR PRIMARY SCHOOL IN WUKARI LGA, TARABA SOUTH SENATORIAL DISTRICT, TARABA STATE	410,703,022.12	NA'AM GENERAL CONSTRUCTION NIGERIA LTD	WORK IN PROGRESS	ONGOING
34	CONTRACT FOR ESTABLISHMENT OF ICT CENTRE IN TARABA SOUTH SENATORIAL DISTRICT TARABA STATE	48,350,000.00	MICROFLEX LTD	PERKINS GENERATING SET WAS NOT INSTALLED BY THE CONTRACTOR	ONGOING
35	CONTRACT FOR THE CONSTRUCTION OF 2 BLOCK OF 12 CLASSROOMS EACH FOR PRIMARY SCHOOL IN KURMI LGA, TARABA CENTRAL SENATORIAL DISTRICT OF TARABA STATE	410,703,022.12	KERJIM GLOBAL RESOURCES LTD	WORK IN PROGRESS	ONGOING
36	AWARD OF CONTRACT FOR THE CONSTRUCTION OF ADMINISTRATIVE BLOCK, 4 UNITS OF 2 BEDROOM SEMI-DETACHED STAFF QUARTERS AND OTHER BUILDING (COMMERCIAL CENTRE, GATEHOUSE AND FENCE) IN BALI LGA, IN TARABA STATE	284,946,184.15	GUA GLOBAL CONCEPT LTD	WORK IN PROGRESS-NEDC	ONGOING
37	CONTRACT FOR THE CONSTRUCTION OF 2 BLOCK OF 12 CLASSROOMS EACH FOR SECONDARY SCHOOL IN WUKARI LGA, TARABA SOUTH SENATORIAL DISTRICT, TARABA STATE	403,597,427.99	AL-BABAI DYNAMICS CONCEPTS LTD	WORK IN PROGRESS	ONGOING
38	CONTRACT FOR THE CONSTRUCTION OF 2 BLOCKS OF 12 CLASSROOMS EACH FOR PRIMARY SCHOOL IN JALINGO LGA, TARABA NORTH SENATORIAL DISTRICT, TARABA STATE	410,703,022.12	NTS NIG. LTD	WORK IN PROGRESS	ONGOING
39	CONTRACT FOR THE CONSTRUCTION OF 5 BLOCKS (56-60) OF 4 UNITS OF 2 BEDROOMS HOUSES IN ZING, TARABA STATE	97,040,911.30	FIRST QUALITY CONSTRUCTION PROJECTS LTD	WORK IN PROGRESS	ONGOING
40	CONTRACT THE CONSTRUCTION OF 5 BLOCKS (11-15) OF 4 UNITS OF 2 BEDROOMS HOUSES IN JALINGO, STATE	97,040,911.30	BARGE & BEDROCK LTD	WORK IN PROGRESS	ONGOING
41	CONTRACT FOR THE CONSTRUCTION OF 5 BLOCKS (88-92) OF 4 UNITS OF 2 BEDROOMS HOUSES IN BALI, TARABA STATE	97,040,911.30	PUKIEL GLOBAL CONCEPT LTD	WORK IN PROGRESS	ONGOING
42	CONTRACT FOR THE CONSTRUCTION OF 5 BLOCKS (81-85) OF 4 UNITS OF 2 BEDROOMS HOUSES IN WUKARI, TARABA STATE	97,040,911.30	PUKIEL GLOBAL CONCEPT LTD	WORK IN PROGRESS	ONGOING
43	CONTRACT FOR THE CONSTRUCTION OF 5 BLOCKS (21-25) OF 4 UNITS OF 2 BEDROOMS HOUSES IN JALINGO, TARABA STATE	97,040,911.30	AD ABBA MARWA NIG. LTD	WORK IN PROGRESS	ONGOING

S/N	PROJECT DESCRIPTION	CONTRACT SUM (N)	NAME OF CONTRACTOR	REASON FOR GOING BACK TO SITE	STATUS/REMARK
45	CONTRACT FOR THE CONSTRUCTION OF 5 BLOCKS (93-97) OF 4 UNITS OF 2 BEDROOMS HOUSES IN BALI, TARABA STATE	97,040,911.30	MUSA'AB TECHNOLOGICAL BAG LTD	WORK IN PROGRESS	ONGOING
46	CONTRACT FOR THE CONSTRUCTION OF ADMINISTRATIVE BLOCK, 4 UNITS OF 2 BEDROOM SEMI DETACHED STAFF QUARTERS, COMMERCIAL CENTER, GATEHOUSE AND FENCE IN WUKARI LGA IN TARABA STATE.	284,946,184.15	GATEWAY ROCK INTERNATIONAL LTD	WORK IN PROGRESS-NEDC	ONGOING
47	CONSTRUCTION OF MINI STADIUM IN PRIMARY SCHOOL, IDORO, UYO LGA AKWA IBOM STATE.	89,999,192.30	ANISET INTEGRATED SERVICES LIMITED.	CONSTRUCTION NOT ACCORDING TO SPECIFICATIONS	COMPLETED
48	CONTRACT FOR THE ESTABLISHMENT OF 3 NEW FORESTRY NURSERIES WITH GENERAL SILVICULTURAL SERVICES THROUGH: DRILLING OF SOLAR-POWERED BOREHOLES, RETICULATION OF WATER SUPPLY, AND CHAIN-LINK FENCING OF BOREHOLE AREAS IN EACH OF THE NEW NURSERIES IN BORNO STATE	49,950,000.00	BASHEW GLOBAL CO. LTD	CONSTRUCTION AND INSTALLATION NOT ACCORDING TO SPECIFICATIONS.	THE PROJECT WAS COMPLETED
49	CONSTRUCTION OF FIRE SERVICE STATION IN TORU-ORUA COMMUNITY, SAGBAMA LGA, BAYELSA WEST SENATORIAL DISTRICT, BAYELSA STATE	167,436,800.00	ZEECHY MULTI-CONCEPT LIMITED	SOME ITEMS IN THE BOQ THAT WERE NOT EXECUTED	PROJECT COMPLETED.
50	CONSTRUCTION OF SOLAR-POWERED BOREHOLE IN GORONYO/GADA FEDERAL CONSTITUENCY, SOKOTO STATE	101,606,489.50	DE-OWNMEE NIGERIA LIMITED	1N0. SOLAR POWERED BOREHOLE NOT INSTALLED	COMPLETED
51	CONTRACT FOR THE CONSTRUCTION OF STAFF OFFICE BLOCK (THIRD PHASE) AND LANDSCAPING IN SOKOTO ENERGY RESEARCH, SOKOTO STATE	49,317,899.20	ROLLER BLADE ENGINEERING LIMITED	NOT COMPLETED	ONGOING
52	CONTRACT FOR THE PROVISION OF 1NO. BOREHOLE AND RETICULATION TO SETTLEMENT OF MAKARANTAR ALLO/ALMAJIRI SCHOOL IN BODINGA/DANGE-SHUNI/TURETA FEDERAL CONSTITUENCY, SOKOTO STATE	7,250,338.00	TOPDESK INTERNATIONAL LTD	TO COMPLETE 1NO. SOLAR POWERED BOREHOLE	CONTRACTOR YET TO HONOR INVITATION
53	CONTRACT FOR CONSTRUCTION OF 1KM EARTH ROAD KALMALOTO ILLELA RURAL ROAD IN ILLELA/GWADABAWA FEDERAL CONSTITUENCY, SOKOTO STATE	22,850,300.00	ADAMU ILIYASU PETROLEUM LIMITED	TO COMPACT THE ROCKY LATERITE THAT WAS APPLIED IN THE CONSTRUCTION OF THE ROAD	COMPLETED
54	CONTRACT FOR THE PROVISION OF 5NOS. BOREHOLE AND RETICULATION TO SETTLEMENT OF MAKARANTAR ALLO/ALMAJIRI SCHOOL IN BODINGA/DANGE-SHUNI/TURETA FEDERAL CONSTITUENCY, SOKOTO STATE	36,251,690.00	ALLADUK LIMITED	TO COMPLETE 1NO. SOLAR POWERED BOREHOLE AMONGST THE 5NOS. CONTAINED IN THE BOQ.	ONGOING
55	CONTRACT FOR THE PROVISION OF 1NO. BOREHOLE AND RETICULATION TO SETTLEMENT OF MAKARANTAR ALLO/ALMAJIRI SCHOOL IN BODINGA/DANGE-SHUNI/TURETA FEDERAL CONSTITUENCY, SOKOTO STATE	7,250,338.00	DYNAFINE NIG. LIMITED	TO COMPLETE 1NO. SOLAR POWERED BOREHOLE	ONGOING



S/N	PROJECT DESCRIPTION	CONTRACT SUM (N)	NAME OF CONTRACTOR	REASON FOR GOING BACK TO SITE	STATUS/REMARK
56	SUPPLY AND INSTALLATION OF PUMPING MACHINES (BOREHOLES) IN ILLELA/GWADABAWA FEDERAL CONSTITUENCY, SOKOTO STATE	40,375,000.00	ADA ABDULRAHMAN GLOBAL INVESTMENT LIMITED	TO COMPLETE THE 2NOS. SOLAR POWERED BOREHOLE THAT THE CONTRACTOR ABANDONED	TO BE COMPLETED
57	CONTRACT FOR THE CONSTRUCTION AND FURNISHING OF HOSTEL	427,091,909.00	LOGARITHM ENERGY LIMITED	UNCOMPLETED	COMPLETED
58	CONSTRUCTION OF 2NOS BLOCK OF 3 CLASSROOM EACH FOR ESAN WEST, CENTRAL & IGUEBEN FEDERAL CONSTITUENCY, EDO STATE	49,969,950.00	LUPRES NIGERIA LTD	UNCOMPLETED	COMPLETED
59	CONTRACT FOR THE RENOVATION OF PRIMARY HEALTH CENTRE AT ERHURUN IN UNEME WARD 9, AKOKO-EDO LGA, EDO STATE.	40,099,934.90.	SALX NIGERIA LIMITED	UNCOMPLETED	ONGOING
60	CONSTRUCTION OF 0.8KM ASPHALTIC AMORYA EKE IMOVIE ROAD OWAN EAST LGA	179, 994,870.	QLS GLOBAL SERVICES LIMITED	UNCOMPLETED	COMPLETED
61	CONTRACT FOR THE CONSTRUCTION OF OPEN MARKET STORES WITH BOREHOLES, TOILET FACILITIES IN UZANUN VILLAGES, EDO STATE	68, 500,000.	SAL-BEN CONSOLIDATED	UNCOMPLETED	ONGOING
62	GULLY EROSION CONTROL AT OKOKHUA, OVIA NORTH-EAST, EDO STATE	878,057,443.60	IMSY VENTURES LIMITED	UNCOMPLETED	ONGOING
63	CONSTRUCTION AND EQUIPPING OF CASSAVA PROCESSING PLANT IN SELECTED LOCAL GOVERNMENT IN ANAMBRA AND EDO	470,720,125.00	MKG GLOBAL SERVICES LTD	UNCOMPLETED	ONGOING
64	CONSTRUCTION OF MOTORIZED BOREHOLES IN EKITI SOUTH WEST/IKERE/ISE FEDERAL CONSTITUENCY, EKITI STATE	49,913,110.00	DOBANK GLOBAL CONCEPTS LTD	LEAKING TANK STAND.	COMPLETED
65	CONTRACT ON THE EXTENSION OF ELECTRICITY AND INSTALLATION OF TRANSFORMER IN EKITI NORTH CENTRAL SENATORIAL DISTRICT, EKITI STATE	58,000,000.00	RICH COROLLA ELECTRICAL NIG.LTD	TRANSFORMER WORKED FOR JUST 6 DAYS	COMPLETED
66	CONTRACT FOR THE PROVISION OF BOREHOLES IN EKITI STATE	93,100,000.00	TOPCREST MULTI-FACETED VENTURES LTD	LEAKING TANKS	ON-GOING
67	CONTRACT FOR THE CONSTRUCTION OF COMMUNITY CLINIC IN AGADAGBA, OHIMINI LGA, BENUE SOUTH SENATORIAL DISTRICT.	35,985,677.15	MARI_KAY CORPORATE SERVICES NIG. LTD.	SOME COMPONENTS OF THE PROJECT WERE NOT EXECUTED, I.E. MECHANICAL FIXTURES, FIXTURES AND FURNITURE.	COMPLETED

S/N	PROJECT DESCRIPTION	CONTRACT SUM (N)	NAME OF CONTRACTOR	REASON FOR GOING BACK TO SITE	STATUS/REMARK
68	CONTRACT FOR CONSTRUCTION OF RIVER OGBADIBO BRIDGE AND GRADING OF ALEKPOM OKPAFIE-OGBADIBO ROAD, BENUE SOUTH SENATORIAL DISTRICT	42,500,000.00	GAT PLUS DYNAMIC RESOURCES LIMITED	THE SAND FILLING OF THE BRIDGE AND GRADING OF THE ROAD WERE NOT DONE AT THE TIME OF TRACKING.	COMPLETED
69	CONTRACT FOR CONSTRUCTION OF PRIMARY HEALTH CENTRE/FURNISHING/EQUIPPING WITH SOLAR POWERED BOREHOLE AND OVERHEAD TANK IN AJEGBE AWUME AHAJE OHININI LGA, BENUE STATE.	52,250,000.00	CROWNED EAGLE PREMIUM SERVICES LIMITED	THE BOREHOLE WAS NOT FUNCTIONING AT THE TIME OF TRACKING AND THERE WERE OBSERVED LEAKAGES ON THE ROOF DUE TO POOR WORKMANSHIP.	COMPLETED
70	CONTRACT FOR THE CONSTRUCTION OF BRIDGE (AGADAGBA & CO) IN OTUKPO/OHIMINI FEDERAL CONSTITUENCY, BENUE STATE.	48,487,844.04	TAMGAJ CORPORATE SERVICES LTD	THE CONSTRUCTION OF THE BRIDGE WAS NOT COMPLETED AT THE TIME OF TRACKING THE PROJECT.	ONGOING
71	CONSTRUCTION OF 1 NOS PAVILLION WITH FOOTBALL PITCH AT PROPOSED YOUTH CENTRE YOLA SOUTH LGA ADAMAWA STATE	211,759,238.73	MESSRS TRCC NIGERIA LTD	SOME ITEMS ON THE BOQ WERE NOT EXECUTED	ONGOING
72	CONSTRUCTION OF 19 NOS SOLAR-POWERED BOREHOLES (TYPE B) AT ADAMAWA CENTRAL SENATORIAL DISTRICT ADAMAWA STATE	230,870,477.53	MESSRS SABAL KAUTAL NIGERIA LIMITED	SOME OF THE BOREHOLES WERE NOT WORKING	ONGOING
73	CONSTRUCTION OF 1 NOS PAVILLION WITH FOOTBALL PITCH AT PROPOSED YOUTH CENTRE YOLA NORTH LGA ADAMAWA STATE	211,759,238.73	MESSRS INFINITY GLOBAL NIGERIA LTD	SOME ASPECTS OF THE BOQ WERE NOT EXECUTED	COMPLETED
74	CONSTRUCTION AND FURNISHING CENTRE (HALL) AT GDSS LUGGERE JIMETA YOLA NORTH ADAMAWA STATE	323,000,000.00	MESSRS BINANI NIGERIA LTD	SOME ITEMS ON THE BOQ WERE NOT EXECUTED	ONGOING
75	CONTRACT FOR THE REMODELLING AND RENOVATION OF HOME ECONOMICS LIVING FLAT AT FCE, YOLA	120,846,098.18	MESSRS VESTEEM EQUIPMENT LTD	SOME ITEMS ON THE BOQ WERE NOT SUPPLIED	ONGOING
76	CONSTRUCTION OF AN ADMINISTRATIVE BLOCK OF THREE OFFICES WITH TOILET EACH AT ST JOHN'S SECONDARY SCHOOL ALOR, IDEMILI LGA, ANAMBRA STATE.	20,125,000.00	NAOMI ENGINEERING LTD	THE CONTRACTOR USED PVC CEILINGS WHICH FELL OFF INSTEAD OF THE HARD BOARD AS PROVIDED IN THE BOQ. THE CONTRACTOR ALSO USED CHINA DOORS INSTEAD OF THE FABRICATED METAL DOORS AS PROVIDED IN THE BOQ.	COMPLETED
77	COMPLETION OF EROSION CONTROL PROJECT AT DUNUKOFIA LGA	139,990,396.88	CONNAFLO LIMITED	THE CONTRACTOR CONSTRUCTED 400M INSTEAD OF THE 520M PROVIDED FOR IN THE BOQ	COMPLETED
78	CONSTRUCTION OF OCHENDO OBIGBUNAM/ HOSPITAL ROAD, NRI OPS/CEPTD/P6/AN/036	100,488,420.00	SFIX CONSULT INTERNATIONAL SERVICES LTD	THE CONTRACTOR ONLY DID EARTHWORK AND DRAINAGE ON 450M OF ROAD INSTEAD OF 622M OF ROAD WITH ASPHALT PROVIDED IN THE BOQ.	COMPLETED

S/N	PROJECT DESCRIPTION	CONTRACT SUM (N)	NAME OF CONTRACTOR	REASON FOR GOING BACK TO SITE	STATUS/REMARK
79	CONTRACT FOR THE CONSTRUCTION OF 1,5KM ROAD IN MACHINA, YOBE STATE	179,500,000.00	ISMASOL CONSTRUCTION LTD	REMEDIAL WORKS ON THE GUTTER AND TO COMPLETE THE DISTANCE OF THE ROAD.	COMPLETED
80	CONTRACT FOR PROVISION OF SOLAR STREET LIGHT IN NGELZARMA, YOBE STATE	165,057,751.00	MU'AYYAT GLOBAL CO. NIG. LTD	TO INSTALL 50NOS OF SOLAR STREET LIGHT TO COMPLETE 250 AS AGAINST THE 200 COUNTED.	COMPLETED
81	CONTRACT FOR CONSTRUCTION OF TOWNSHIP STADIUM, YOBE STATE	491,021,961.00	CELESONIC NIGERIA LIMITED	THE GATEHOUSE, INTERLOCKING, CHANGE OF THE PITCH SYNTHETIC GRASS TO THE SPECIFIED BRAND, COMPLETION OF THE AUDITORIUM SEATS AND REMEDIAL WORKS IN THE TOILET	COMPLETED
82	CONTRACT FOR THE CONSTRUCTION OF ACCESS ROAD WITH CULVERTS TO RURAL FARMING COMMUNITIES OF BADE, NGURU AND YUSUFARI LGA	165,272,112.50	NORTSEAL GLOBAL INVESTMENT LTD	TO CARRY OUT REMEDIAL WORKS ON THE ROAD	COMPLETED
83	CONTRACT FOR THE CONSTRUCTION OF 1.5KM ROAD AT JAKUSKO LGA	179,855,928.00	MELLON-DE COMPANY INTERNATIONAL LTD	TO CARRY OUT REMEDIAL WORKS ON THE ROAD AND TO COMPLETE THE DISTANCE TO 1.5K AS AGAINST 1.3KM CONSTRUCTED BY THE CONTRACTOR	COMPLETED
84	CONTRACT AWARD: FLOOD CONTROL AT DIKE IN ALARGANO, BADE LGA, YOBE STATE	1,097,815,883.26	SEAK RISK MANAGEMENT LIMITED	TO CARRY OUT REMEDIAL WORKS ON THE DIKE	COMPLETED
85	CONTRACT FOR THE CONSTRUCTION AND FURNISHING OF ONE FLOOR 16 ROOM FEMALE MEDICAL STUDENT 2(NO) COMMON ROOM (1NO) POTTERS OFFICE, 20 (NOS) TOILETS AT YOBE STATE UNIVERSITY TEACHING HOSPITAL	149,178,395.00	MARWEZ LTD	ABANDONED.	ONGOING
86	CONTRACT FOR THE CONSTRUCTION OF 3 UNITS OF 2BEDROOM SEMI-DETACHED STAFF QUARTERS AT YOBE STATE WOMEN AND CHILDREN HOSPITAL	75,000,000.00	SAMEMA INVESTMENT LTD	UNCOMPLETED BUILDING	COMPLETED
87	CONTRACT FOR THE RENOVATION AND EXPANSION OF MATERNITY BUILDING COMPLEX AT YOBE STATE SPECIALIST HOSPITAL	108,969,172.68	HAFDALA CORPORATE LIMITED	TO CARRY OUT REMEDIAL WORKS ON THE HOSPITAL BUILDING	COMPLETED
88	CONTRACT FOR THE PART-FUNDED PROVISION OF SOLAR LIGHT IN YOBE SOUTH SENATORIAL DISTRICT YOBE STATE	175,000,000.00	FRONTIERS RESOURCES INTERNATIONAL LIMITED	TO INSTALL ADDITIONAL 24 SOLAR STREET.	COMPLETED
89	CONTRACT FOR THE PART-FUNDED CONSTRUCTION OF SKILL ACQUISITION CENTRE IN YOBE SOUTH SENATORIAL DISTRICT, YOBE STATE	68,184,721.00	MODULAR CONSTRUCTION PROJECT LTD	CONCRETE SIDE DRAIN, PAVE WALKWAYS AND PROPER LANDSCAPING UNCOMPLETED.	COMPLETED

S/N	PROJECT DESCRIPTION	CONTRACT SUM (N)	NAME OF CONTRACTOR	REASON FOR GOING BACK TO SITE	STATUS/REMARK
90	PROVISION AND INSTALLATION OF SOLAR STREET LIGHTS AT THE UMAR SULEIMAN COLLEGE OF EDUCATION, HIGH ISLAM SCHOOL NGURU AND UMAR SULEIMAN PRIMARY SCHOOL GASHUA, BADE LGA	123,761,250.00	MAHASIN INTEGRATED SERVICES	SOLAR LIGHTS NOT FUNCTIONING	COMPLETED
91	CONTRACT FOR THE RENOVATION OF TWO (2) PRIMARY HEALTH CARE CENTRES IN YOBE STATE	50,193,168.38	TASHA ENERGY & ENGINEERING SERVICES LTD	UNCOMPLETED. GENERATOR IN THE BILL, 2 FANS. TOILET SEATS AND OTHER REMEDIAL WORKS IN BUILDING TILES AND WINDOWS NOT COMPLETED	COMPLETED
92	CONTRACT FOR THE CONSTRUCTION OF 150 CAPACITY BIOLOGY LABORATORY AT FCE POTISKUM FUNDED THROUGH 2020 TETFUND ANNUAL INTERVENTION 2020R/FX722	166,769,425.11	NATA'ALLA INVESTMENT LTD	PROJECT NOT COMPLETED. THE PLANTING AND LAND RESERVOIR, ROOF FELTING, INSTALL THE FIRE EXTINGUISHER AND 21 AIR CONDITIONS	COMPLETED
93	CONTRACT FOR PROVISION OF 4NOS SOLAR-POWERED BOREHOLE IN JAKUSKO FEDERAL CONSTITUENCY, YOBE STATE	27,458,725.00	Q. ASSOCIATES LTD	ONE BOREHOLE IS NOT FUNCTIONING	COMPLETED
94	CONTRACT FOR T CONSTRUCTION OF BLOCKS OF 3 CLASSROOMS EACH WITH FURNITURE, AND VIP TOILETS AND UPSTAIRS BLOCKS OF 8 NOS CLASSROOMS IN SELECTED PRIMARY AND SECONDARY SCHOOLS IN DKD LGA KANO	204,000,000.00	J15 NIGERIA LIMITED	SHODDY JOB	COMPLETED
95	CONSTRUCTION OF SPORTING AREA IN DANBATTA	199,050,980.00	SANKALP ENGINEERING & SERVICES LIMITED	UNCOMPLETED	COMPLETED
96	FLOOD CONTROL THROUGH RECONSTRUCTION OF PALANKAWA DAM AND ITS APPURTENANCES STRUCTURES FOR IRRIGATION AT GAMASA, AJINGI LGA KANO STATE	632,729,885.00	XENON CONSTRUCTION LIMITED	SPILLWAYS RENOVATIONS	ONGOING
97	CONTRACT FOR THE CONSTRUCTION OF 8 NOS OF MOTORIZED SOLAR-POWERED BOREHOLES IN SELECTED LGAS OF KOGI STATE	107,204,160.00	IIDC LIMITED	UNCOMPLETED	ONGOING
98	CONTRACT FOR THE CONSTRUCTION OF A BLOCK OF THREE CLASSROOMS WITH OFFICE AND SIX COMPARTMENTS VIP TOILETS IN KOTON KARFE LGA, KOGI STATE AND 1 NO OF PROJECT VEHICLE	58,503.980.23	ESMAYI GLOBAL SERVICE LIMITED	UNDER CONSTRUCTION.	ONGOING
99	CONTRACT FOR THE CONSTRUCTION OF 60 NOS HAND PUMP BOLEHOLES IN SELECTED LGAS OF KWARA STATE.	166,061,700:00	KHALIDTECH GLOBAL CONCEPTS LIMITED	SOME OF THE BOLEHOLES DID NOT FUNCTION FROM THE ONSET.	COMPLETED
100	DEVELOPMENT OF LABORATORIES, WORKSHOP AND INCUBATION UNITS AT TIC MABUDI EXTENSION, PLATEAU STATE	106,276,959.53	PREMIO TECHNOLOGY LTD	UNCOMPLETED	ONGOING

S/N	PROJECT DESCRIPTION	CONTRACT SUM (N)	NAME OF CONTRACTOR	REASON FOR GOING BACK TO SITE	STATUS/REMARK
101	EXECUTION OF REHABILITATION AND EQUIPPING OF NBTI CENTRE OF MABUDI, PLATEAU STATE	84,623,575.38	REMOTE RESOURCE LIMITED	UNCOMPLETED	ONGOING
102	CONSTRUCTION OF ROAD IN PLATEAU CENTRAL SENATORIAL DISTRICT, PLATEAU STATE (KABWIR DISTRICT, KANKE)	288,844,663.62	A.V.I CONSTRUCTION NIG. LTD	THE WORK MEASURED ON THE GROUND WAS NOT IN LINE WITH THE SPECIFICATION IN THE BOQ	ONGOING
103	CONSTRUCTION OF 3 CLASSROOM BLOCK IN MANGU/BOKKOS FEDERAL CONSTITUENCY PLATEAU STATE	40,850,950.57	REOMOTWEBNET DYNAMICS LIMITED	LEAKING ROOF AND SAGGING CEILING WAS OBSERVED DURING TRACKING. THE CONTRACTOR WAS MADE TO RETURN TO THE SITE TO FIX THE SAME	ONGOING
104	CONTRACT FOR THE COMPLETION OF BLOCK OF CLASSROOMS IN THE COLLEGE AT NVRI	25,950,220.78	TIME ENGINEERING DESIGN & CONSTRUCTION LIMITED	NOT COMPLETED IN LINE WITH THE STANDARD IN THE BOQ	COMPLETED
105	PART-CONSTRUCTION OF GUM-GAGDI, BADAKOSHI TO DUL ROADS IN PANKSHIN/KANKE/KANAM FEDERAL CONSTITUENCY, PLATEAU STATE	118,125,000.00	SHAYE ENGINEERING AND CONSTRUCTION CO. LTD	NOT COMPLETED.	ONGOING
106	EROSION CONTROL AND ROAD IMPROVEMENT WORKS FROM WASA TO GUDE CENTRAL IN FCT (PHASE 1), ABUJA	2,279,032,569.91	Y.S WORLDWIDE CONCERTS LIMITED	THE CONTRACTOR HAS NOT COMPLETED THE SCOPE OF WORK 1. SOME METRES OF THE LINE DRAINS. 2. SOME KM OF THE EARTHWORK.	COMPLETED
107	CONSTRUCTION OF ACCESS ROADS AT THE FCT COLLEGE OF EDUCATION PERMANENT SITE	410,990,000.00	ASPIRE MULTI-ALLIED PROJECT LIMITED	UNCOMPLETED	ONGOING
108	CONSTRUCTION OF BRIDGE, CULVERTS AND UPGRADING OF ROADS AT LUGBE 1 CADASTRAL ZONE, 07-07 OFF UMARU YARADUA, AIRPORT ROAD, LUGBE, ABUJA	466,108,400.75	IWT & K VENTURES LIMITED	NOT COMPLETED	ONGOING
109	CONSTRUCTION OF A PRIMARY HEALTH CARE CENTRE (LEVEL 2) IN AMAC/BWARI FEDERAL CONSTITUENCY OF FCT	47,520,184.70	EDD-TOLAD LTD	THE SCOPE OF THE PROJECT WAS NOT COMPLETELY EXECUTED SUCH AS THE SOLAR PANEL	COMPLETED
110	CONSTRUCTION OF MINI SPORTS CENTRE IN OLD KARU, ABUJA	497,650,200.83	CHIGO INTEGRATED AND ALLIED SERV. LTD	NOT EXECUTED JUST 30% OF THE PROJECT	ONGOING
111	CONTRACT FOR GULLY EROSION AND FLOOD CONTROL WORK ALONG TAFAWA BALEWA WAY, AREA 3, GARKI FCT	544,266,208.56	BAJEM TRUST LIMITED	NOT COMPLETED. THE PROJECT DRAINS COLLAPSED	COMPLETED
112	CONTRACT FOR THE CONSTRUCTION AND FURNISHING OF ACADEMIC STAFF OFFICE COMPLEX FOR THE FACULTY OF LAW, UNIVERSITY OF ABUJA.	209,708,688.06	CLOVERFIELDS LIMITED	PART OF THE ROOFING SHEETS AND CEILING HAVE PULLED OFF	COMPLETED

S/N	PROJECT DESCRIPTION	CONTRACT SUM (N)	NAME OF CONTRACTOR	REASON FOR GOING BACK TO SITE	STATUS/REMARK
113	CONSTRUCTION OF ROADS, DRAINAGES AND ASPHALT IN NYANYA ANGWAN-DADI, AMAC OF FCT SENATORIAL DISTRICT	345,245,478.28	GIOSHEN GLOBAL CONCEPT LTD	THE REQUIRED LENGTH OF THE ROAD WAS NOT COMPLETED	COMPLETED
114	CONTRACT FOR CONSTRUCTION OF NATIONAL YOUTH DEVELOPMENT CENTRE AT GWAGWALADA, ABUJA, FCT	420,737,884.66	BIATEMP VENTURES LTD	THE PROJECT WAS ABANDONED	ONGOING
115	SOIL EROSION AND FLOOD CONTROL, CHANNELIZATION AND ROAD IMPROVEMENT WORKS AT NIGERIAN INSTITUTE OF SECURITY STUDIES, BWARI AREA COUNCIL, FCT, ABUJA	495,414,062.92	RHESTON INTERNATIONAL SERVICES LTD	PART OF THE PROJECT WAS NOT COMPLETELY EXECUTED	COMPLETED
116	PROVISION AND INSTALLATION OF SOLAR STREET LIGHTS AND TRANSFORMER IN GALADIMAWA, FCT	15,091,631.44	BROWN OBILITY & CO LTD	THE STREETLIGHTS WERE NOT COMPLETE	COMPLETED
117	CONTRACT FOR THE CONSTRUCTION OF ORODO-OGWA ROAD IN MBAITOLI LGA, IMO STATE	479,113,635.00	EMBECO NIG. LTD	PROJECT NOT COMPLETED	ONGOING
118	CONSTRUCTION OF TOWN HALL VIEWING CENTRES FOR 3 SELECTED COMMUNITIES IN OHAJI EGBEMA OGUTA ORU WEST FEDERAL CONSTITUENCY IMO STATE	106,249,470.37	EMUDDY GLOBAL LTD	PROJECT NOT COMPLETED	ONGOING
119	COMPLETION AND RENOVATION OF NKWERE COUNTRY CLUB AND UNITY FORUM AMAIGBO IN NKWERE ISU NWANGELE NJABA FEDERAL CONSTITUENCY	127,500,000.00	KRISHAKEM NIG.LTD	PROJECT NOT COMPLETED.	COMPLETED
120	CONTRACT FOR CONSTRUCTION OF INTERNAL ROADS IN EZINHITTE MBAISE LOCAL GOVERNMENT	95,723,901.99	EDMAG TECHNICAL CO. LTD.	PROJECT NOT COMPLETED (STONE BASE/ASPALTING WORK)	COMPLETED
121	PROVISION OF SICKBAY IN SELECTED PRIMARY SCHOOLS IN PARTS OF MUSHIN 1, SHOMOLU AND AGEGE FEDERAL CONSTITUENCIES	150,134,054.04	MASON GLOBAL CONSTRUCT LIMITED	THE 1.5HP SPLIT AIR CONDITIONERS WERE NOT INSTALLED BY THE CONTRACTOR	COMPLETED
122	CONTRACT FOR THE REHABILITATION OF ROADS IN MUSHIN 2, FEDERAL CONSTITUENCY, LAGOS STATE.	188,149,080.00	BRIDGEVINE RESOURCES LIMITED	TO REPAIR FAILED PORTIONS ON THE ROAD.	COMPLETED
123	CONTRACT FOR THE REHABILITATION OF ROADS IN AJEROMI/IFELODUN, FED. CONSTITUENCY, LAGOS STATE.	186,374,572.13	COTIKUMPLUS LIMITED	PROVISION AND LAYING OF 200MM LONG DIAMETER 2-INCH PIPE TO COLLECT BASE WATER INTO DRAINAGE.	COMPLETED
124	CONTRACT FOR THE REHABILITATION OF ROADS IN ETI-OSA, FED. CONSTITUENCY, LAGOS STATE.	189,509,354.25	AMARCHY PEN PROJECT LIMITED	TO REPAIR FAILED PORTIONS ON THE ROAD. PROVISION AND LAYING OF 6INCHES DIAMETER PIPE TO COLLECT WATER CARRIAGE TO DRAINS	COMPLETED



S/N	PROJECT DESCRIPTION	CONTRACT SUM (N)	NAME OF CONTRACTOR	REASON FOR GOING BACK TO SITE	STATUS/REMARK
125	CONSTRUCTION AND FURNISHING OF TWO BLOCKS OF 3 CLASSROOMS IN OGBOMO COMMUNITY JUNIOR HIGH SCHOOL AND ST. MATHIAS BOYS PRIMARY SCHOOL, 30 FORESTYHE STREET IN LAGOS CENTRAL SENATORIAL DISTRICT, LAGOS STATE.	33,000,000.00	SOLID TEAM INNOVATIVE PROJECTS LIMITED	TO POWER THE CLASSROOMS AT ST. MATHIAS BOYS PRIMARY SCHOOL. TO FIX THE LEAKAGES. TO INSTALL 2NOS 60AMP 8-WAY TNP.	COMPLETED
126	PART-CONSTRUCTION OF BLOCKS OF CLASSROOMS & LIBRARY IN AMUWO ODOFIN FEDERAL CONSTITUENCY, LAGOS STATE.	37,187,500.00	LUGE DYNAMIC SERVICES LIMITED	THE CONTRACTOR DID NOT EXECUTE THE PROJECT AS SPECIFIED IN THE BOQ.	ONGOING
127	CONTRACT FOR THE CONSTRUCTION AND FURNISHING OF COMMUNICATION BUILDING, LAGOS STATE UNIVERSITY, OJO.	349,123,081.52	DALORI GLOBAL ENGINEERING LIMITED	UNDERSUPPLIED ITEMS	COMPLETED
128	ELECTRIFICATION PROJECT IN 1. OKEYA COMMUNITY AKURESOUTH LG, 2. IJOKA COMMUNITY AKURE SOUTH LG, 3. EMERUKU ONIGARI COMMUNITY AND REHABILITATION OF IGBUSHI EGBATORO AKURE NORTH AND AKURE SOUTH LG, ONDO STATE	64,867,504.9	I.U.K INTERNATIONAL COMPANY LIMITED	THE PROJECT WAS EXECUTED BUT NOT FUNCTIONAL	ONGOING
129	CONTRACT FOR SUPPLY OF 3 NOS 300KVA TRANSFORMER IN ONDO CENTRAL SENATORIAL DISTRICT 2, ONDO STATE	31,875,000.00	KELASCO RESOURCES NIGERIA LIMITED	THE PROJECT WAS EXECUTED BUT NOT DISTRIBUTED	COMPLETED
130	CONTRACT FOR THE CONSTRUCTION OF 2KM ROAD AT IDANRED OKE, ONDO STATE	451,560,802.00	HEADSTONE ENGINEERING LIMITED	THE PROJECT WAS ABANDONED	INADEQUATE FUNDING
131	CONTRACT FOR THE CONSTRUCTION OF 2KM ROAD AT IGBARA OKE, ONDO STATE	232,988.775.88	TICKTOS NIGERIA LIMITED	THE PROJECT WAS ABANDONED	INADEQUATE FUNDING
132	CONTRACT OF LIBRARY AT ONDO WEST FEDERAL AT ONDO WEST FEDERAL CONSTITUENCY, ONDO STATE	99,576,667.50	GLOBAL KEDOT SERVICES NIGERIA LIMITED	THE PROJECT E-LIBRARY INTERNET WAS NOT INSTALLED	COMPLETED
133	CONTRACT FOR THE COMPLETION OF CONSTRUCTION OF LIBRARY AT ONDO-WEST FEDERAL CONSTITUENCY, ONDO STATE	85,000,000.00	GLOBAL KEDOT SERVICES NIGERIA LIMITED	THE PROJECT E-LIBRARY INTERNET WAS NOT INSTALLED	INSTALLED AND FUNCTIONAL
134	CONSTRUCTION AND REHABILITATION OF INTERNAL ROAD NETWORK AND EROSION CONTROL FOR NATIONAL INSTITUTE FOR EDUCATIONAL PLANNING AND ADMINISTRATION (NIEPA), ONDO STATE	1,354,074,631.59	HMF CONSTRUCTION LIMITED	THE PROJECT HAS EXCEEDED THE 8-MONTH TIMEFRAME	PROJECT COMPLETED AND FUNCTIONAL
135	CONSTRUCTION OF ONE BLOCK OF TWO CLASSROOMS WITH FURNITURE IN THREE (3) LOCATIONS OF (1) SAINT PAUL ANGLICAN PRIMARY SCHOOL, GEDEGEDE AKOKO, (2) COMMUNITY PRIMARY SCHOOL, ESE AKOKO, (3) COMMUNITY PRIMARY SCHOOL, AFIN AKOKO, AKOKO SOUTH LGA, AKOKO (ESE, AFIN GEDEGEDE) ONDO NORTH SENATORIAL DISTRICT, ONDO STATE	61,518,750	NUEL IZUAGBA LIMITED	THE PROJECT WAS NOT DONE ACCORDING TO THE SPECIFICATIONS ON THE BOQ	ONGOING

S/N	PROJECT DESCRIPTION	CONTRACT SUM (N)	NAME OF CONTRACTOR	REASON FOR GOING BACK TO SITE	STATUS/REMARK
136	SUPPLY OF FOOD ITEMS AND FARM IMPLEMENTS WITHIN ONDO WEST AND EAST FEDERAL CONSTITUENCY, ONDO STATE.	84,985,000.00	MODESCOM SOLUTIONS LIMITED	NO FARM IMPLEMENTS WERE DISTRIBUTED	COMPLETED
137	CONSTRUCTION AND FURNISHING OF DEPARTMENTAL BUILDING FOR SCHOOL OF AGRICULTURAL, FOOD AND NATURAL RESOURCES AT OLUSEGUN AGAGU UNIVERSITY OF SCIENCE AND TECHNOLOGY, OKITIPUPA, ONDO STATE	292,925,439.00	APD ASSOCIATES	THE CONTRACTOR TO FIX THE FALLEN SHEETS OF CEILINGS	COMPLETED
138	CONTRACT FOR THE CONSTRUCTION OF 2KM CONCRETE WALKWAY OF ERUUNA OKORO-AJIGA ILAJE ROAD LGA, ONDO STATE, (PHASE1)	1,241,397,238.67	MESSRS SI-OL SYNERGY LIMITED	THE PROJECT WAS ABANDONED	NOT CAPTURED IN 2023 BUDGET
139	CONTRACT FOR CONSTRUCTION OF 2KM CONCRETE WALKWAY AT OLOWO ILAJE, LGA, ONDO	1,398,942,298.42	MESSRS SI-OL SYNERGY LIMITED	THE PROJECT WAS ABANDONED	NOT CAPTURED IN 2023 BUDGET
140	CONTRACT FOR CONSTRUCTION OF 2KM CONCRETE WALKWAY AT IKORIGHO ILAJE, LGA, ONDO STATE	1,132,522.339.61	MESSRS DEGAN CONSTRUCTION LIMITED	THE PROJECT WAS ABANDONED	INADEQUATE FUNDING
141	CONTRACT FOR THE COMPLETION OF OGBESE BRIDGE IN OKRLUSE BORDERING EDO AND ONDO STATES (LOT W321)	374,947,929.00	TSALECH DYNAMIC AND INNOVATION LIMITED	THE PROJECT WAS ABANDONED	INADEQUATE FUNDING
142	CONTRACT LOT W18 CONSTRUCTION OF TOWN COMMUNITY HALLS AT IPELE AND OJOMO IN OWO/OSE LGA, ONDO STATE	84,703,912.00	OVAD DYNAMICS NIGERIA LIMITED	THE HALL AT OJOMO WAS ALMOST COMPLETED WHILE THE HALL AT IPELE WAS ABANDONED.	COMPLETED
143	CONTRACT FOR THE CONSTRUCTION OF OWO-UTE ROAD IN OWO LGA IN ONDO STATE (2.93KM)	456,947,526.42	DULIZ DREDGING AND CONSTRUCTION LIMITED	THE PROJECT SEEMS TO BE ABANDONED	90% PROJECT COMPLETED AND FUNCTIONAL
144	CONSTRUCTION OF 1.3KM ASPHALTIC TOWNSHIP/RURAL ROAD IN APONMU-LOMA IN ONDO CENTRAL SENATORIAL DISTRICT, ONDO STATE	209,400,840.00	SENAPAT ENGINEERING LIMITED	THE PROJECT WAS PURELY EXECUTED	ONGOING
145	CONTRACT FOR THE CONSTRUCTION OF AND FURNISHING O SCHOOL OF EARTH AND MINERAL SCIENCE (PHASE III) BUILDING OF THE FEDERAL UNIVERSITY OF TECHNOLOGY, AKURE-LOT1	262,391,683.38	YUSAI TELEVIEW NIGERIA LIMITED	THE PROJECT WAS NOT COMPLETED AT THE TIME OF TRACKING	PROJECT COMPLETED AND FUNCTIONAL
146	CONTRACT FOR THE CONSTRUCTION OF BRIDGE AT LUKOTO-ODE IRELE LGA, ONDO STATE	490,528,936.89	CRCC (INT'L) NIGERIA LIMITED	THE PROJECT WAS ABANDONED	INADEQUATE FUNDING
147	CONTRACT FOR THE SUPPLY AND INSTALLATION OF TRANSFORMERS IN SELECTED L.G.A.S OF ONDO STATE (LOT N10)	68,701,121.56	MESSRS MURSHE BASE LIMITED	ONLY TWO OUT OF THE THREE TRANSFORMER HAS BEEN SUPPLIED	THE PROJECT IS NOT COMPLETED DUE TO FUNDING
148	CONSTRUCTION OF 1.3KM ASPHALTIC TOWNSHIP/RURAL ROAD IN APONMU-LOMA IN ONDO CENTRAL SENATORIAL DISTRICT, ONDO STATE	139,755,740.50	SENAPAT ENGINEERING LIMITED	THE PROJECT WAS PURELY EXECUTED	ONGOING



S/N	PROJECT DESCRIPTION	CONTRACT SUM (N)	NAME OF CONTRACTOR	REASON FOR GOING BACK TO SITE	STATUS/REMARK
149	CONSTRUCTION OF A PRIMARY HEALTH CARE CENTRE AT HUNDEJE IN SHANGA LGA OF KEBBI STATE	49,302,678.78	AADIL INTEGRATED NIGERIA LIMITED,	THE PROJECT WAS NOT EXECUTED ACCORDING TO SPECIFICATIONS	COMPLETED
150	SUPPLY OF COMPUTERS AND FURNITURE TO ICT CENTRE IN NGASKI/SHANGA/YAURI FEDERAL CONSTITUENCY, KEBBI STATE.	80,146,646.50	SEVEN GREEN STARS INTERNATIONAL LTD	NOT EXECUTED ACCORDING TO SPECIFICATIONS	COMPLETED
151	SUPPLY AND INSTALLATION OF TRANSFORMERS IN JEGA TOWN FOR EMPOWERMENT OF ELECTRICITY, KEBBI STATE	97,103,063.68	BAYI-SADA AND ASSOCIATE LIMITED	NOT FUNCTIONAL	COMPLETED
152	CONTRACT FOR THE CONSTRUCTION OF 2 BLOCKS OF 2 CLASSROOMS AT COMMUNITY SECONDARY SCHOOL, NKALAGU, ISHIELU LGA, EBONYI STATE”	25,000,000.00	MESSRS ODEY BERRIT NIGERIA LTD	ABANDONED SINCE 2022 AFTER FULL PAYMENT WAS MADE TO THE CONTRACTOR	ONGOING
153	CONTRACT FOR PART-FUNDED REHABILITATION AND CONSTRUCTION OF AMAEZE-AMAEKE ROAD (1KM) IN IVO LGA, EBONYI SOUTH SENATORIAL DISTRICT, EBONYI STATE	98,560,000.00	MESSRS DAISYGO CONCEPTS LTD	THE PROJECT WAS PART-FUNDED AND ONGOING AT THE TIME OF TRACKING	PROJECT COMPLETED
154	CONTRACT FOR THE REHABILITATION AND CONSTRUCTION OF ISU COMMUNITY ROAD (1) IN ONICHA LGA, EBONYI SOUTH SENATORIAL DISTRICT, EBONYI STATE	66,497,700.00	MESSRS DAISYGO CONCEPTS LTD	THE PROJECT WAS ONGOING AT THE TIME OF TRACKING	THE PROJECT WAS COMPLETED AFTER THE CONTRACTOR RETURNED TO SITE.
155	CONTRACT FOR THE CONSTRUCTION OF MINI SPORTS CENTRE AT GOVERNMENT SECONDARY SCHOOL, AFIKPO NORTH LGA, EBONYI STATE	223,468,140.50	MESSRS GARYKON COMPANY LTD	LIMITED LAND SPACE FOR THE CONSTRUCTION OF TENNIS COURT & BASKETBALL COURT	CONTRACTOR COMMENCED WORK
156	CONTRACT FOR THE CONSTRUCTION OF TERRACE MINI STADIUM AT NKALAGU, ISHIELU LGA, EBONYI STATE	403,056,168.90	MESSRS DAISYGO CONCEPTS LTD	THE PROJECT WAS ONGOING AT THE TIME OF TRACKING	PROJECT COMPLETED
157	CONTRACT FOR CONSTRUCTION OF SOLAR ENERGY STREET LIGHTS AROUND MINI STADIUM IN NKALAGU, EBONYI STATE	41,388,085.00	MESSRS OWOGOGA & OCHECHE OWONI NIG. LTD	THE PROJECT WAS ONGOING AT THE TIME OF TRACKING	ONGOING
#	TOTAL VALUE FOR PROJECTS ON WHICH CONTRACTORS RETURNED TO SITE	N29,597,541,340.69			



*Tracked the supply of medical equipment  
at a Federal Medical Centre*

# Policy Advisory

- ☑ Agencies are to ensure that only competent and capable consultants with requisite manpower generated through transparent processes are given consultancies and some mechanisms should be developed to checkmate and ward off possible collusion between contractors and consultants.
- ☑ NEDC and HYPPADEC should consider decentralising their storage processes in such a way that their state offices or nearest state offices should be able to receive supplied items meant for their locations and dispense with same forthwith.
- ☑ MDAs providing empowerment items may where it becomes very necessary, receive recommendations of deserving beneficiaries from stakeholders but must always share same directly to the beneficiaries in a manner that meets the intent and purpose of the empowerment.
- ☑ MDAs should devise an in-house disciplinary mechanism for erring project supervisors who are found to have certified poorly executed projects as properly executed.
- ☑ Need Analysis should always be carried out in the conception of projects. This is to avoid non-usage or underutilisation of projects after completion.
- ☑ MDAs must refrain from awarding contracts without adequate budgetary provision and cash backing. This is responsible for lots of abandoned projects and requests for variation as project timelines have elapsed.
- ☑ MDAs must ensure proper funding and timely execution of projects and administer sanctions to erring contractors who delay project execution leading expiration of the contract.
- ☑ BPP should be advised to watch out for abuse of the emergency procurement processes and ensure scrutiny of each application before approving same.





*Enforced the distribution of empowerment items in Akwa Ibom State*







[f](#) [@](#) [▶](#) [X](#) @ICPCNigeria [🌐](#) www.icpc.gov.ng
